




BIŁOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF NOV. 6-12, 2017

<i>Turned around in route (no fire) / Citizen Complaint/Explosion/ other</i>	1
<i>Fires (Structure & Vehicle)</i>	4
<i>Rescue & Emergency Medical Services</i>	91
<i>Medical Involving Homeless Persons</i>	3
<i>Hazardous Conditions</i>	3
<i>Service Call;</i>	6
<i>Good Intent Call:</i>	19
<i>Special Incident Type</i>	0
<i>Fire Alarm Calls; Active, Malfunction</i>	16
Total	<u>143</u>

WEEKLY COUNT OF INCIDENT TYPE



Criminal Intelligence Unit

T. (228) 702-3160
 T. (228) 702-3122
 T. (228) 702-1276
 F. (228) 702-3179
 ciu@biloxi.ms.us

**Police Chief
John B. Miller**

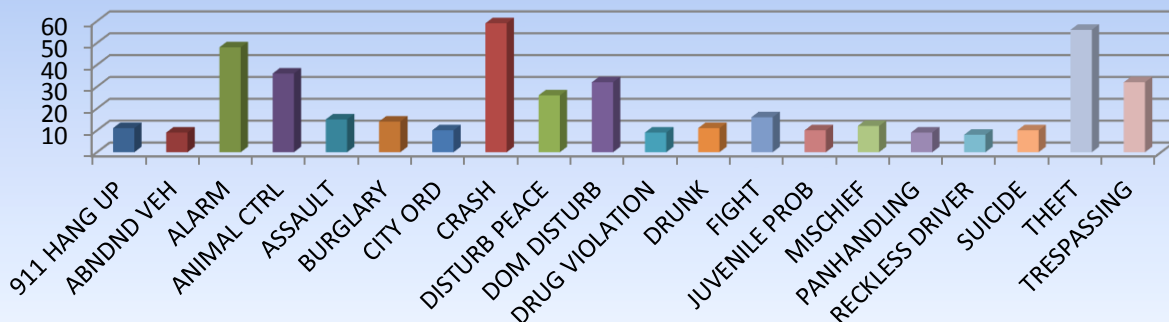

170 Porter Avenue
 Biloxi, Mississippi 39533
 Office: 228.435.6100
 Fax: 228.374.1922
 www.biloxi.ms.us

DATE: November 13, 2017

RE: Biloxi Police activity for Nov 6 – 12, 2017

TOTAL CALLS FOR SERVICE	2,108
TOTAL INCIDENT REPORTS (Case Numbers)	238
TOTAL OFFENSES (Violations/Reports)	201
TOTAL ARRESTS	90

Calls excluded from call type charts were: Checking Building – 76; Extra Patrol – 829; Suspicious Circumstances – 101; Traffic Stops – 242; and Walk & Talk – 74. Additional details may be viewed at <http://www.crimemapping.com/map/ms/biloxi>.

TOP 20 CALL TYPES BY DESCRIPTION**OFFENSES BY CRIME CATEGORY**



DATE: Nov. 13, 2017

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Nov. 6 – 12, 2017

Building permits issued	34
Construction Valuation of permits issued	\$233,500
Building inspections performed	70
Business licenses	1
Renewals	16
Charter Boats	
Peddler's licenses	
Certificates of occupancy issued	3
Code enforcement cases opened	1
Code enforcement cases resolved	116

Engineering Department

Christy LeBatard, P.E.
Director of Engineering



214-A Delauney Street
P. O. Box 429
Biloxi, Mississippi 39533
Office: 228.435.6265
Fax: 228.435.6179
www.biloxi.ms.us

Engineering Department Weekly Update

November 13, 2017

(updates in bold)

Railroad sign installation is complete, contractor working on punchlist

Cityworks –

- P&R training is complete
- CD is working on inputting their data then training can start
- Fire Department training is complete

Census Address Points – 85% complete

Acacia Storm Drain relocation – request by homeowner for City to purchase pipe

Hurricane Nate

- Starting detailed cost estimates for damages
- Damage repairs for large items pending budget

Projects

- Amtrak rail platform grant – Continuing assisting Southern Rail Commission with grant application
- Bellewood Subdivision – paving complete, contractor still working on punchlist
- **Canaan Fishing Dock Improvements** – meeting with Seymour Wednesday Nov. 15th for project update
- Clearview Drainage – Received PO, contractor finishing Lafayette, then Tremont (Lloyd Moon), then will start on this work
- CSX Crossing Closure – NS contract awarded to begin preliminary work; have MOU with MDOT, working through minor changes; waiting for authority to enter into contract with NS for design work from MDOT

- Dredging – Finished Canaan, working at Point Cadet; Point Cadet & Bayou LaPointe DMR permit modifications currently being processed with DMR;
- Ellzey Place II – continuing with storm drain installation, water & sewer 95% done
- Ellzey Place III – design contract awarded, Rumsey Engineering given ok to proceed
- Emerald Lake Subdivision (Hudson Krohn Rd.) – Utility installation complete; water line still to be testing; working on grading, digging pond, asphalt installation is planned for this week
- Excursion Pier – J.E. Borries given NTP date Oct. 1st.
- Fire Station No. 7 – design 95% complete; working out bid details with SMPDD
- Fire Station No. 10 – clearing and grubbing complete, topographic survey pending
- Holly Bluff – finishing punchlist and MDEQ closeout paperwork
- Howard Avenue –50% design review underway; getting PO for survey for maps & deeds for ROW; 4 way intersection for MLK/Howard/Dukate; need to contact Cotton Fore to request permission to dig up bricks
- Layette Street Drainage – installing drainage in front of Punzo property; contractor should begin work on this in the next few weeks
- Lighthouse Parking Lot - change order to add alternates back to project was approved
- Jordan Subdivision (Old Hwy 78) – Utility installation complete; waiting for road base to set
- Kayleigh Cove Sewer – asphalt complete, waiting for striping; Change Order on tomorrow's agenda for reconstructing road base; change order for sidewalks will be on the 11/14/17 agenda
- Keesler Gate Outside – ready to begin parcel acquisition
- Keesler Gate Inside – design work approximately 90% complete; bidding still on schedule for January 2018
- Ohr O'Keefe Fire Damage Repairs – clean up on-going; kitchen equipment cleaning and repairing finished; floor will be complete this week; change order for additional painting on council agenda tomorrow

- Popp's Ferry Extension – preparing maps & deeds for property acquisition; talking to Coliseum about contributing funds for project
- Pedestrian Crosswalk @ MGM – MDOT opened bids, bids were over budget, waiting to hear back from MDOT on how they plan to proceed
- Pedestrian Crosswalk @ Harbor – Survey complete
- Point to Palace Boardwalk – survey being finalized
- Police Substation Exterior – under construction; expected completion date Nov. 17th
- Police Substation Interior – preparing bid documents to harden the interior, plan to have ready to bid in 30 days
- Public Safety Center Roof Leaks – met with Dale Partners last week, getting a proposal
- **Popp's Ferry Bridge Submarine Cable** – Pre-bid meeting on November 15th
- Popp's Ferry Bridge & Approaches – adding funding back to budget for this year to keep project moving forward
- Popp's Ferry Causeway – construction continuing; adding the following work – sidewalk to Cambridge Drive, additional solar lights, fishing cleaning stations, bait tanks at bait shop, kayak racks at bait shop, additional educational signs and components, upgrade walking trail materials to flexipave; trying to fit in additional parking but looking like there's not enough room; any work at the boat ramp was denied because it wasn't in original scope and there are not permits covering that area
- Post Office Build-out – Finalizing layout for empty space for IS and training facility; then will start preparing plans to go out to bid
- Rock Creek Subdivision Phase II – contractor finishing punchlist, working toward final plat approval; contractor working on re-grading some of the properties along Sage Road to drain toward street instead of toward existing homes in rear
- **Saenger Theater** – Dale Partners submitted an amendment, need direction
- Small Craft Boat Launch – Work has started
- Snyder Center Roof – Met with Dale Partners last week, getting a proposal

- Tennis Court Repairs – Coordinating start date with contractor and Tennis Pro
- Tremont (Lloyd Moon) driveway repairs – contractor will complete Lafayette Street then move to Tremont, expect work to begin before end of year
- **West Biloxi Boardwalk** - Opened bids on Nov. 8th, apparent lowest bidder CM Combs Construction at \$1.097M; apparent 2nd KR Borries Construction at \$1.32M; bids currently under legal review
- Woolmarket Master Plan – Received final draft for review
- Woolmarket Drainage – ready to start easement acquisition and environmental
- Woolmarket water line – have identified a potential grant through the Corps of Engineers, waiting for confirmation from Corps
