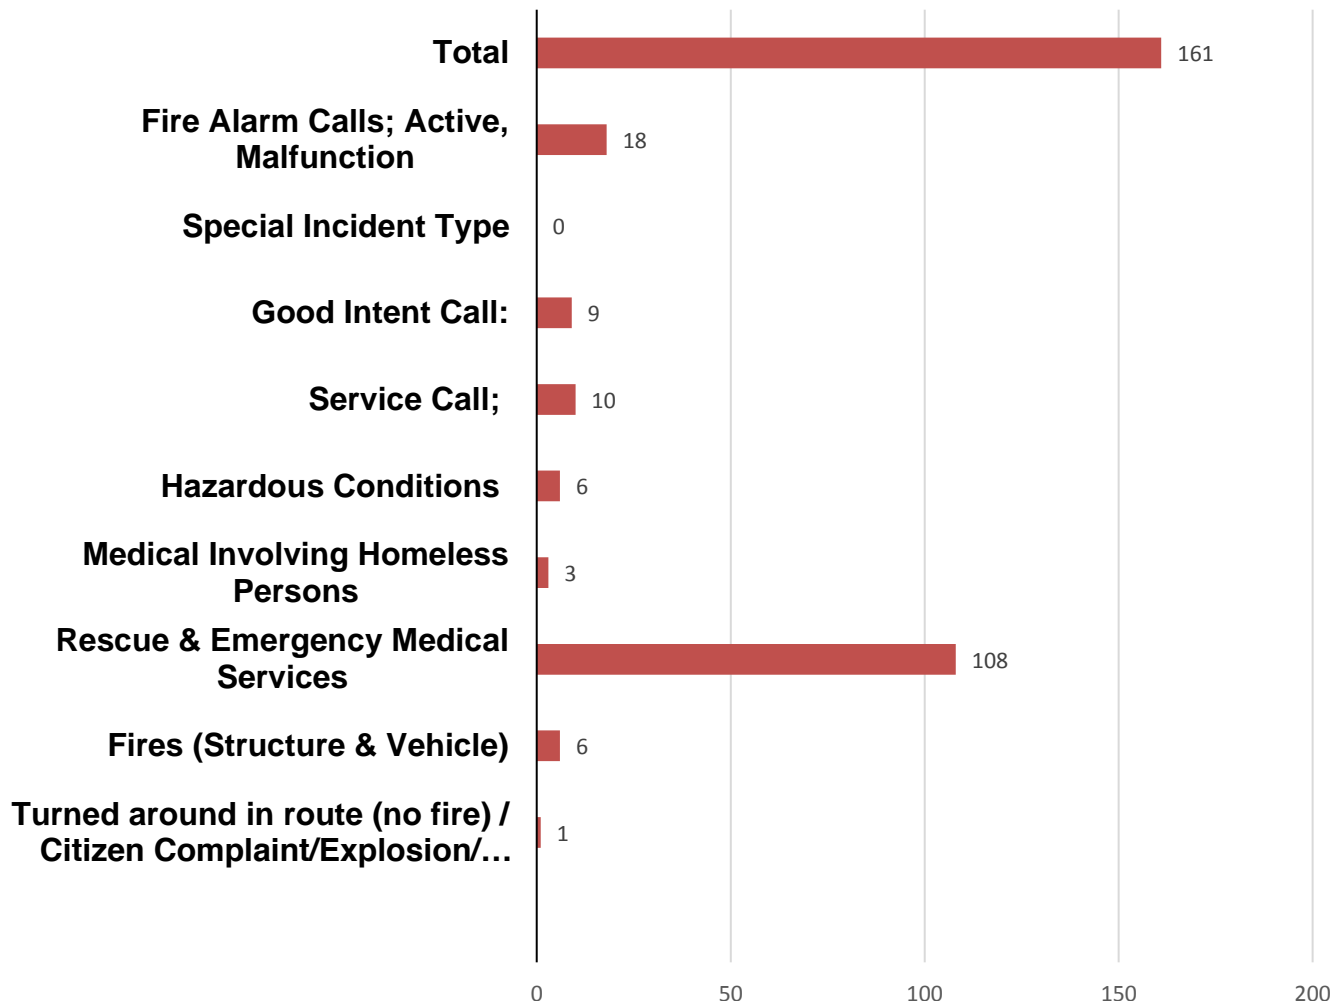




BIŁOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF JUNE 24-30, 2019

<i>Turned around in route (no fire) / Citizen Complaint/Explosion/ other</i>	1
<i>Fires (Structure & Vehicle)</i>	6
<i>Rescue & Emergency Medical Services</i>	108
<i>Medical Involving Homeless Persons</i>	3
<i>Hazardous Conditions</i>	6
<i>Service Call;</i>	10
<i>Good Intent Call:</i>	9
<i>Special Incident Type</i>	0
<i>Fire Alarm Calls; Active, Malfunction</i>	18
Total	<u>161</u>

WEEKLY COUNT OF INCIDENT TYPE



Criminal Intelligence Unit

T. (228) 435-6159

F. (228) 702-3179

ciu@biloxi.ms.us

**Police Chief****John B. Miller**

170 Porter Avenue

Biloxi, Mississippi 39530

Office: 228.435.6100



Fax: 228.374.1922

www.biloxi.ms.us

DATE: July 1, 2019**RE:** Biloxi Police activity for June 24 – 1 July, 2019

TOTAL CALLS FOR SERVICE	2,028
TOTAL INCIDENT REPORTS (Case Numbers)	243
TOTAL OFFENSES (Violations/Reports)	328
TOTAL ARRESTS	145

Calls excluded from call type charts were: Checking Building – 37; Extra Patrol – 570; Suspicious Circumstances – 100; Traffic Stops – 197, and Walk & Talk – 165. Additional details may be viewed at <http://www.crimemapping.com/map/ms/biloxi>.

TOP 20 CALL TYPES BY DESCRIPTION**OFFENSES BY CRIME CATEGORY**



DATE: *July 1, 2019*

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR June 24 – 30, 2019

Building permits issued	<i>60</i>
Construction Valuation of permits issued	<i>\$635,500</i>
Building inspections performed	<i>146</i>
Business licenses Renewals Charter Boats Peddler's licenses	
Certificates of Occupancy issued	<i>14 (0 of those were for Short- Term Rentals)</i>
Code enforcement cases opened	<i>191</i>
Code enforcement cases resolved	<i>120</i>



Engineering Department Weekly Update

July 1, 2019

(updates in bold)

Cspire Fiber Install –

- East Biloxi (North of Division) – should be complete by end of June
- Howard Avenue from Nixon to Maple – complete in 2 weeks
- Pass Road from Hiller Dr. to McDonnell – complete by end of May
- Popps Ferry south of Bridge – complete by end of June
- Irish Hill – need to get a status
- Rejected sidewalk; going to be replaced waiting on a date

Centerpoint Repairs –

- We've already notified Centerpoint that the temporary patches made at Esters & Reynoir and Esters & Main are not acceptable, they must be limestone
- We've also requested they be paved asap
- Met with Centerpoint again last week notified them again the repairs are not happening fast enough – reminded them that ordinance gives them 3 days and they are not meeting that requirement
- Had another issue last week working without a permit twice and damaged water lines both times – getting costs from PW to charge Centerpoint

Projects

- Atkinson Road – Met with GRPC, they agreed to fund the traffic study funding won't be available until October 2019
- Bayview Avenue Boardwalk – Permits are approved; Revised plan estimated cost \$2.8 million; ready to move forward with design contract when funding is available;
- Bayview Ave. Bridge Replacement (State-Aid Project) – Bridge construction started; demolition should be this week
- **Belle La Vie Parkway** – wetlands permit application has been submitted; received bid plans; waiting on specifications; plan to advertise for construction this week.
- Building Façade Program (CDBG) – program has been advertised; work is pending applications

- Canaan Fishing Dock Improvements – received DMR & Corps permits, ready to move forward with design contract when funding is available
- Cedar Lake Bridge Repairs (Const. Funding 2021) – Have executed MOA; met with DE to request an updated contract; and then met again on site for them to review the current condition of bridge; waiting on a design contract
- Circle Park Upgrades – working up preliminary site plan for approval;
- Citywide Street Paving
 - Jim Byrd Road – *waiting on County*
- Crowder Drainage – on the list for the Repair/Replace Contract which opens bids on June 12th
- **CSX Crossing Closure (CDBG Funded)** – *received application for inspection fees from CSX, once that is approved by council we will have clearance from CSX to work; only have two acquisitions remaining and then construction can begin*
- CSX Crossing Closure Delauney & Nixon – had a very successful meeting with CSX, once we receive the crossing closure agreements from CSX we can proceed with those two closures
- **East Biloxi Public Access & Living Shoreline** – DCD Construction \$1.8M; NTP Oct. 8, 2018; Completion Aug. 9, 2019; *change order for additional lighting on July 2nd council meeting*
- East Biloxi Boardwalk (Small Craft to Kuhn St.) – Pending design contract
- Eagle Point Park – project status meeting on 5/29; plans will be ready to bid in mid July;
- Ellzey Place II – final plat approved; Lane Construction submitted a bond for the sidewalk repairs
- **Ellzey Place III (Medical Park Drive Extension)** – Wetlands permitting public comment period has ended; should have permit by mid-June barring no issues; project out to bid; receive bids August 31st
- Fire Station No. 7 – NTP August 15, 2018, Starks Construction; foundation work complete; structure up; CMU walls are up; roof nearing completion
- Fire Station No. 10 – Completion Date: 6/28/2019; Contractor: JW Puckett \$2.35 million; foundation work complete & waterline along old Hwy 67 underway; CMU walls are up, roof work starting next

- Glen Eagle Subdivision (formerly Jordan Subdivision) – waiting for dry weather to do soil cement
- **Henry Beck Park Restroom** – *Bids opened June 12th; bids came in over budget*
- **Hiller Park Trail** – Bids opened May 15th, *additional funding from MSDWF on council agenda for July 2nd*
- Howard Avenue – Completed final walkthrough; punchlist items remaining;
- **Keesler Gate Outside** – Property acquisitions continuing with only 8 just compensations remaining, and approx. 15 out of 27 acquired. All but one *asbestos survey completed ,once reports are available we will begin demo of houses using Community Development's contractor; we'll start getting the PO's this week*

Ready for Demolition

- Michael S. McCarty – ready for demo
- Howard Ave. Properties – ready for demo
- Eric & Martha O'Connell – ready for demo
- Arlan & Lorna Richard – ready for demo

Already demolished

- Adcock Family Partnership

- Keesler Gate Inside – Necaise Brothers Const. \$4.8 million, Completion Date 11/12/2019; change order approving the roundabout approved by council
- **Main Street Railroad Crossing Upgrades** (MDOT Funding 2020) – *held the MDOT kickoff/field review meeting; project ready to bid by September 2019;*
- Malpass Landing/Watersview – regrading of rear yards is complete as a temporary fix; need to hire a DE to come up with a more permanent solution; using the Repair/Replace contract which opens bids June 12th
- Nature's Trail – sewer complete, waterline delayed due to rain
- Old Brick House Sidewalk – sidewalk is laid out, making a final few adjustments then will be PO from sidewalk semi annual bid contractor
- **Parking Lot upgrades** – Lot next to Margaritaville and south of Bridge at Golden Nugget; *met with both proposers; selection committee meeting this week to make a recommendation*
- Pine Grove Drainage – pipe videos are complete, received videos and reports; pipe videos show damages from Hwy 90 to Mercury Lane;

- Pedestrian Crosswalk @ Harbor –Dan Hensarling, Inc. \$2.4M; NTP October 8, 2018; work on-going;
- Point Cadet Marina Improvements (West) #1024 – Old Task “A” & “C”; currently on hold
- Point Cadet Waterfront (Boardwalk) – Design pending final scope of work
- **Popps Ferry Extension #913** – Coliseum has the draft MOU for Board approval; 32 parcels to acquire; all surveys complete; 15 appraisals complete; 4 acquired; *Build Grant application proceeding*

Ready for Demolition

- 310 Oakmont – pending asbestos report

Already demolished

-

- **Popps Ferry Bridge Submarine Cable** – *shutdown is complete; bridge back operating for marine traffic*
- **Popps Ferry Bridge & Approaches** – pending EA approval; once the EA is approved by MDOT and FHWA, we will be asking for permission to start acquiring ROW; *received comments back on revised EA; have a few issues to respond back to; still working toward having it approved by early Fall with final ROW plans before the end of the year*
- Port Commission Roof Repairs – 90% plans under review
- Public Excursion Pier South of Pine/Cedar #1030 – Old Task “B” on hold
- **Public Safety Center Roof Leaks (3rd floor sealing)** – *Notice to Proceed July 7th; should only take 3 weeks to complete*
- Repair/Replace Contract – *Bids open June 12th*
 - Churchhill Ditch
 - Pine Grove Drainage
 - Dr. Crowder Drainage
 - Saenger Alley
- Saenger Theater Phase I & II Fly Tower & Exterior – Bids opened April 10th; bids on hold pending additional funding; need alley work completed
- Saenger Theater Phase III Interior – start design in summer 2019, bid for construction by beginning of 2020

- **Sediment Removal Phase II** – Hiller Park Pond/Beau Chene/Cedar Lake Rd. Canal/Cedar Lake – Broadus/Kennedy Ln/Savannah Estates; Eagle Point Pin Oak; we still have Goosepoint/Lakeview/Fairview area that is already permitting but hasn't been dredged; *met with Seymour to discuss developing a dredging maintenance plan*
- **Shriners Blvd. Drainage** - Overstreet & Associates developing a drawing for the additional drainage pipe crossing Shriners Blvd.; *waiting on a proposal from Overstreet*
- Smith Subdivision (north corner of Woolmarket Rd. & Old Hwy 67) – water line tie into Larkin is complete
- Snyder Fence Repairs – Parks and Rec to get quotes
- Snyder Pool Repairs – Pending scope of work from Parks & Rec.
- **Tanglewood Infrastructure** – Machado Patano contract approved on May 7th; scheduling their surveyor will forward date when available; *meeting with MP this week for a project update*
- Ward 4 Paving
 - Waiting for County approval to cover half the costs for Baywood & Rustwood
 - On The Green – on County's schedule to complete
 - La Bonne Terre – PO for finishing and concrete emailed to PW
 - Working on a list of streets for pavement preservation will have by end of May
- Ward 6 Paving
 - Working on a list of streets for pavement preservation, will have by end of May
- West Biloxi Boardwalk Phase 1B – Construction pending tidelands leases and easements
- **Woolmarket City Center Addition** – *preconstruction meeting held; start date pending delivery of metal building structure approx.. 6 weeks out.*
- Woolmarket Rd. East Drainage – Met with DE 5/29 for progress; bid plans & specs will be ready by end of July; wetlands permit will be submitted by end of June; legal & acquisitions contracts are in place to being easements
- **Woolmarket Rd. East (Larkin) water line** – *final change order and pay estimate on city council for July 2nd*
- **Woolmarket Road Sidewalks** – pending design contract from Machado Patano; *scheduling a project status meeting with week with MP*
