

**Criminal Intelligence Unit**

T. (228) 435-6159  
 F. (228) 702-3179  
 ciu@biloxi.ms.us



**Police Chief  
 John B. Miller**



170 Porter Avenue  
 Biloxi, Mississippi 39530  
 Office: 228.435.6100  
 Fax: 228.374.1922  
 www.biloxi.ms.us

**DATE:** May 30, 2022

**RE:** Biloxi Police activity for May 23-29, 2022

<b>TOTAL CALLS FOR SERVICE</b>	<b>1,442</b>
<b>TOTAL INCIDENT REPORTS</b>	<b>160</b>
<b>TOTAL OFFENSES (Violations/Reports)</b>	<b>194</b>
<b>TOTAL ARRESTS</b>	<b>67</b>

Calls excluded from call type charts were: Extra Patrol – 194; Suspicious Circumstances – 93; Traffic Stops – 133; and Walk & Talk – 49. The Biloxi Police Crime Map may be viewed at <https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f>.

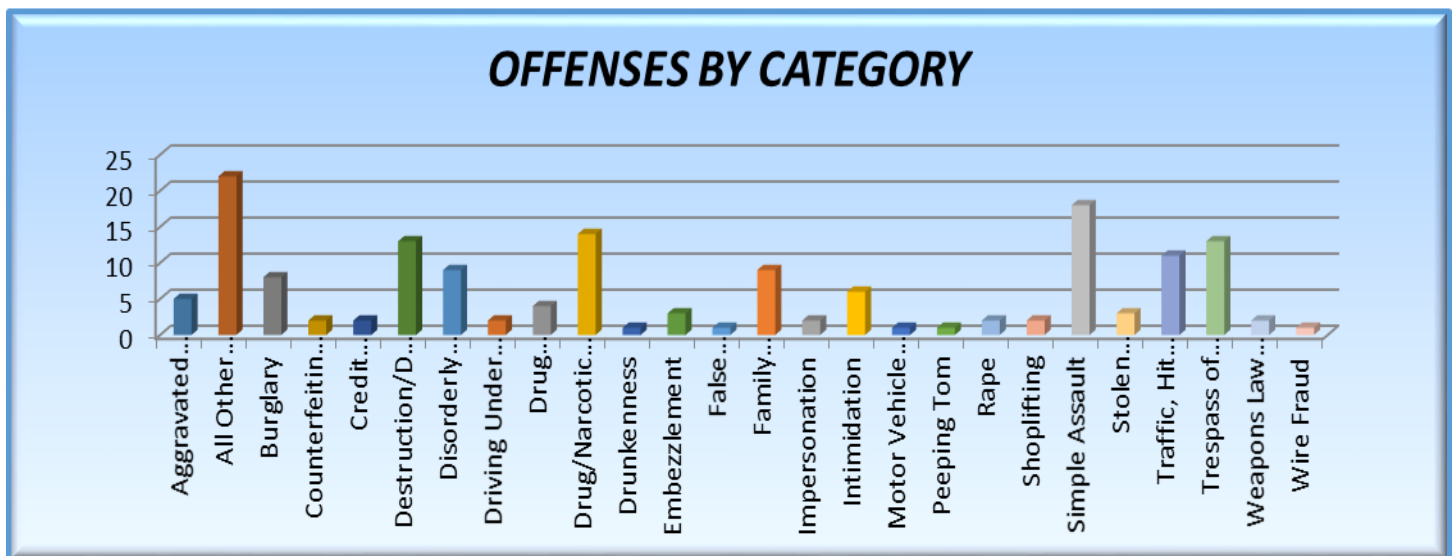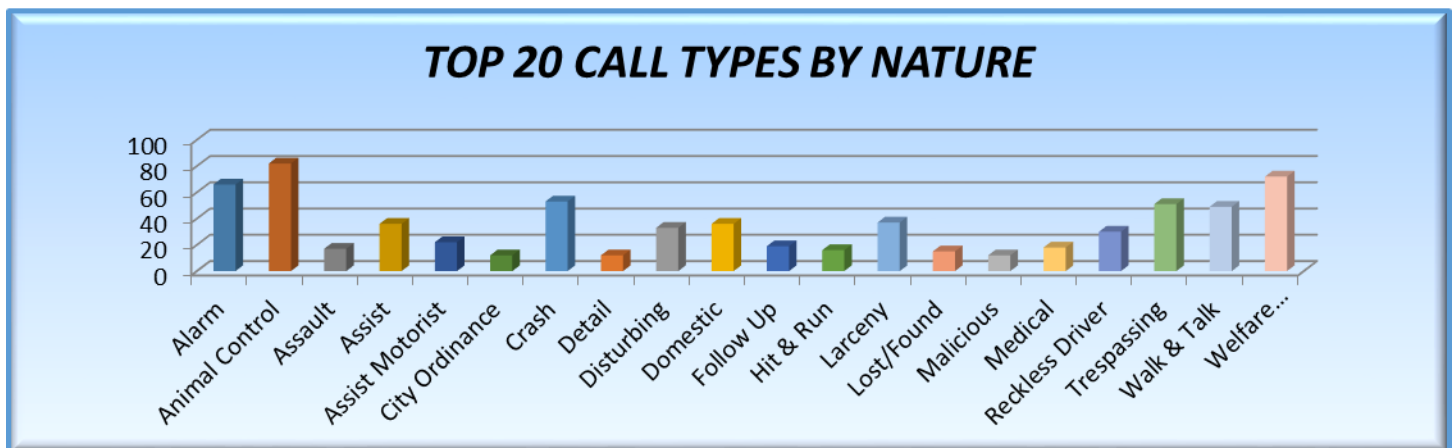



DATE: May 30, 2022

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR May 23 - 29, 2022

<i>Building permits issued</i>	59
<i>Construction Valuation of permits issued</i>	\$133,000
<i>Building inspections performed</i>	102
<i>Business licenses</i>	2
<i>Renewals</i>	1
<i>Charter Boats</i>	
<b>Peddler's licenses</b>	
<i>Certificates of Occupancy issued</i>	13 (3 were Short-Term Rentals)
<i>Code enforcement cases opened</i>	77
<i>Code enforcement cases resolved</i>	67



Engineering Department Weekly Update

May 25, 2022

PROJECT	ENGINEER ASSIGNED	STATUS
Bay Vista Water Well	EO	Received permit, Design completed. Ready to bid. Awaiting ARPA funding decision.
Bayview Avenue Walkway	MH	Finishing punch list. Substantial completion was March 29 <sup>th</sup> Ribbon cutting June 14 <sup>th</sup>
Canaan Fishing Dock	ML	On hold for GOMESA funding
Cedar Lake Bridge Repairs	EO	Design of repairs working through MDOT LPA process. GRPC TIP shows no design funding – only construction. Awaiting result of State Aid bridge inspection. Public Works is making temporary repairs to roadway
Citywide Street Paving	DN	Backlog waiting paving are Laurel Wood and Ravenwood streets Croesus between Jackson and Hwy90. And Esters from Caillavet to Reynoir.
Concrete Annual Contract	DN	Sidewalk on Irish Hill completed. Working Curb and gutter on Ravenwood done.
Eagle Point Park	MH	Ordered playground equipment. Contractor on pavilion terminated – new contract awarded and started. Parking lot ordered for paving. Benches ordered. Fencing completed
CSX Crossings		Nixon and Dorries crossings closed; Delauney and Iriquois closings will be scheduled next
Dredging City Wide	PD	Tidelands grant for Parkers Creek boat ramp dredging was received. Permit mitigation issues with Subsurface Aquatic Vegetation being worked. Permit received for maintenance dredging in Point Cadet Marina and work done.
Hiller Park Boat Ramp Project #1077 Seymour Engineering	GP	Design complete. Project bid and awarded to JE Talley. Notice to proceed will be issued.

<b>PROJECT</b>	<b>ENGINEER</b>	<b>STATUS</b>
Keesler Gate Outside	MH	MS power has wires in duct bank Road work underway... Additional 128 days to be added for lighting only. Base course pavement placed round about to Benachi
Keegan's Bayou Restoration Project #1068	GP	GOMESA Project Submitted to DMR. Permits being requested. Also put project in Restore Act Portal
Kuhn Street Boat Ramp and Parking	PD	Phase 1 (boat ramp) working design and permits. Funding for Phase 2 (parking) was received from Tidelands fund. Removal of marine vegetation being mitigated.. With funding received have restarted design effort
Point Development Project #1092	GP	Conceptual phase – Machado Patano
Lorraine Road Water Line	EO/PD	First phase complete. Lorraine water line phase 2 design complete and being prepared to bid. Have done "peer review" with Neel Schaffer. Water model for pressure at terminus.indicates pressure is acceptable. Bid awaiting ARPA funding decision.
Main Street Railroad Crossing	EO	Design complete. Authority to bid received from MDOT. CSX has committed support for project. Will advertise in May
Passenger Train Rail Platform	EO	AMTRACK taking over design and construction of passenger platform. Status request sent to Southern Rail Commission
Point Cadet Living Shoreline Project #1066 (BMA)	GP	Tidelands project awarded. Kick off meeting held with Design Engineer (BMA). Coordinating with BMA and Covington Engineering on a companion shoreline project funding by National Fish & Wildlife Foundation Need BMA Contract
Popp's Ferry Extension	ML	Right of Way acquisition nearly complete.. Pending Construction Funding. Submitted RAISE Grant 2022. Additional funding \$3 Million approved in Gulf Coast Restoration Fund. CSX closing permit being worked. Plan to bid in late 2022. Construction in 2023. RAISE grant submitted.
Sand Re-nourishment GOMESA funded	GP	Permitting being completed. Bid package for acquisition of sand and placement being worked by Covington. \$1 Million
<b>PROJECT</b>	<b>ENGINEER</b>	<b>STATUS</b>
Popp's Ferry Bridge	ML	Design Phase I being completed; Contract for Right of Way property acquisition being developed. Environmental Assessment being updated

Repair Replace Contract	DN	DNA underground contract expired. New contract being awarded to Bottom to Top. Pre- construction meeting with engineering, public works and contractor held.
Saenger Theatre Restoration	MH	Fly Tower, Roof and HVAC complete. selective interior demolition complete, Approved change order for west (front) elevation. Requested Gulf Coast Restoration funding for interior work – no luck. Change order issued for doors and other exterior work including repair/painting of stucco on west facade
Shriners Road Utility Extension (The “Preserve”)	PD	Survey complete. Design complete. Health Department approval received. Coordinating with developer for “the Preserve” on date needed the water/sewer service. Awaiting ARPA funding decision
Walkway - Small Craft Harbor to Oak Street	MH	Work underway . Construction of vertical “knee) wall has begun.. horizontal walk way 90% complete July 8 <sup>th</sup> is current completion date. Lease Turn nesting area has caused a 30 day extension of work
Visitor Center Repairs	EO	Roof replacement bid awarded to Mandell Roofing. NTP issued. Change order issued for additional days awaiting roof tiles. Bids opened for hurricane Zeta and non hurricane repairs. Award made to Hopkins Construction. Notice to Proceed ordered
Woolmarket Sidewalks	EO/PD	Sidewalk extended to Shriners Blvd. Bid package reviewed by MDOT. Working changes that resulted from MDOT review. Hope to advertise in May
Pickleball bathroom	PD	Design complete ready to prepare bid package
McDonnell road extension	DN	Working design of roadway and extension of utilities
West Biloxi Master Plan	GP	complete
Causeway Park floating docks	DN	Preparing re-bid with revised bid tab
<b>ZETA (Hurricane Damage Repairs)</b>		
Oak Street Pier (South)	DN	Cypress engineering presented concept plans to Mayor – will now work in

		developing design contract. PO issued for immediate repairs
Coliseum Pier	PD	work complete
Small Craft and Commercial Harbor	GP	Opened bids. Contract awarded to JE Borries. Notice to Proceed issued.
Causeway Park Bait Shop Roof	DN	Roof warranty work completed
Multiple Piers – minor repairs	DN	Oak street north, Ice wharf pier, Forrest ave pier and Kuhn street pier – PO issued to Boories and work complete and invoiced
Ed Ott	EO	
Milady Howard	MH	
Parker Darphin	PD	
Danny Nguyen	DN	
Gerald Pitalo	GP	
Mike Leonard	ML	

**SUBDIVISION STATUS**

Parker Darwin is point of contact for DRC

Subdivision	Units	Engineer / Builder	Status	Inspector Assigned
The Preserve	207	Pickering	Preliminary plat given, waiting on material submittals	Ryan
Eula Cove Townhomes	40	Andy Phelan	Preliminary plat given, material submittals recieved	Jacob
Emerald Lake	131	Dennis Stieffel	Under Construction. Paving last two sections in April	Wiley
Anchors Landing	66	Heinrich & Associates (Terry Moran)	Approved, waiting on MDEQ approval	Not yet assigned
The Reserve at Marsh Landing	9	Machado Patano (Jack Schmidt)	Under Review – need drainage and utilities plans	Ryan
Pointe Breeze (Grande View)	39	Knesal Engineering	Preliminary Plat approved by council. Infrastructure approved by engineering	Ryan
Shorecrest Road	54	Kris Rienman	Under Review	Wiley
Caillavett Cottages	9	Machado Patano (Jack Schmidt)	Under Review	Jacob
College Cove Townhomes	12	Andy Phelan	Under Review	Jacob
Park Court North	11	Thom Newman	Under Review	Not yet assigned
Jim Byrd Road Subdivision	30	Dennis Stieffel	Under Review	Wiley
