


## BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF Aug. 1- Aug. 7, 2022

The same of the sa	THE WEEK OF Kag. 1 Hag. 1, 2022		
	1- Fires (Structure & Vehicle)		4
	2 - Rupture/Explosion		1
	3 - Emergency Medical Services/Rescue		1 19
	4 - Hazardous Conditions		0
	5 - Service Calls		11
	6 - Good Intent		6
	7 - Fire Alarm Calls; Active, Malfunction		14
	8 - Weather/Natural Disaster		0
	9 - Special Incident Type		3
<u> </u>		Total	158

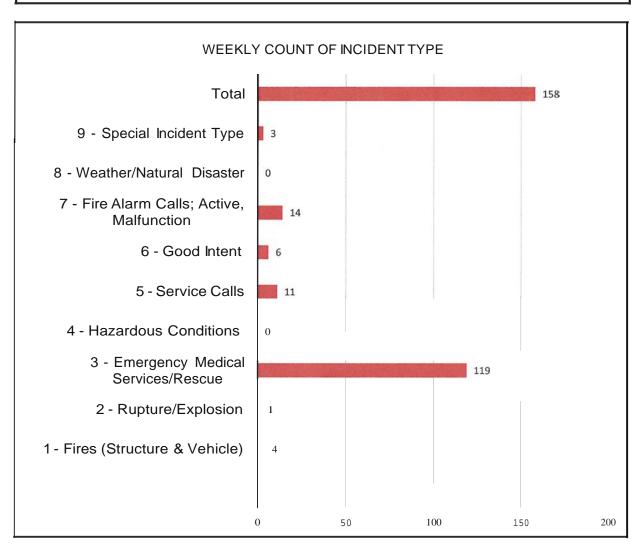

#### **Criminal Intelligence Unit**

T. (228) 435-6159 F. (228) 702-3179 ciu@biloxi.ms.us



#### Police Chief John B. Miller


170 Porter Avenue Biloxi, Mississippi 39530 Office: 228.435.6100 Fax: 228.374.1922 www.biloxi.ms.us


**DATE:** August 8, 2022

RE: Biloxi Police activity for August 1-7, 2022

TOTAL CALLS FOR SERVICE	1,573
TOTAL INCIDENT REPORTS	196
TOTAL OFFENSES (Violations/Reports)	183
TOTAL ARRESTS	99

Calls excluded from call type charts were: Extra Patrol – 293; Suspicious Circumstances – 95; Traffic Stops – 211; and Walk & Talk – 71. The Biloxi Police Crime Map may be viewed at <a href="https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f">https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f</a>.







# DATE: August 8, 2022 COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Aug 1 - 7, 2022

Building permits issued	67
Construction Valuation of permits issued	\$3,044,500
Building inspections performed	74
Business licenses	13
Renewals	0
Charter Boats	
Peddler's licenses	
Certificates of Occupancy issued	7 (1 was Short-
	Term Rentals)
Code enforcement cases opened	30
Code enforcement cases resolved	41



# **Engineering Department Weekly Update**

# August 05, 2022

ENGINEER ASSIGNED	STATUS
EO	Received permit, Design completed. Ready to bid. Awaiting ARPA funding decision. Awaiting tree removal by Public Works to help access to site.
MH	In 2-year warranty phase
ML	On hold for GOMESA funding
EO	Design of repairs working through MDOT LPA process. GRPC TIP shows no design finding or construction funding. State Aid Bridge Inspection Report received. Plan to submit for MDOT Emergency Road & Bridge Repair Grant.
DN	Working to rebid annual contract with fuel adjustment added
DN	No work issued at the moment
MH	Pavilion complete.
	Nixon and Dorries crossings closed; Delauney and Iroquois closings will be scheduled next
GP	Tidelands grant for Parkers Creek boat ramp dredging was received. Permit mitigation issues with Subsurface Aquatic Vegetation being worked. Permit received for maintenance dredging in Point Cadet Marina and work done.
GP	Design Complete. Project bid and awarded to JE Talley. Construction started on 7/18 as per NTP for 90 days complete on December 1 2022.
MH	I-110 ramp closure 8/15, delivery of light poles 10/14. Completion expected Nov 2022.
	ASSIGNED EO  MH ML EO  DN DN MH GP

PROJECT	ENGINEER	STATUS
	ASSIGNED	
Keegan's Bayou	GP	GOMESA Project Submitted to DMR.
Restoration Project #1068		Permits being requested. Project in
		Restore Act Portal
Kuhn Street Boat Ramp	GP	Conceptual design started; vegetation
and Parking		removal started. Pickering Firm, Inc.
		Decision made to remove parking on
		eastern end of parking lot due to
		TIDELANDS FUNDING ISSUE. Budget
		for project reduced from \$696+ to
		\$500K for construction and remaining
		Engineering Fee.
Point Development Project	GP	SEYMOUR ENGINEERING Final
#1092		design pending DMR permitting
		approval & ACOE PROJECT COST set
		at \$3,000,000.
Lorraine Road Water Line	EO	First phase complete. Lorraine water
		line phase 2 design complete and being
		prepared to bid. Have done "peer
		review" with Neel Schaffer. Water model
		for pressure at terminus indicates
		pressure low but acceptable. Awaiting
		ARPA funding decision.
Main Street Railroad	EO	Design complete. Authority to bid
Crossing		received from MDOT. CSX has
or occurig		committed support for project. Open
		bids on August 31st.
		Contract Awarded
Passenger Train Rail	EO	AMTRACK taking over design and
Platform		construction of passenger platform.
		Status request sent to Southern Rail
		Commission
		TV coverage stated \$3 million for
		rebuilding/repairing the 5 stations
		(Bay Saint Louis, Gulfport, Biloxi, and
		Pascagoula)
Point Cadet Living	GP	BMA started design. Topo completed.
Shoreline		Tidelands/National Fish & Wildlife
Project #1066 (BMA)		Foundation Funding.
Popp's Ferry Extension	ML	Right of Way acquisition nearly
Opp 3   Giry Exterision	IVIL	complete. Pending Construction
		Funding. Submitted RAISE Grant 2022.
		Additional funding \$3 Million approved in
		Gulf Coast Restoration Fund. CSX
		closing permit being worked. Plan to bid
		in late 2022. Construction in 2023.
		III IALO ZUZZ. GUIISLI UGLIUII III ZUZS.

PROJECT	ENGINEER	STATUS
	ASSIGNED	
Sand Re-nourishment	GP	GOMESA PROJET 1064 Covington
		Engineering presented project
		construction and engineering
		schedule, project construction to
		complete prior to turtle's beach
	ML	season November 1,2022.  Design Phase I being completed;
Popp's Ferry Bridge	IVIL	Contract for Right of Way property
Topps reny bridge		acquisition being developed.
		Environmental Assessment being
		updated
Repair Replace Contract	DN	Bottom 2 Top contractor has been
Tropan replace commen		given 12 POs as of 7/11/2022. Work
		on St. George and Seal Avenue has
		been completed. Now finishing up
		Melissa Dr.
Saenger Theatre	MH	Change Order issued for doors and
Restoration		other exterior work including
		repair/painting of stucco on west
		façade. Time extended to 10/31.
		Awaiting CO#14 for remaining west
		façade work below canopy.
		Estimated CO amount is \$85k.
Shriners Road Utility	MH	AFB is imminent. Should open bids
Extension (The "Preserve")		within 4-5 weeks. Overstreet &
Mallana Creat Creat	N 41 1	Assoc. will provide CEI services.
Walkway - Small Craft Harbor to Oak Street	MH	Gray Falcon demobilized from site
Harbor to Oak Street		due to least tern fencing but has been notified to return to work. A change
		order for re-mobilization is expected.
Visitor Center Repairs	EO	Roof replacement bid awarded to
Visitor Certier Nepairs		Mandell Roofing. Change order issued
		for additional days awaiting roof tiles.
		Bids opened for hurricane Zeta and non-
		hurricane repairs. Award made to
		Hopkins Construction. Both contractors
		on site and working as weather permits.
Woolmarket Sidewalks	EO	Sidewalk extended to Shriners Blvd. Bid
		package reviewed by MDOT. Working
		changes that resulted from MDOT
		review. Plan to advertise once
		Environmental approvals are obtained
		which are projected for January 2023.
Pickleball bathroom	GP	Design complete ready to prepare bid
		package

McDonnell road extension	DN	Completed design of roadway and extension of utilities, \$220K+
West Biloxi Master Plan	GP	complete
Lighthouse Pier Parking	GP/MH	Work Complete, Warranty Phase
Causeway Park floating docks	DN	Ready for Bid. Advertised on August 7 & 14
ZETA (Hurricane Damage Repairs)	ENGINEER ASSIGNED	STATUS
(Kepans)	Abbioned	
Oak Street Pier (South)	DN	Cypress engineering presented concept plans. – will now work in developing design contract. PO issued for immediate repairs. Repairs have been completed
Coliseum Pier	GP	Work complete
Small Craft and Commercial Harbor	GP	Project awarded JE Borries Inc, \$555K+ NTP for material PROCUREMENT on 5/17 complete when material received est. Nov. 1, 2022 NTP CONSTRUCTION estimated to begin on NOV 1 for 90 days est completion
Causeway Park Bait Shop Roof	DN	Roof warranty work completed
Multiple Piers – Minor Repairs	DN	Oak Street North, Ice Wharf Pier, Forrest Avenue Pier and Kuhn Street Pier – PO sent to Boories and work complete and invoiced.
HARRISION COUNTY UTILITY AUTHORITY (HCUA)	EO	Studies and planning inside city limits of Biloxi. Two water mains discussed, one to improve low pressure concerns.
MDOT TITLE VI & ADA COMPLIANCE REPORTING	EO	Quarterly and Yearly Updates
WOOLMARKET TRAFFIC STUDY	UA	Traffic counts for 3 intersections involving Shriners with (I-110, Shortcut, and Woolmarket Road) 2 intersections with Old Hwy 67 (Hudson-Krohn, Woolmarket Road) and 1 intersection @ Wash Fayard & John Lee Roads.

Ed Ott	EO	
Milady Howard	MH	
Parker Darphin	PD	
Danny Nguyen	DN	
Gerald Pitalo	GP	
Mike Leonard	ML	
UNASSIGNED	UA	

### **SUBDIVIDION STATUS**

## Dr. Gerald Pitalo is point of contact for DRC

Subdivision	Units	Engineer / Builder	Status	Inspector
The Dreserve	207	Diakarina	Draliminary plat given weiting	Assigned
The Preserve	207	Pickering	Preliminary plat given, waiting	Ryan
Fula Cava	40	Cara Wassas	on material submittals	laaah
Eula Cove	40	Cara Wagner	Preliminary plat given; material	Jacob
Townhomes	404	Description of the following	submittals received	1477
Emerald Lake	131	Dennis Stieffel	In process of signing Final	Wiley
			Approval Letter this week in	
			order to get on next BCC	
Anchors	66	Heinrich	Mtg. Agenda.	Maturat
	00		Approved, waiting on MDEQ	Not yet
Landing		&Associates (Terry Moran)	approval	assigned
The Reserve at	9	Machado Patano	Under Review - Design	Ryan
Marsh Landing		(Jack Schmidt)	submittals estimated end of	
			August.	
Pointe Breeze	39	Knesal Engineering	Preliminary Plat approved by	Ryan
(Grande View)			council. Infrastructure	
,			approved by engineering	
Shorecrest	54	Kris Rienman	Under Review	Wiley
Road				
Caillavett	9	Machado Patano	Design submittals estimated	Jacob
Cottages		(Jack Schmidt)	end of August.	
College Cove	12	Andy Phelan	Under Review	Jacob
Townhomes				
Park Court	11	Thom Newman	Under Review	Not yet
North				assigned
Jim Byrd Road	30	Dennis Stieffel	Under Review	Wiley
Subdivision				
