Criminal Intelligence Unit T. (228) 435-6159 F. (228) 702-3179 ciu@biloxi.ms.us



Police Chief John B. Miller


170 Porter Avenue Biloxi, Mississippi 39530 Office: 228.435.6100 Fax: 228.374.1922 www.biloxi.ms.us


DATE: July 27, 2020

RE: Biloxi Police activity for July 20-26, 2020


| TOTAL CALLS FOR SERVICE | 1,522 |
|---------------------------------------|-------|
| TOTAL INCIDENT REPORTS (Case Numbers) | 227 |
| TOTAL OFFENSES (Violations/Reports) | 306 |
| TOTAL ARRESTS | 127 |

Calls excluded from call type charts were: Checking Building – 40; Extra Patrol – 382; Suspicious Circumstances – 86; Traffic Stops – 52; and Walk & Talk – 118. Additional details may be viewed at http://www.crimemapping.com/map/ms/biloxi.



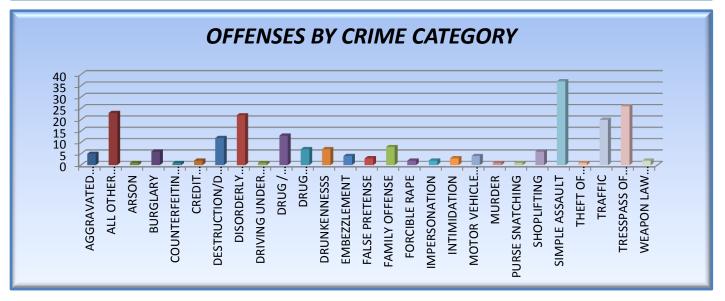

| BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF JULY 20-26, 2020 | |
|---|------------|
| Turned around in route (no fire) / Citizen Complaint/Explosion/ other | 1 |
| Fires (Structure & Vehicle) | 6 |
| Rescue & Emergency Medical Services | 81 |
| COVID 19 | 5 |
| Medical Involving Homeless Persons | 2 |
| Hazardous Conditions | 5 |
| Service Call; | 17 |
| Good Intent Call: | 10 |
| Special Incident Type | 1 |
| Fire Alarm Calls; Active, Malfunction | 12 |
| Total | <u>140</u> |

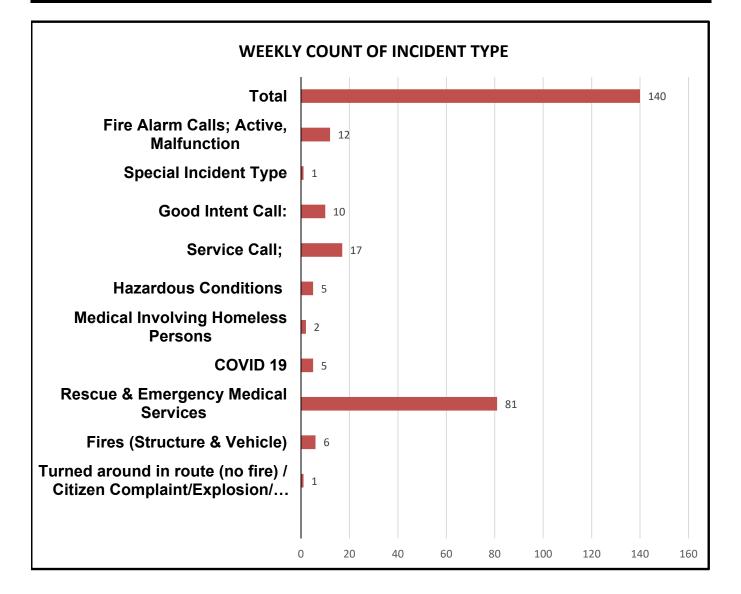



DATE: July 27, 2020 COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Jul. 20 - 26, 2020

| Building permits issued | 84 |
|--|-------------------|
| Construction Valuation of permits issued | \$755,400 |
| Building inspections performed | 128 |
| Business licenses | 3 |
| Renewals | 2 |
| Charter Boats | |
| Peddler's licenses | |
| Certificates of Occupancy issued | 13 (2 were Short- |
| | Term Rentals) |
| Code enforcement cases opened | 205 |
| Code enforcement cases resolved | 54 |

Engineering Department Weekly Update July 27, 2020 (updates in bold)

Projects Out to Bid

- Bayview Ave. Boardwalk (8/5)
- Canaan Fishing Dock Repairs (7/22)
- Oakmont St. House Demo (7/29)
- Tanglewood Infrastructure Rebid (8/5)

Projects in the Process of Being Awarded

Projects Under Construction

- Asphalt Annual Contract
- Belle La Vie Parkway
- Division St. Houses Ph 2
- Division St. Houses Ph 3
- Eagle Point Park
- East Biloxi Connector Rd
- Ellzey Place Phase III
- Fishing Bridge Lights
- Keesler Gate Inside
- Lorraine Rd. Waterline

- Pavement Preservation Ward 4
- Port Commission Roof
- Saenger Theater
- Sidewalk Annual Contract
- Snyder Chiller
- Snyder Pool Repairs
- West Biloxi Boardwalk
- Woolmarket City Center Addition
- Woolmarket Rd. East Drainage

GRANT APPLICATIONS

BUILD Grant Application - Has been submitted and accepted by USDOT

CRISI Grant

- Main St. RR Crossing (recommended by CSX as a source of funding)
- Railroad connector road from Iroquois to Porter north of tracks

Defense Community Infrastructure Pilot Program - Has been submitted

- Keesler Gate Outside shortfall

<u>GOMESA</u> – All have been submitted

- Keegan Bayou Restoration
- Causeway Floating Docks
- Canaan Fishing Dock Improvements
- Point Cadet Living Shoreline & Bulkhead
- Wave Outfalls

<u>Tidelands</u> – All have been submitted.

- Kuhn St. Boat Ramp
- Canaan Fishing Dock Improvements
- West Biloxi Boardwalk White to Rodenberg
- Eagle Point Park
- Causeway Floating Docks
- Point Cadet Living Shoreline (w/o bulkhead)
- Lee St. Boat Ramp

Gulf Coast Restoration Fund

Popps Ferry Extension

Cspire Fiber Install

- Subdivision Installs
 - Bridgefield (boring)
 - Bent Oaks (splicing fiber)
 - Channel Mark (permit pending)
 - o Emerald Lake
 - La Bonne Terre (pulling fiber)
 - Malpass Landing (pulling fiber)
 - North Haven (pulling fiber)

- o Pelican Bayou (pulling fiber)
- Peninsula (boring this week)
- Popps Ferry Landing (pulling fiber)
- Reunion Place (pulling fiber)
- o River Place (splicing fiber/punchlist)
- o Rock Creek
- Taylor Oaks (pulling fiber)
- Debuys & Pass Sewer Main damage Hart's Const. filed a claim on their insurance, adjuster wanted to cut a check to COB for repair. Public Works is getting a cost.
- 911 Bordonne Dr. sprinkler head damaged, Cspire working with homeowner to resolve
- 425 Babineaux Pl. sidewalk needs repair

Centerpoint Repairs

- Repairs
 - o 372 Reynoir St.
 - o 133 Lee St.
 - o 444 Jordan Dr.
 - o 266 Debuys Rd.
 - o 304 Lee St.
- New Services
 - o 421 Debuys Rd.
 - o 734 Buddleia Cv.

Sparklight Projects

- 2108 Baywood Dr.
- 2398 Beau Chene
- 859 Flamingo Cove
- 675 Waters View Dr.
- 2600 LeJuene Dr.

AT&T Projects

- Repaving Roy St. working with Insurance Adjuster
- Small Cell Tower Installs
- Glen Eagle Phase 2
- Nature's Trail Phase 2
- Cedar Crescent (under review)

- New Mains at
 - Cedar Crescent Subd.
 - Jefferson Davis Ave. (I-110 to north of Hwy 90)
 - Hiller Drive East, East Drive & West Drive (pending)

Projects

- Atkinson Road Traffic Study received MDOT MOU, sending design contracts to MDOT for review
- **Bayview Avenue Boardwalk** receive bids August 5th
- Belle La Vie Parkway Notice to Proceed 2/8/2020; Completion 8/26/2020; work ongoing
- Canaan Fishing Dock Improvements (reconstruction) received DMR & Corps permits, have DE contract, going to hold for now
- Canaan Fishing Dock Maintenance Repairs receive bids July 22nd
- Cedar Lake Bridge Repairs (Const. Funding 2021) Have executed MOA; drafting a letter to DE requesting completion of contract
- Churchill Drainage redesign at approximately 50%
- City Hall Lobby Is engineering supposed to be doing anything with this?
- Citywide Street Paving
 - Snug Harbor being done by County
 - McDonnell Avenue \$40K for just road, additional \$40K to add utilities
 - o Sidewalks for Councilman Lawrence
 - o Woolmarket Lake Road
 - o Southern Ave.- requested by Councilman Lawrence, county going to handle
 - Greater Ave. requested by Councilman Lawrence; county going to handle
 - Bay Vista Streets Bay Vista Dr., Randall Dr. and Hilton Dr. requested by Councilwoman Newman
 - o St. Martha & St. Mary requested by Councilwoman Newman
 - o Laurelwood
 - o Ravenwood
 - Tennis Courts at Circle Park

- Concrete Annual Contract

- Work under north contract compiling phase 2 work
 - o Croesus
 - o Reynoir
- o Base for Fred Haise Statue & Bollards
- o Bollards at East Biloxi Boardwalk Project and around splashpad
- Sidewalk at Sunkist and Popps Ferry Road need to work up cost
- o East Biloxi Boardwalk Nate washout areas need concrete

- CSX Crossing Closure Delauney & Nixon have PO, waiting on contractor to schedule the work
- Eagle Point Park Start date of June 1st; work on-going
- East Biloxi Connector Road (CDBG Funded) clearing and grubbing, and house demo's have started.
- Ellzey Place III (Medical Park Drive Extension) NTP Feb. 17, 2020; completion August 16, 2020; *work finishing up*
- Old Hwy 90 Fishing Bridge Lighting repairs project awarded May 26th, contractor is working with light manufacture to ensure fixtures will properly attached to existing poles; we will fix the light poles that are leaning due to Cristobal with this work
- Keesler Gate Outside All asbestos survey completed; demolition has started; Phase 1 to Iroquois Street will be ready to advertise before the end of August

Offers made

o 1011 Division St.

Acquired not ready for demolition

- o 1057 Division St.
- o 987 Division St.
- o 964 Division St.

Ready for Demolition

- o 1015 Division St.
- o 997 Division St.
- o 978 Division St.
- o 962 Division St.
- o 974 Division St.

Ready for moving -

- 956 Division St. pending moving other two houses
- 960 Division St. pending moving other two houses

Acquired not requiring demolition

- o 1029 Division St
- o 1092 Division St.
- o 1067 Division St.
- 0 Division St. 1310H-02-077.000
- 0 Division St. 1310H-02-035.000
- o 305 Seal Ave.
- 970 Division St. (moving house back)
- o 290 Forrest (only have ROE)
- o 1087 Division St.
- o 1075 Division St.
- o 290 Forrest Ave.

Already demolished/moved

- o 301 Seal Ave.
- o 1001 Division St.
- o 1007 Division St.
- o 1098 Division St.
- o 991 Division St.

- Keegan Bayou Restoration - Contract on the May 19th agenda, design work underway

- Keesler Gate Inside Completion Date 6/2020; roundabout complete except for final asphalt and Larcher Blvd. intersection curb being installed then it will be ready for base asphalt
- Kuhn St. Boat Launch Expansion Design contract on June 23rd council meeting; design underway
- Lorraine Road water line extension apparent Low CB Developers \$587,000; award on the July 7th agenda; waiting on contract documents to schedule pre-con
- Main Street Railroad Crossing Upgrades (MDOT Funding 2020) held the MDOT kickoff/field review meeting; looking for additional \$500K in funding, *completed CSX and MDOT comments, plans are now back at MDOT for "office review";*
- Malpass Landing/Watersview regrading of rear yards is complete as a temporary fix; need to hire a DE to come up with a more permanent solution; using the Repair/Replace contract
- Mason Rd. Waterline Extension potential water line project using water/sewer funds
- Natatorium Roof Leaks –met with Machado Patano to look at roof March 4th; they are going to get up there with water hoses this week to see if they can track down the leak
- Passenger Rail Platform have executed grant agreement, need to start design
- **Point Cadet Shoreline** *permit application is being drafted, expecting a minimum of 6 months to get permits approved*
- Point Cadet Marina West Restore Act application has been submitted to Covington; have draft contract from BMA currently reviewing
- Point Cadet Traffic Analysis – received MDOT MOU, sending design contracts to MDOT for review

Popps Ferry Extension #913 – Coliseum has the draft MOU for Board approval; 33 parcels to acquire; all surveys; appraisals, and review appraisals complete; *House demolition contract receives bids on 7/29*

Negotiation

- o 2400 Beach Blvd. (Coliseum)
- o 128 Oakmont (Coliseum)
- o 161 Oakmont (Coliseum)
- o 173 Oakmont (Shows)
- o 0 Hwy 90 (Coliseum)
- 0 Briarfield (Bhakta)
- 0 Briarfield (Coliseum)
- o 0 Pass Rd. (Salloum)
- 0 Pass Rd. (Hardy Court)
- o 2395 Pass Rd. (NM Markup)

Courts

- o 141 Oakmont (Maddox)
- o 145 Oakmont (Maddox)
- o 2416 Beach Blvd. (Spencer)

Ready for Demolition

- o 135 Oakmont (Olin)
- o 164 Oakmont (Patton)
- o 165 Oakmont (Newton)

- o 2395 Pass Rd. (Burger King)
- o 2393 Pass Rd. (Exxon)
- o 0 Pass Rd. (Biloxi Management)
- o 2401 Pass Rd. (Stewart Family)
- o 2404 Pass Rd. (Shoppes @ PF West)
- o 2423 Pass Rd. (Take 5)
- o 0 Covenant Square (Hardy Court)
- o 2415 Pass Rd. (Hardy Court)
- o 2368 Pass Rd. (PF MS Dev Co)

Purchased

- o 129 Oakmont (Trinh)
- o 131 Oakmont (Trinh)
- o 134 Oakmont (Stacy)
- o 137 Oakmont (Stacy)
- o 149 Oakmont (Sumners)
- o 168 Oakmont (Best)
- o 169 Oakmont (Coliseum)

- Already demolished
 - o 130 Oakmont (Serignet)
- Popps Ferry Bridge & Approaches met with Sharen Willis March 4th to discuss how to move into the ROW phase; BMA 90% complete with ROW plans, anticipate completion August 14, 2020
- Port Commission Roof Repairs working on-going

- Repair/Replace Contract

- Churchhill Ditch 50% plans complete; emergency repair complete;
- o Roy Street -
- Debuys & Pass Cspire Damages
- o Malpass/Watersview Drainage
- Lorraine Road (Bruce Wilson)
- Seal @ Howard Sewer Repair
- Scenic River Drainage
- Wash Fayard Rd. Culverts
- o IP Parking Lot

- McDonnell Ave. extension road base only
- o Magnolia Street driveways and curb cuts for Infrastructure
- Cambridge Drive Drainage
- Lorraine Road waterline
- o 229 Dewey Circle inlet
- Tara Lane Drainage (\$200,000)
- Saenger Theater Phase I & II Fly Tower & Exterior Blackline is working up a revised proposal for the brick repair & repointing for a September approval; there are several leaks in the north and south auditorium walls which are not covered in this current contract;
- Saenger Theater Interior Condition Assessment after the 1st of the year
- Sediment Removal Phase III hydrographic surveys complete, working on the permit applications, the sites that have SAV, Seymour is trying to work with DMR on a way to mitigate.
 - Hiller Park Pond
 - o Cedar Lake Rd. Canal
 - Cedar Lake Broadus
 - Kennedy Ln (SAV)
 - Savannah Estates (DMR stated not eligible)
 - Eagle Point Pin Oak (SAV)
 - o Linda Dr. (SAV)
 - Beau Chene (DMR stated not eligible)
- Sediment Maintenance Plan Have 100% draft for review
- Small Craft to Oak St Boardwalk Expect to have 90% plans in early August
- Snyder Center Chiller Replacement contract awarded, going to be 8 weeks until chiller gets here
- Snyder Pool Repairs awarded to Ewing Pool
- **Tanglewood Infrastructure** rejected 1st bids, readvertised for bids, receive on August 5th
- Visitors Center Repairs working on scope of work to develop plans/specs in house
- Ward 4 Paving
 - On The Green on County's schedule to complete
 - o Baywood, Rustwood, Darwood, Camp Wilkes out to bid; receive bids 2/12/2020
 - Site prep work issues should be complete but now we've got rain most of this week

- Watersview Drainage Cleaning Council Glavan has requested assistance from Harrison County and we have submitted application for wetlands permit; received email from Corps that no permit was needed, DMR is issuing a waiver; County has agreed to haul off debris if City removes it from the wetlands
- West Biloxi Boardwalk Phase 1B NTP April 6, 2020/Comp Sept. 27, 2020, work underway no issues; work on-going, no significant issues
- West Biloxi Boardwalk Phase 2 east of existing boardwalk, met with BMA to develop a potential scope of work for next phase. They are drafting a contract for review.
- Woolmarket City Center Addition Completion May 13, 2020, building complete, working through potential drainage issues with the county paving
- Woolmarket Rd. East Drainage NTP is July 27th
- Woolmarket Road Sidewalks Machado Patano contract approved by council on June 23rd
