

**Criminal Intelligence Unit**

T. (228) 435-6159  
 F. (228) 702-3179  
 ciu@biloxi.ms.us



**Police Chief  
 John B. Miller**



170 Porter Avenue  
 Biloxi, Mississippi 39530  
 Office: 228.435.6100  
 Fax: 228.374.1922  
 www.biloxi.ms.us

**DATE:** September 21, 2020

**RE:** Biloxi Police activity for September 14-20, 2020

<b>TOTAL CALLS FOR SERVICE</b>	<b>1,838</b>
<b>TOTAL INCIDENT REPORTS (Case Numbers)</b>	<b>184</b>
<b>TOTAL OFFENSES (Violations/Reports)</b>	<b>254</b>
<b>TOTAL ARRESTS</b>	<b>122</b>

Calls excluded from call type charts were: Checking Building – 117; Extra Patrol – 691; Suspicious Circumstances – 107; Traffic Stops – 80; and Walk & Talk – 133. Additional details may be viewed at <http://www.crimemapping.com/map/ms/biloxi>.






## BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF SEPT. 14-20, 2020

Turned around in route (no fire) / Citizen Complaint/Explosion/ other	1
Fires (Structure & Vehicle)	4
Rescue & Emergency Medical Services	82
COVID 19	0
Medical Involving Homeless Persons	2
Hazardous Conditions	3
Service Call;	18
Good Intent Call:	7
Special Incident Type	0
Fire Alarm Calls; Active, Malfunction	11
<b>Total</b>	<b><u>128</u></b>

### WEEKLY COUNT OF INCIDENT TYPE

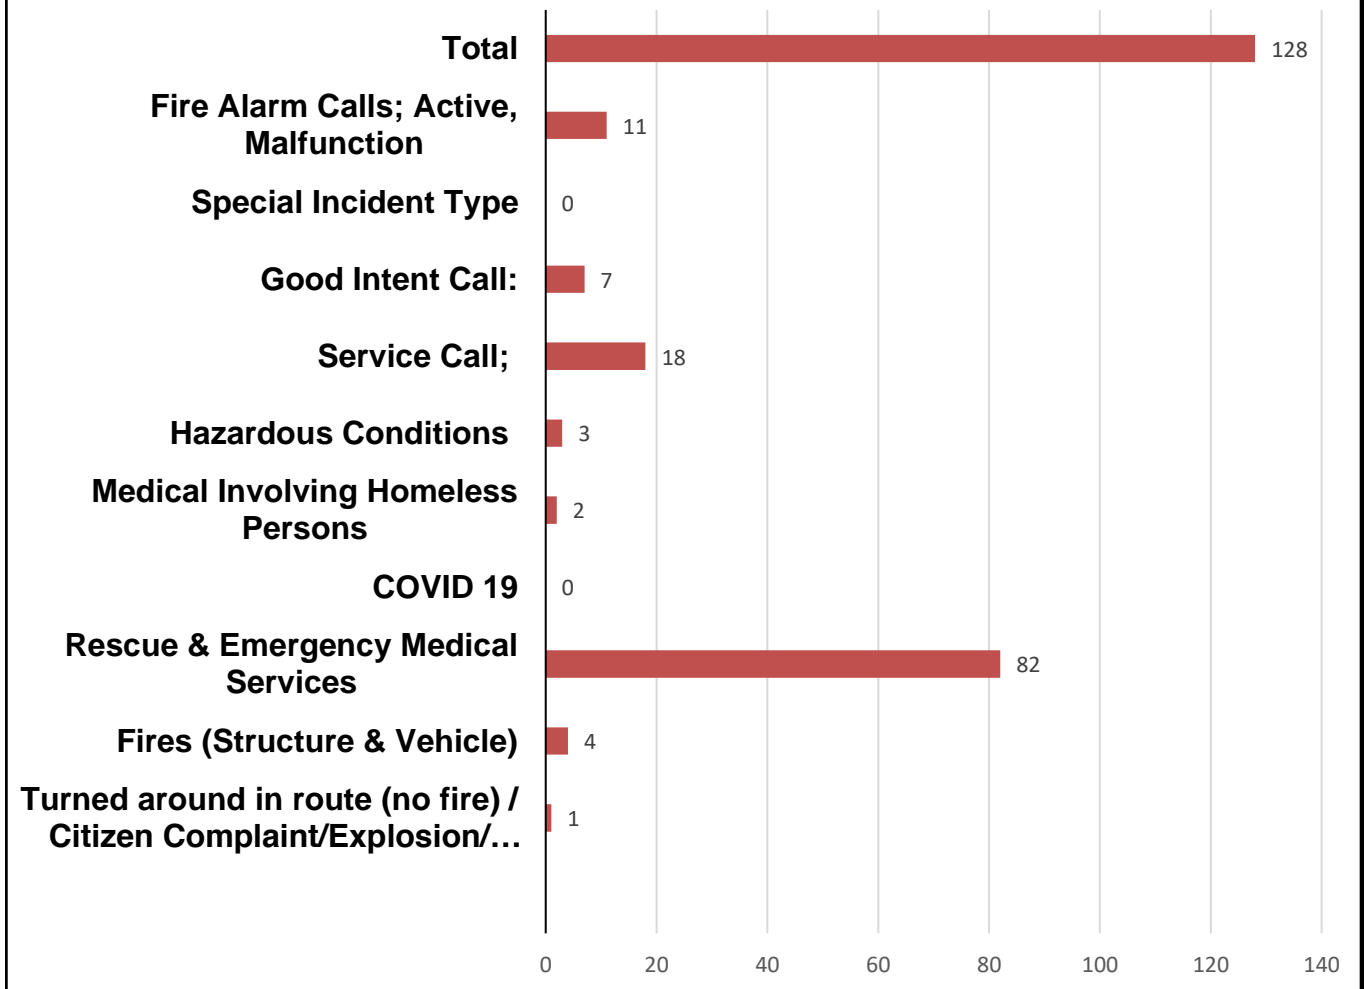



DATE: September 21, 2020

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Sept. 14 - 20, 2020

<i>Building permits issued</i>	77
<i>Construction Valuation of permits issued</i>	\$2,338,500
<i>Building inspections performed</i>	56
<i>Business licenses</i>	0
<i>Renewals</i>	121
<i>Charter Boats</i>	
<b>Peddler's licenses</b>	
<i>Certificates of Occupancy issued</i>	7 (0 was Short-Term Rentals)
<i>Code enforcement cases opened</i>	68
<i>Code enforcement cases resolved</i>	109



**Engineering Department Weekly Update**  
September 21, 2020  
(updates in bold)

**Projects Out to Bid**

- Asphalt Annual Bids (9/30)
- Keesler Gate Outside (9/30)
- Pre-event Debris Monitoring (10/7)

**Projects in the Process of Being Awarded**

- Oakmont St. House Demo (7/29)
- Bayview Ave. Boardwalk (8/5)

**Projects Under Construction**

- Asphalt Annual Contract
- Belle La Vie Parkway
- Canaan Fishing Dock Repairs
- Division St. Houses Ph 3
- Eagle Point Park
- East Biloxi Connector Rd
- Fishing Bridge Lights
- Keesler Gate Inside
- Lorraine Rd. Waterline
- Port Commission Roof
- Saenger Theater
- Sidewalk Annual Contract
- Tanglewood Infrastructure
- West Biloxi Boardwalk
- Woolmarket Rd. East Drainage

**Cspire Fiber Install**

- Phase II Subdivision Installs (still in design)
  - o Eagle Point
  - o Scenic River Dr.
  - o Natures Trail
  - o Rock Creek
  - o Glen Eagle
  - o Cedar Crescent
  - o Eastland Subdivision
  - o Shorecrest Rr.
- Active Projects
  - o 2781 CT Switzer Dr. bore for Gulf Coast Outpatient Surgery Clinic

- Relocate fiber on 4<sup>th</sup> & Maple St. due to conflicts with SXSS storm drain
- Debuys & Pass Sewer Main damage – Received the insurance check, getting on R/R contractors schedule
- 425 Babineaux Pl. – sidewalk needs repair

### **Centerpoint Repairs**

- Repairs
  - 820 Dr. MLK Blvd.

### **Sparklight Projects**

- 231 Rue Petit Bois

### **AT&T Projects**

- Repaving Roy St./Agin Court – received insurance check, working with R/R contractor to get this scheduled
- Small Cell Tower Installs

### **Projects**

- **Atkinson Road Traffic Study** – *Design contracts have been reviewed and are now ready to be approved by City Council, they will be on council agenda before end of September.*
- **Bayview Avenue Boardwalk** – receive bids August 5<sup>th</sup>, apparent low JE Talley \$2.22M; *should be on the Oct. 6<sup>th</sup> council agenda*
- **Belle La Vie Parkway** – Notice to Proceed 2/8/2020; *Completion Nov. 2020*
- Canaan Fishing Dock Improvements (reconstruction) – received DMR & Corps permits, have DE contract, going to hold for now
- **Canaan Fishing Dock Maintenance Repairs** – *waiting on contract documents to have pre-construction meeting and set NTP date*
- Cedar Lake Bridge Repairs (Const. Funding 2021) – Have executed MOA; drafting a letter to DE requesting completion of contract
- Churchill Drainage – residents voted to do nothing for now, but we do need to install some riprap in one area of bank erosion
- Citywide Street Paving
  - Snug Harbor – being done by County
  - McDonnell Avenue – \$40K for just road, additional \$40K to add utilities
  - Sidewalks for Councilman Lawrence
  - Woolmarket Lake Road



- Bay Vista Streets – Bay Vista Dr., Randall Dr. and Hilton Dr. - requested by Councilwoman Newman
  - St. Martha & St. Mary – requested by Councilwoman Newman
  - Laurelwood
  - Ravenwood
  - **Tennis Courts at Circle Park**
- Concrete Annual Contract
    - Base for Fred Haise Statue & Bollards
    - Bollards at East Biloxi Boardwalk Project and around splashpad
    - *Sidewalk at Sunkist and Popp's Ferry Road – need to work up cost*
    - *East Biloxi Boardwalk Nate washout areas need concrete*
  - CSX Crossing Closure Delauney & Nixon – have PO, waiting on contractor to schedule the work
  - Eagle Point Park – work on-going, no additional issues
  - East Biloxi Connector Road (CDBG Funded) – Dorries is now closed, work continuing no outstanding issues
  - Ellzey Place III (Medical Park Drive Extension) – construction complete, waiting on as-builts
  - **Hiller Park Boat Ramp** – *project set up on the 9/22 council meeting; need to schedule a meeting with Seymour to get under contract*
  - Old Hwy 90 Fishing Bridge Lighting repairs – project awarded May 26<sup>th</sup>, contractor is working with light manufacture to ensure fixtures will properly attached to existing poles; we will fix the light poles that are leaning due to Cristobal with this work
  - **Keesler Gate Outside** – All asbestos survey completed; demolition has started; *Phase 1 to Iroquois Street advertises Aug. 13<sup>th</sup> & 20<sup>th</sup>, receives bids Sept. 30<sup>th</sup>*

Offers made

- All offers have been made

*Acquired not ready for demolition*

- *1011 Division St. (Hankins)*
- *987 Division St. (Meltz)*

*Ready for Demolition*

- *1057 Division St. (PJ's)*

*Ready for moving –*

- *956 Division St. (Golden)*

Acquired not requiring demolition

- 1029 Division St
- 1092 Division St.
- 1067 Division St.
- 1310H-02-077.000
- 1310H-02-035.000
- 305 Seal Ave.
- 970 Division St.
- 290 Forrest (only have ROE)
- 1087 Division St.
- 1075 Division St.
- 290 Forrest Ave.

Already demolished/moved

- 301 Seal Ave.
- 962 Division St.
- 974 Division St.
- 978 Division St.
- 997 Division St.
- 1001 Division St.
- 1007 Division St.
- 1015 Division St.
- 1098 Division St.
- 991 Division St.

- Keegan Bayou Restoration – had preliminary plan review meeting on August 21<sup>st</sup>, once the layout is approved they will begin the permitting process
- Keesler Gate Inside – Completion Date 6/2020; roundabout complete except for final asphalt and Larcher Blvd. intersection curb being installed then it will be ready for base asphalt
- Kuhn St. Boat Launch Expansion – Design contract on June 23<sup>rd</sup> council meeting; preliminary layout approved by Mayor 9/7/2020; ready to start applying for permits
- Lorraine Road water line extension – *CB Developers \$587,000; NTP date Oct. 5<sup>th</sup>*
- **Main Street Railroad Crossing Upgrades** (MDOT Funding 2020) –looking for additional \$500K in funding MDOT stated don't worry about funding to just get project to final design stage, *MDOT "office review" meeting August 25<sup>th</sup>*
- Malpass Landing/Watersview – regrading of rear yards is complete as a temporary fix; need to hire a DE to come up with a more permanent solution; using the Repair/Replace contract
- Natatorium Roof Leaks –met with Machado Patano to look at roof March 4<sup>th</sup>; they are going to get up there with water hoses this week to see if they can track down the leak
- Passenger Rail Platform – Design approx. 30% complete, continuing to meet with FRA, SRC and Amtrak on the design
- Point Cadet Shoreline – permits submitted to DMR and Corps, expecting a minimum of 6 months to get permits approved
- Point Cadet Marina West – submitted revised drawing and cost estimate for grant agreement
- Point Cadet Traffic Analysis – design contract has been sent to MDOT for review
- **Popps Ferry Extension #913** – Coliseum has the draft MOU for Board approval; 33 parcels to acquire; all surveys; appraisals, and review appraisals complete; *House demolition contract receives bids on 7/29; under review*

Negotiation

- 2400 Beach Blvd. (Coliseum)
- 128 Oakmont (Coliseum)
- 161 Oakmont (Coliseum)
- 173 Oakmont (Shows)
- 0 Hwy 90 (Coliseum)
- 0 Briarfield (Bhakta)
- 0 Briarfield (Coliseum)
- 0 Pass Rd. (Salloum)
- 0 Pass Rd. (Hardy Court)
- 2395 Pass Rd. (NM Markup)
- 2395 Pass Rd. (Burger King)
- 2393 Pass Rd. (Exxon)
- 0 Pass Rd. (Biloxi Management)
- 2401 Pass Rd. (Stewart Family)
- 2404 Pass Rd. (Shoppes @ PF West)
- 2423 Pass Rd. (Take 5)
- 0 Covenant Square (Hardy Court)
- 2415 Pass Rd. (Hardy Court)
- 2368 Pass Rd. (PF MS Dev Co)

Courts

- 141 Oakmont (Maddox)
- 145 Oakmont (Maddox)
- 2416 Beach Blvd. (Spencer)

Ready for Demolition

- 135 Oakmont (Olin)
- 164 Oakmont (Patton)
- 165 Oakmont (Newton)

Already demolished

- 130 Oakmont (Serignet)

Purchased

- 129 Oakmont (Trinh)
- 131 Oakmont (Trinh)
- 134 Oakmont (Stacy)
- 137 Oakmont (Stacy)
- 149 Oakmont (Summers)
- 168 Oakmont (Best)
- 169 Oakmont (Coliseum)

- Popp's Ferry Bridge & Approaches – met with Sharen Willis March 4<sup>th</sup> to discuss how to move into the ROW phase; BMA 90% complete with ROW plans, anticipate completion August 14, 2020
- Port Commission Roof Repairs – working on-going
- **Repair/Replace Contract**
  - Churchhill Ditch – 50% plans complete; emergency repair complete;
  - **Roy Street** – complete
  - *Debuys & Pass – Cspire Damages – scheduling with contractor start date 9/14 now pushed back due to TS Sally*
  - Malpass/Watersview Drainage – scheduling the survey
  - Lorraine Road (Bruce Wilson)
  - Seal @ Howard Sewer Repair
  - Scenic River Drainage
  - Wash Fayard Rd. Culverts
  - IP Parking Lot
  - McDonnell Ave. extension road base only
  - Magnolia Street driveways and curb cuts for Infrastructure
  - Cambridge Drive Drainage
  - Lorraine Road waterline



- 229 Dewey Circle inlet
- Tara Lane Drainage (\$200,000)
- Saenger Theater Phase I & II Fly Tower & Exterior – Blackline is working up a revised proposal for the brick repair & repointing for a September approval; there are several leaks in the north and south auditorium walls which are not covered in this current contract;
- Saenger Theater Interior Condition Assessment – need to schedule this walkthrough
- Sediment Removal Phase III – hydrographic surveys complete, working on the permit applications, the sites that have SAV, Seymour is trying to work with DMR on a way to mitigate, Seymour updated council on Aug. 25<sup>th</sup>
  - Hiller Park Pond
  - Cedar Lake Rd. Canal
  - Cedar Lake Broadus
  - Kennedy Ln (SAV)
  - Savannah Estates (DMR stated not eligible)
  - Eagle Point Pin Oak (SAV)
  - Linda Dr. (SAV)
  - Beau Chene (DMR stated not eligible)
- Sediment Maintenance Plan – Have 100% draft for review
- **Small Craft to Oak St Boardwalk** – *markups will be ready in about two weeks then project is ready to advertise for bids*
- Snyder Center Chiller Replacement – contract awarded, going to be 8 weeks until chiller gets here
- Snyder Pool Repairs – awarded to Ewing Pool
- Tanglewood Infrastructure – received bids Aug. 19<sup>th</sup>, bids were up by about \$100K; currently reviewing bid tab
- Visitors Center Repairs – working on scope of work to develop plans/specs in house
- Ward 4 Paving
  - **Sunkist Country Club Sidewalks** – *scheduling with annual concrete contractor*
- Watersview Drainage Cleaning – Council Glavan has requested assistance from Harrison County and we have submitted application for wetlands permit; received email from Corps that no permit was needed, DMR is issuing a waiver; County has agreed to haul off debris if City removes it from the wetlands

- West Biloxi Boardwalk Phase 1B – NTP April 6, 2020/Comp Sept. 27, 2020, work underway no issues; work on-going, no significant issues
- West Biloxi Boardwalk Phase 2 – east of existing boardwalk, met with BMA to develop a potential scope of work for next phase. They are drafting a contract for review.
- Woolmarket City Center Addition – Completion May 13, 2020, county was supposed to start last week, will check on status; 8-17-20 additional issues came up we got those resolved with the county and they are supposed to be back working
- **Woolmarket Rd. East Drainage** – July 27<sup>th</sup> met with Billy Broadus onsite Thursday and will be extending pipe to past his driveway, that change order is on this council agenda
- Woolmarket Road Sidewalks – Machado Patano contract approved by council on June 23<sup>rd</sup> design work on-going



**Date:** *Monday, Sept. 21, 2020*  
**Public Works Activity Report for**

**Sept. 14 -20, 2020**

After the threat of Hurricane Sally passed, our Streets and Drainage crews switched gears and began the task of Auction Prep. Loading and moving the materials from several city departments to the auction site was a time consuming and arduous task. Upon completion of this task, crews returned to their territories and continued with their normal list of duties.

We would like to take this time to remind everyone preparations for Cruisin' the Coast will begin very soon. Once again, Streets and Drainage crews will be placing traffic cones, barricades, and other traffic control devices to assist in the event. Please be mindful of crews working on or near roadways and please slow down when passing these crews.

**Did you know:** Working in or near roadways are one of the most dangerous jobs in the United State? Please help us not be a statistic. Slow down around work zones. It only takes a second.

**Work orders closed for week - 144**

**FY 2020 - Work orders closed to date - 9351**

WO CLOSED BY SHOP LAST WEEK

