

Criminal Intelligence Unit

T. (228) 435-6159
 F. (228) 702-3179
 ciu@biloxi.ms.us



**Police Chief
 John B. Miller**



170 Porter Avenue
 Biloxi, Mississippi 39530
 Office: 228.435.6100
 Fax: 228.374.1922
 www.biloxi.ms.us

DATE: June 28, 2021

RE: Biloxi Police activity for June 21-27, 2021

TOTAL CALLS FOR SERVICE	2,111
TOTAL INCIDENT REPORTS (Case Numbers)	244
TOTAL OFFENSES (Violations/Reports)	320
TOTAL ARRESTS	167

Calls excluded from call type charts were: Checking Building – 32; Extra Patrol – 381; Suspicious Circumstances – 94; Traffic Stops – 336; and Walk & Talk – 75. Additional details may be viewed at <http://www.crimemapping.com/map/ms/biloxi>.

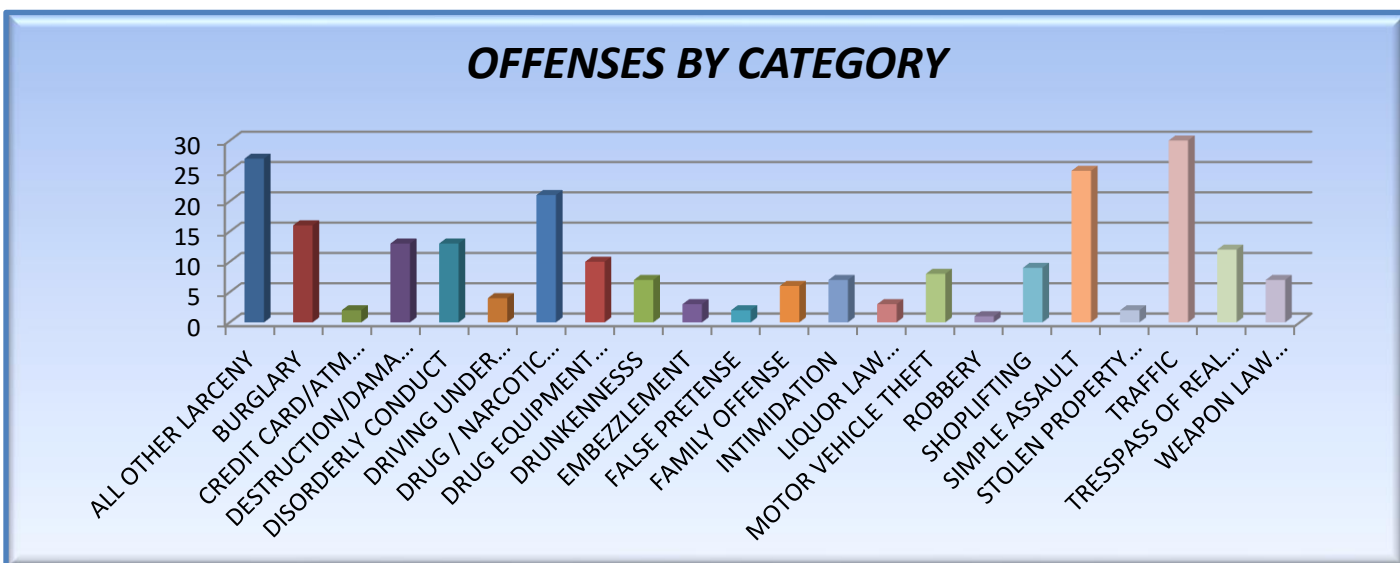




BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF JUNE 21 - 27, 2021

1 - Fires (Structure & Vehicle)	2
2 - Rupture/Explosion	0
3 - Emergency Medical Services/Rescue	116
4 - Hazardous Conditions	5
5 - Service Calls	17
6 - Good Intent	9
7 - Fire Alarm Calls; Active, Malfunction	22
8 - Weather/Natural Disaster	0
9 - Special Incident Type	0
Total	<u>171</u>

WEEKLY COUNT OF INCIDENT TYPE

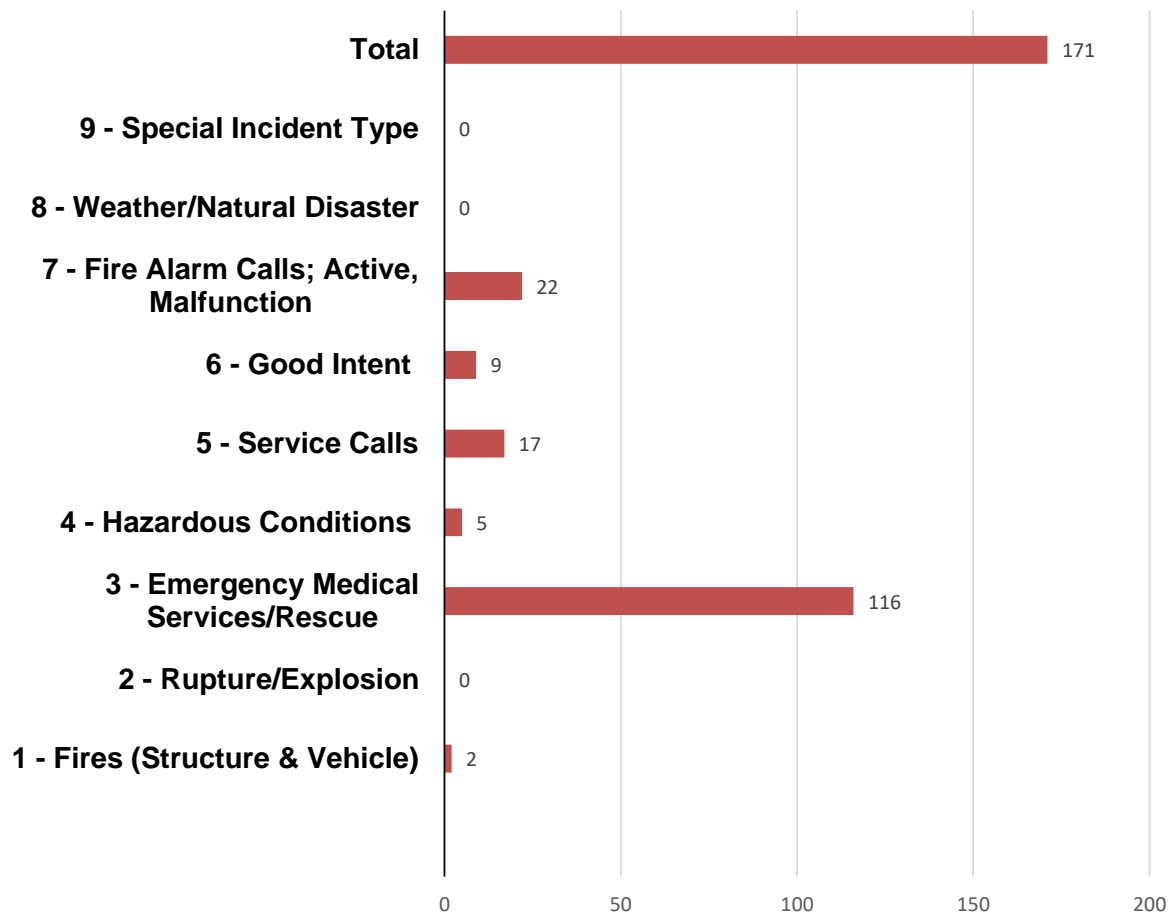



DATE: *June 28, 2021*

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Jun 21 - 27, 2021

Building permits issued	<i>90</i>
Construction Valuation of permits issued	<i>\$504,600</i>
Building inspections performed	<i>61</i>
Business licenses Renewals Charter Boats Peddler's licenses	<i>6</i>
Certificates of Occupancy issued	<i>7(1 was Short-Term Rentals)</i>
Code enforcement cases opened	<i>121</i>
Code enforcement cases resolved	<i>44</i>



**Engineering Department Weekly Update
June 28, 2021**

Atkinson Road Traffic Study	Report Complete
Bay Vista Water Well	Preparing RFP
Bayview Avenue Walkway	Work going well -
Canaan Fishing Dock Improvements	On hold for funding
Cedar Lake Bridge Repairs	Kick off meeting with MDOT pending
Citywide Street Paving	
Concrete Annual Contract	Concrete annual contract expired – being rebid. Pavillion at Eagle Point Park is next project
Eagle Point Park	Basketball court and pickleball court completed.
CSX Crossings	Nixon and Dorries crossings closed; Delauney and Holley closings will be scheduled next
Dredging City Wide	No activity at this time. Permit mitigation issues with Subsurface Aquatic Vegetation being worked – mitigation plan to be submitted to MDMR
East Biloxi Connector Road	Completed
Hiller Park Boat Ramp	Preliminary design stage, Permit received
Old Hwy 90 Fishing Bridge lights	electrical panel elevated. Project complete
Keesler Gate Inside	Lighting repairs due to Hurricane Zeta. Nearing closeout.
Keesler Gate Outside	Completing box culverts on Division and Benachi;. Utility duct bank under construction February 2022 completion
Keegan’s Bayou Restoration	GOMESA Project Submitted to DMR. Permits being submitted.
Kuhn Street Boat Ramp and Parking	Working preliminary design and permits
Lighthouse Pier – Hurricane Zeta Damage	Received Statements of Qualifications on April 14. Building back as hazard mitigation effort.
Lorraine Road Water Line	Complete – closing project. Lorraine water line phase 2 being reviewed by Dept of Health.

Main Street Railroad Crossing	Design being completed – construction funds pending; Requesting additional MDOT funding.
Malpass Landing	Ditch cleanup done.
Passenger Train Rail Platform	AMTRACK taking over design and construction of passenger platform
Point Cadet Shoreline Restoration	GOMESA project submitted; On hold pending funding
Point Cadet Improvements (West)	Restore Act Funding was approved. Continuing with design work and completing US Dept of Treasury documents
Point Cadet Traffic Study	Work has begun.
Popp's Ferry Extension	Right of Way acquisition nearly complete. Design being completed; Pending Construction Funding
Popp's Ferry Bridge	Design Phase I being completed; Contract for Right of Way property acquisition being developed
Repair Replace Contract	Hampton Lane drainage repair completed as well as Dundewood. Other storm drainage task orders in the que: <ul style="list-style-type: none"> • Trentwood • Brandon James • Hartness CT
Saenger Theatre Restoration	Fly Tower, Roof and HVAC complete. Exterior brick sealing near complete, selective interior demolition underway, developing scope of exterior work to west (front) side
Shriners Road Utility Extension (The "Preserve")	Survey underway, design to be complete and bid ready by mid to late July
Walkway - Small Craft Harbor to Oak Street	Work paused due to design changes.. Width of walkway decreased to 10 feet wide Restart shortly
Visitor Center Repairs	Request for Proposals for roof replacement on the street- bids open July 7 th . Working scope for other repairs
Woolmarket Drainage	Work complete.
Woolmarket Sidewalks	Sidewalk extended to Shriners Blvd. MDOT reviewing increased scope
ZETA (Hurricane Damage Repairs)	Currently working repair estimates on many city facilities. Many smaller jobs underway including five elevator repairs, MGM Park, Bond House roof and others.
