

Criminal Intelligence Unit

T. (228) 435-6159
 F. (228) 702-3179
 ciu@biloxi.ms.us



**Police Chief
 John B. Miller**



170 Porter Avenue
 Biloxi, Mississippi 39530
 Office: 228.435.6100
 Fax: 228.374.1922
 www.biloxi.ms.us

DATE: August 30, 2021

RE: Biloxi Police activity for August 23-29, 2021

TOTAL CALLS FOR SERVICE	1,515
TOTAL INCIDENT REPORTS (Case Numbers)	151
TOTAL OFFENSES (Violations/Reports)	192
TOTAL ARRESTS	114

Calls excluded from call type charts were: Checking Building – 30; Extra Patrol – 382; Suspicious Circumstances – 83; Traffic Stops – 133; and Walk & Talk – 55. Additional details may be viewed at <http://www.crimemapping.com/map/ms/biloxi>.

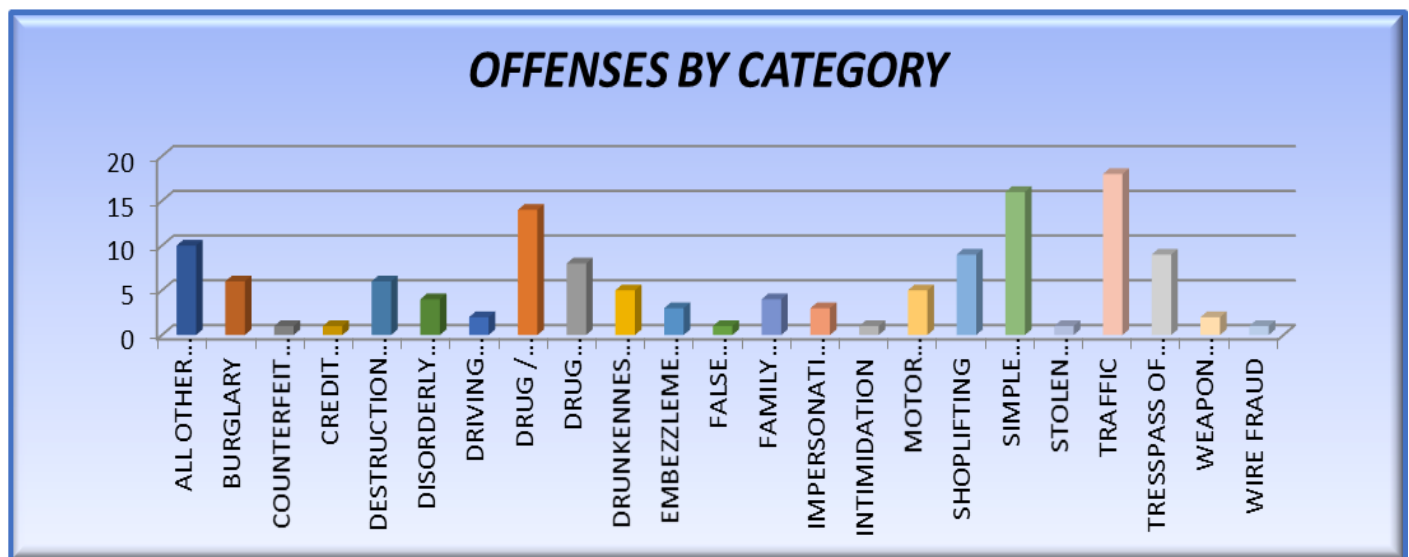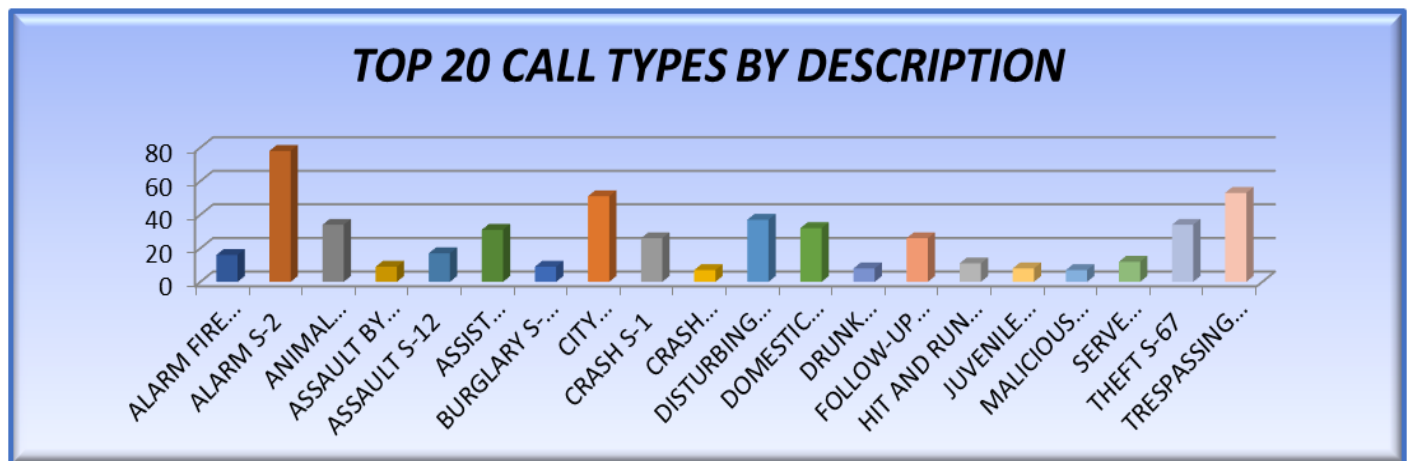




BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF AUG. 23 - AUG. 29, 2021

1 - Fires (Structure & Vehicle)	3
2 - Rupture/Explosion	0
3 - Emergency Medical Services/Rescue	120
4 - Hazardous Conditions	4
5 - Service Calls	16
6 - Good Intent	16
7 - Fire Alarm Calls; Active, Malfunction	19
8 - Weather/Natural Disaster	0
9 - Special Incident Type	0
Total	<u>178</u>

WEEKLY COUNT OF INCIDENT TYPE

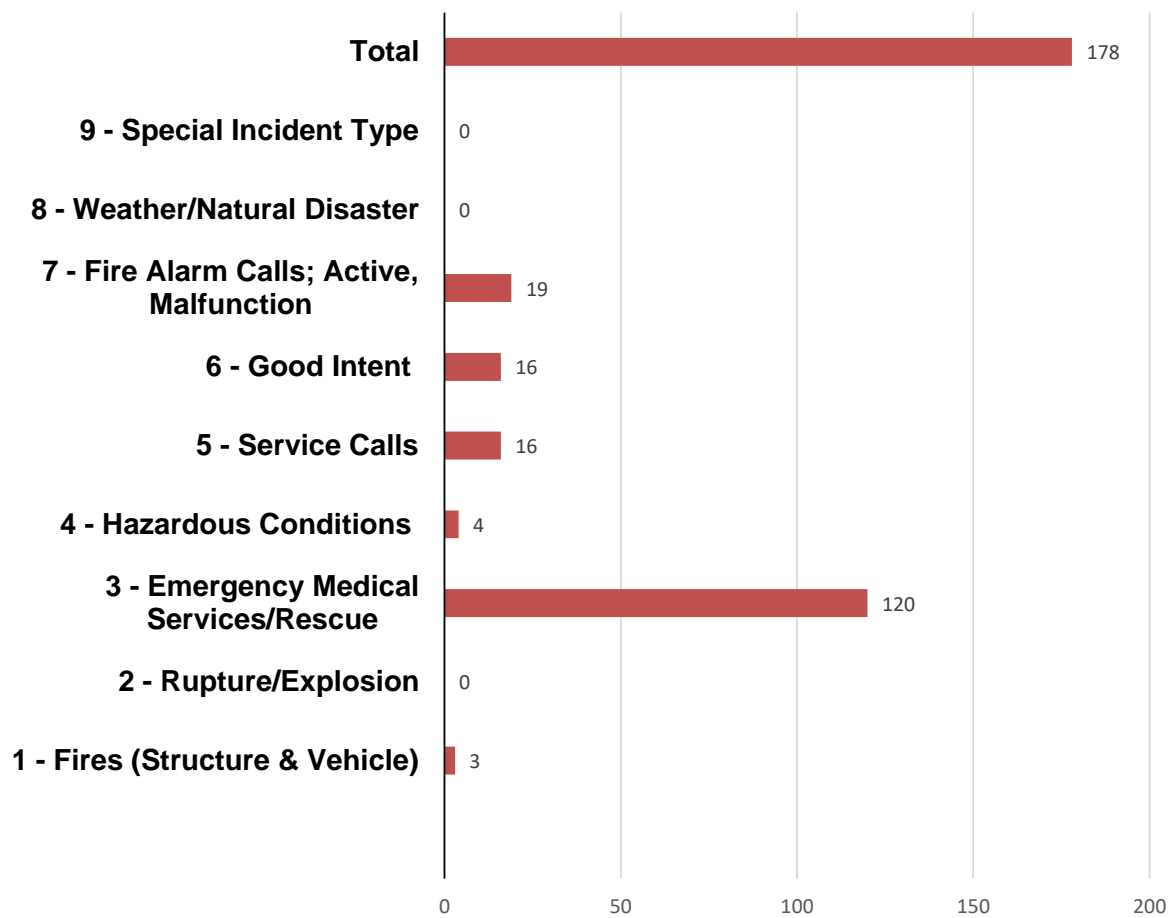



DATE: *August 30, 2021*

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Aug 23 - 29, 2021

Building permits issued	<i>64</i>
Construction Valuation of permits issued	<i>\$789,000</i>
Building inspections performed	<i>64</i>
Business licenses	<i>3</i>
Renewals	<i>250</i>
Charter Boats	
Peddler's licenses	
Certificates of Occupancy issued	<i>7 (0 were Short-Term Rentals)</i>
Code enforcement cases opened	<i>86</i>
Code enforcement cases resolved	<i>59</i>



Engineering Department Weekly Update
August 30, 2021

Bay Vista Water Well	Design Engineer (BMA) has submitted permit to State and notice of intent is being printed
Bayview Avenue Walkway	Work is on schedule
Canaan Fishing Dock Improvements	On hold for GOMESA funding
Cedar Lake Bridge Repairs	Have sent application for MS Emergency Road and Bridge Repair Program.
Citywide Street Paving	Lawrence Street done. Next is Tara Lane, McDonnel and Camp 4 Jacks Road
Concrete Annual Contract	Concrete annual contract has been rebid –Plan to award September 8th. Job backlog includes Eagle Park pavilion, Fire Station 5 concrete apron and gutter pan on parallel roadway east biloxi
Eagle Point Park	Basketball court and pickleball court completed. Awaiting concrete contract rebid to place pavilion slab. Adding some fill dirt and sod for low spot. Ordering playground
CSX Crossings	Nixon and Dorries crossings closed; Delauney and Holley closings will be scheduled next
Dredging City Wide	No activity at this time. Permit mitigation issues with Subsurface Aquatic Vegetation being worked. Will do one test case on Linda Drive to see how mitigation works. Need to designate mitigation site
Hiller Park Boat Ramp	Permit received .
Keesler Gate Inside	Project closed out and assets transferred
Keesler Gate Outside	Completing box culverts on Division and Benachi;. Utility duct bank done. MS power will now be putting wire in the duct bank in preparation to transfer power underground and remove poles
Keegan’s Bayou Restoration	GOMESA Project Submitted to DMR. Permits being requested
Kuhn Street Boat Ramp and Parking	Phase 1 (boat ramp) working preliminary design and permits. Funding for Phase 2 (parking) being requested from Tidelands fund. Removal of marine vegetation being mitigated

Lighthouse Pier – Hurricane Zeta Damage	Building back as hazard mitigation effort. . working cost benefit analysis to build back better. Contract with Design Firm approved.
Lorraine Road Water Line	First phase complete. Lorraine water line phase 2 design complete and being reviewed by Dept of Health. Running water (hydraulic) model to ensure adequate pressure
Main Street Railroad Crossing	Design being completed – construction funds pending GRPC has committed additional federal funding. Coordinating with CSX on their support for the project
Passenger Train Rail Platform	AMTRACK taking over design and construction of passenger platform
Point Cadet Living Shoreline	Tidelands project awarded \$800,000. MOU with DMR being executed. Kick off meeting held with Design Engineer (BMA)
Point Cadet Improvements (West)	Restore Act Funding approved. Subgrant agreement with MDEQ executed. Design 60% approved – 100% design and bid in October with work to begin early CY22
Point Cadet Traffic Study	Work has begun. Traffic counts being done
Popp's Ferry Extension	Right of Way acquisition nearly complete. Design being completed; Pending Construction Funding. Have submitted” RAISE grant” to US DOT and also request to Gulf Coast Restoration Fund
Popp's Ferry Bridge	Design Phase I being completed; Contract for Right of Way property acquisition being developed. Working approach roadway alignment being reviewed by MDOT
Repair Replace Contract	Hampton Lane, Dundewood, Harkness and Victory Lane task orders complete. Brandon James task also completed Atkinson/Popps Ferry completed, Tara Lane pending
Saenger Theatre Restoration	Fly Tower, Roof and HVAC complete. Exterior brick sealing near complete, selective interior demolition complete, Have developed scope of exterior work to west (front) side and change order 10 executed. Requested Gulf Coast Restoration funding for interior work.
Shriners Road Utility Extension (The “Preserve”)	Survey complete. Design complete. Have submitted to Health Department for approval. Bid ready by early fall.
Walkway - Small Craft Harbor to Oak Street	Work paused due to design changes. Width of walkway decreased to 9.5 feet wide Construction Directive issued to restart work.

Visitor Center Repairs	Request for Proposals for roof replacement on the street- bids opened. Awarded roof work to Mandel. Working scope for other repairs
Woolmarket Drainage	Work complete. Closing project. Working on drainage easement between Shriners and Woolmarket Road
Woolmarket Sidewalks	Sidewalk extended to Shriners Blvd. Final alignment to MDOT
ZETA (Hurricane Damage Repairs)	Currently working repair estimates on many city facilities. Many smaller jobs underway including five elevator repairs, MGM Park, Bond House roof and Commercial Harbor
