

Criminal Intelligence Unit

T. (228) 435-6159
 F. (228) 702-3179
 ciu@biloxi.ms.us



**Police Chief
 John B. Miller**



170 Porter Avenue
 Biloxi, Mississippi 39530
 Office: 228.435.6100
 Fax: 228.374.1922
 www.biloxi.ms.us

DATE: August 16, 2021

RE: Biloxi Police Activity for August 9-15, 2021

TOTAL CALLS FOR SERVICE	1,544
TOTAL INCIDENT REPORTS (Case Numbers)	210
TOTAL OFFENSES (Violations/Reports)	287
TOTAL ARRESTS	130

Calls excluded from call type charts were: Checking Building – 36; Extra Patrol – 360; Suspicious Circumstances – 110; Traffic Stops – 88; and Walk & Talk – 61. Additional details may be viewed at <http://www.crimemapping.com/map/ms/biloxi>.

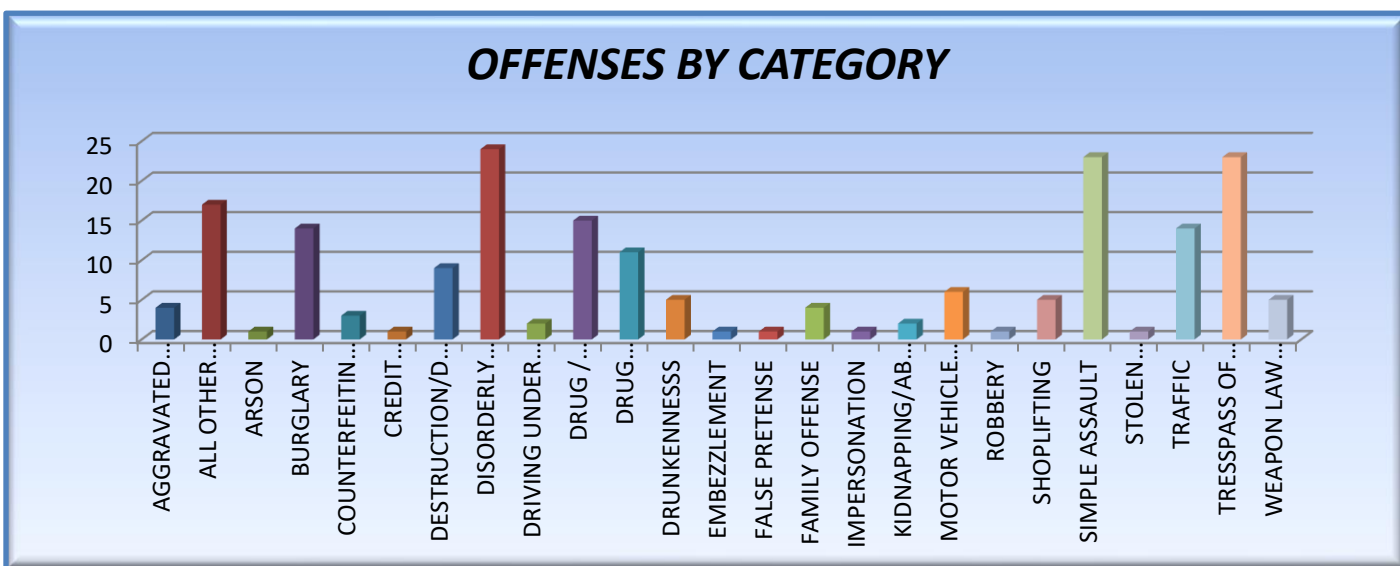




BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF AUG. 9 - AUG. 15, 2021

1 - Fires (Structure & Vehicle)	4
2 - Rupture/Explosion	0
3 - Emergency Medical Services/Rescue	136
4 - Hazardous Conditions	4
5 - Service Calls	17
6 - Good Intent	6
7 - Fire Alarm Calls; Active, Malfunction	7
8 - Weather/Natural Disaster	0
9 - Special Incident Type	0
Total	<u>174</u>

WEEKLY COUNT OF INCIDENT TYPE

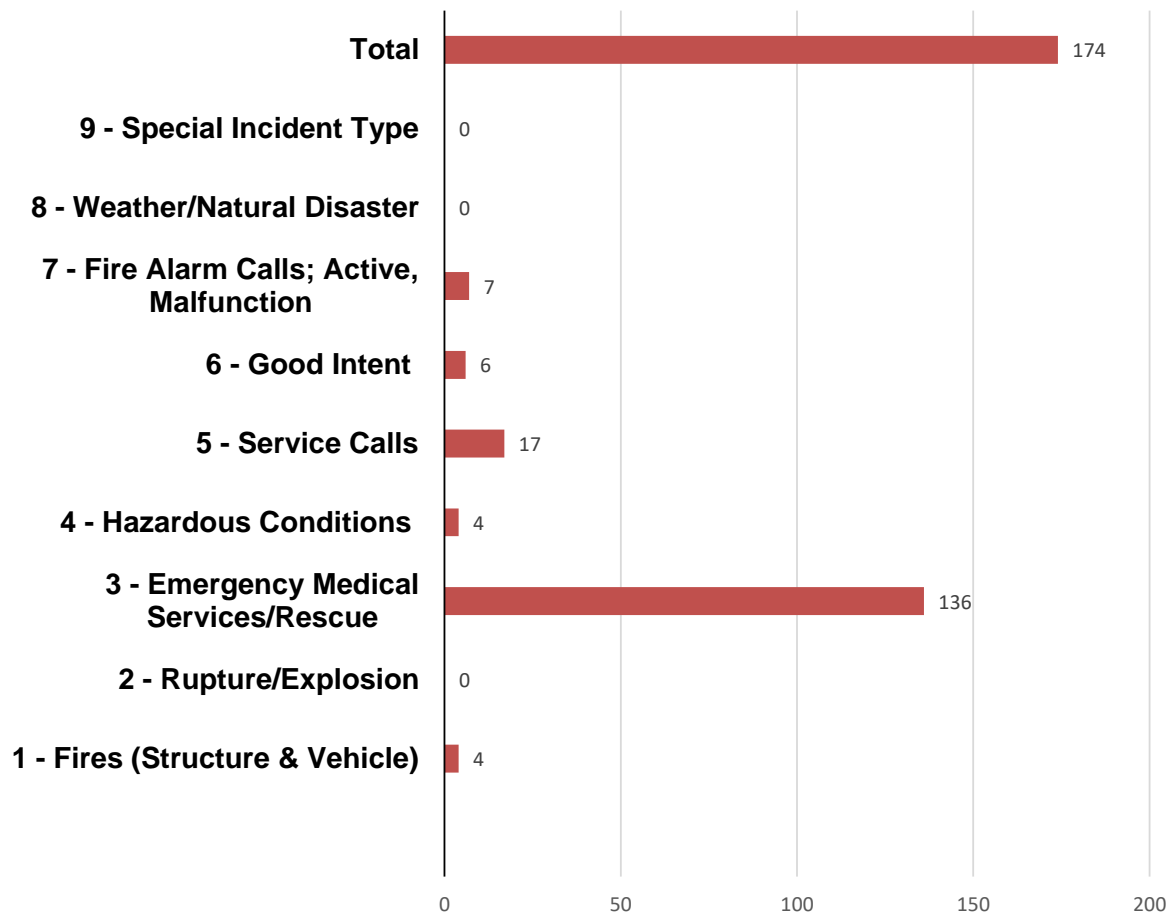



DATE: August 16, 2021

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Aug 7 - 15, 2021

Building permits issued	115
Construction Valuation of permits issued	\$1,713,500
Building inspections performed	95
Business licenses	4
Renewals	1
Charter Boats	
Peddler's licenses	
Certificates of Occupancy issued	11 (1 was Short-Term Rentals)
Code enforcement cases opened	65
Code enforcement cases resolved	108



**Engineering Department Weekly Update
August 16, 2021**

Bay Vista Water Well	Design Engineer (BMA) on site doing assessment
Bayview Avenue Walkway	Work is on schedule
Canaan Fishing Dock Improvements	On hold for GOMESA funding
Cedar Lake Bridge Repairs	Have sent application for MS Emergency Road and Bridge Repair Program.
Citywide Street Paving	Lawrence Street done. Next is Tara Lane, McDonnel and Camp 4 Jacks Road
Concrete Annual Contract	Concrete annual contract has been rebid –Plan to award September. 8th. Job backlog includes Eagle Park pavilion, Fire Station 5 concrete apron and gutter pan on parallel roadway east biloxi
Eagle Point Park	Basketball court and pickleball court completed. Awaiting concrete contract rebid to place pavilion slab. Adding some fill dirt and sod for low spots
CSX Crossings	Nixon and Dorries crossings closed; Delauney and Holley closings will be scheduled next
Dredging City Wide	No activity at this time. Permit mitigation issues with Subsurface Aquatic Vegetation being worked. Will do one test case on Linda Drive to see how mitigation works.
Hiller Park Boat Ramp	Preliminary design stage, Permit received
Keesler Gate Inside	Project being closed out and assets transferred
Keesler Gate Outside	Completing box culverts on Division and Benachi;. Utility duct bank nearly done.
Keegan’s Bayou Restoration	GOMESA Project Submitted to DMR. Permits being requested
Kuhn Street Boat Ramp and Parking	Phase 1 (boat ramp) working preliminary design and permits. Funding for Phase 2 (parking) being requested from Tidelands fund. Removal of marine vegetation being mitigated
Lighthouse Pier – Hurricane Zeta Damage	Building back as hazard mitigation effort. Contract with Design Firm approved.

Lorraine Road Water Line	First phase complete. Lorraine water line phase 2 design complete and being reviewed by Dept of Health. Running water (hydraulic) model to ensure adequate pressure
Main Street Railroad Crossing	Design being completed – construction funds pending; Requesting additional MDOT funding.
Passenger Train Rail Platform	AMTRACK taking over design and construction of passenger platform
Point Cadet Living Shoreline	Tidelands project awarded \$800,000. MOU with DMR being executed. Kick off meeting held with Design Engineer (BMA)
Point Cadet Improvements (West)	Restore Act Funding approved. Subgrant agreement with MDEQ executed.. Design 60% approved – 100% design and bid in October with work to begin early CY22
Point Cadet Traffic Study	Work has begun. Traffic counts being done
Popp's Ferry Extension	Right of Way acquisition nearly complete. Design being completed; Pending Construction Funding. Have submitted” RAISE grant” to US DOT and also request to Gulf Coast Restoration Fund
Popp's Ferry Bridge	Design Phase I being completed; Contract for Right of Way property acquisition being developed. Working approach roadway alignment being reviewed by MDOT
Repair Replace Contract	Hampton Lane, Dundewood, Harkness and Victory Lane task orders complete. Brandon James task underway. Atkinson/Popps Ferry and Tara Lane pending
Saenger Theatre Restoration	Fly Tower, Roof and HVAC complete. Exterior brick sealing near complete, selective interior demolition complete, Have developed scope of exterior work to west (front) side and will do change order 10 on August 17th
Shriners Road Utility Extension (The “Preserve”)	Survey complete. Design complete. Have submitted to Health Department for approval. Bid ready by early fall.
Walkway - Small Craft Harbor to Oak Street	Work paused due to design changes. Width of walkway decreased to 9.5 feet wide Construction Directive issued to restart work.
Visitor Center Repairs	Request for Proposals for roof replacement on the street- bids opened. Awarded roof work to Mandel. Working scope for other repairs
Woolmarket Drainage	Work complete. Closing project. Working on drainage easement between Shriners and Woolmarket Road

Woolmarket Sidewalks	Sidewalk extended to Shriners Blvd. Final alignment to MDOT
ZETA (Hurricane Damage Repairs)	Currently working repair estimates on many city facilities. Many smaller jobs underway including five elevator repairs, MGM Park, Bond House roof and others.
