




**BIŁOXI FIRE DEPARTMENT
INCIDENT SUMMARY REPORT FOR
THE WEEK OF Oct 31 - Nov 06, 2022**

1 - Fires (Structure & Vehicle)	6
2 - Rupture/Explosion	0
3 - Emergency Medical Services/Rescue	101
4 - Hazardous Conditions	0
5 - Service Calls	17
6 - Good Intent	12
7 - Fire Alarm Calls; Active, Malfunction	10
8 - Weather/Natural Disaster	0
9 - Special Incident Type	2
Total	148

WEEKLY COUNT OF INCIDENT TYPE



Criminal Intelligence Unit

T. (228) 435-6159

F. (228) 702-3179

ciu@biloxi.ms.us

**Police Chief****John B. Miller**170 Porter Avenue
Biloxi, Mississippi 39530

Office: 228.435.6100

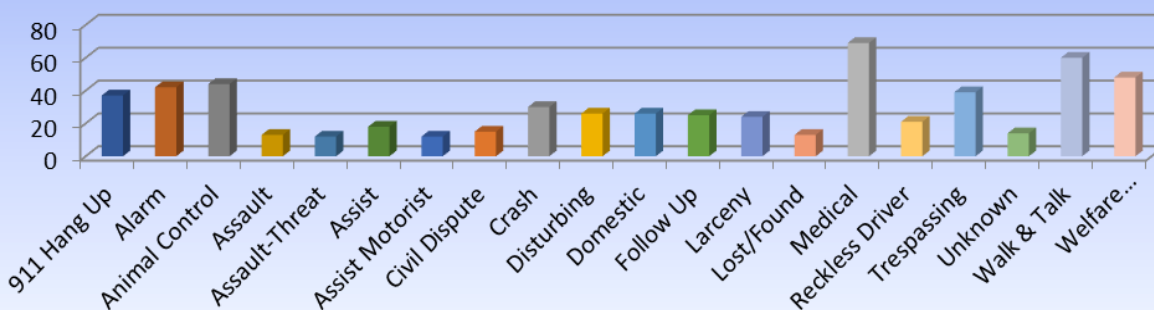

Fax: 228.374.1922

www.biloxi.ms.us

DATE: November 7, 2022**RE:** Biloxi Police activity for October 31 – 6 November, 2022

TOTAL CALLS FOR SERVICE	1,525
TOTAL INCIDENT REPORTS	130
TOTAL OFFENSES (Violations/Reports)	152
TOTAL ARRESTS	62

Calls excluded from call type charts were: Extra Patrol – 362; Suspicious Circumstances – 74; Traffic Stops – 140; and Walk & Talk – 60. The Biloxi Police Crime Map may be viewed at <https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f>.

TOP 20 CALL TYPES BY NATURE**OFFENSES BY CATEGORY**



DATE: *November 7, 2022*

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Oct 31 – Nov 6, 2022

Building permits issued	65
Construction Valuation of permits issued	\$2,807,500
Building inspections performed	109
Business licenses	5
Renewals	18
Charter Boats	
Peddler's licenses	
Certificates of Occupancy issued	3 (0 were Short-Term Rentals)
Code enforcement cases opened	50
Code enforcement cases resolved	39

Engineering Department

Christy LeBatard, P.E.
Director of Engineering



Engineering Department Weekly Update November 7, 2022 (updates in red)

214-A Delauney Street
P. O. Box 429
Biloxi, Mississippi 39533
Office: 228.435.6265
Fax: 228.435.6179
www.biloxi.ms.us

Projects Out to Bid

Projects in the Process of Being Awarded

- Shriners Blvd. Water/Sewer Extension (10/12)

Projects Under Construction

- Causeway Park Floating Docks
- Bluff Subdivision Concrete Repairs
- Hiller Park Boat Ramp
- Keesler Gate Outside
- Point Cadet Marina West
- Franks Drive Storm Drain
- Saenger Theater Restoration
- Visitors Center Repairs

Fiber Installs

Centerpoint Repairs

Sparklight Projects

AT&T Projects

Projects

- Bay Vista Water Well (CL) - Received permit, design complete, ready to bid pending ARPA funding; tree removal by Public Works needed for access to site
- Causeway Parking Floating docks – project awarded to JE Borries, **pre-construction meeting held, NTP pending delivery of materials**
- Canaan Fishing Dock Improvements (reconstruction) (ML) – received DMR & Corps permits, on how for GOMESA funding
- Cedar Lake Bridge Repairs (CL) – Plan to submit for MDOT Emergency Road & Bridge Repair Grant and BRIC Grant for M&E and structural repairs

- Citywide Street Paving (DN) (Landshapers)
 - Laurelwood
 - Ravenwood
 - Croesus
 - Esters – Caillavet to Reynoir
 -
- Concrete Annual Contract (DN) (ADS)
 - Concrete panels in The Bluff Subdivision – **one side of street panels have been demo'd, plan to pour concrete 11/7**
- CSX Crossings – Nixon and Dorries Closed: Delauney and Iroquois next
- Dredging – Tidelands grant for Parkers Creek boat ramp dredging was received. Permit mitigation issues with Subsurface Aquatic Vegetation being worked. Permit received for maintenance dredging in Point Cadet Marina
- Eagle Point Park (MH) – need Public Works to muck out area of parking not complete, and then pave, rest of project in Warranty period
- East Biloxi Connector Road Porter to Hopkins (CL) (CDBG Funded) – **appraisals have been started, expect to start making offers in December**
- Hiller Park Boat Ramp (GP) – Completion date December 1, 2022, **paving is complete**
- Keesler Gate Outside (MH) – Completion date November 2022, expecting CO for MDOT electrical to traffic signal at exit ramp, expecting CO for water leave at a valve, **paving contractor is expected to mobilize this week, light pole delivery date is expected 11/11, bases have been built and wire pulled**
- Lighthouse Pier (GP) – design efforts continue
- Keegan Bayou Restoration (GP) – Permits being requested, GOMESA project submitted to DMR, also in the Restore Act Portal
- Kuhn St. Boat Launch Expansion (GP) – Conceptual started by Pickering, vegetation removal started, project scope revised to match tidelands funding grants
- Lorraine Road Water Line Extension Ph 2 (CL) – Design complete, ready to bid, ARPA application for funding submitted, water/sewer funding is available if not selected for ARPA
- Main Street Railroad Crossing Upgrades (CL) – Award to Gulf Breeze approved at 9/20 Council Meeting, MDOT authorization to award process is underway

- McDonnell Road Extension (DN) – Completed design of roadway and extension of utilities \$220K
- Oak Street Pier (South) (DN) – Cypress presented conceptual plans, working on a design contract
- Pickleball Restroom (GP) – design complete ready to prepare bid package
- Point Cadet Development #1092 (GP) – Machado Patano is working concept
- Point Cadet Living Shoreline (GP)– BMA started design, topo complete, Tidelands/National Fish and Wildlife Funding
- Point Cadet Marina West (MH) – AnderCorp NTP 10/24, 240 day contract, **construction laydown area fencing will start this week, fence has been delivered, job site trailer also expected this week, lead time for some electrical components and floating docks is 48-52 weeks so additional time will be anticipated**
- Popps Ferry Extension #913 (ML) – Coliseum has the draft MOU for Board approval; ROW acquisition continues, funding secured for construction, close one additional RR crossing and send final crossing design to CSD, final roadway design required, Plan is to bid in 2023 and begin construction in 2024
- Popps Ferry Bridge & Approaches (ML) – Ph I design complete, contract for right of way acquisition being developed, EA being updated, top priority to obtain funding to repair existing bridge, submitted to emergency road and bridge repair program
- Repair/Replace Contract (DN)
 - o **Franks Drive Storm drain – on-going**
 - o **Park Drive Drainage**
 - o Campbell Drive – done
 - o Country Lane – done
 - o Saenger sewer investigation - done
- Rodenberg at Pass Road Intersection (CL) – Activated with MDOT, kickoff meeting held and parcel research underway as initial steps in row & easement acquisition process starts
-
- Saenger Theater Restoration (MH) – ticket booth and entrance doors removed. Brick wash in progress and nearing completion, waiting on new brick for lower part of west façade, **waiting on MDAH to approve parge coat color for concrete at base of west façade, waiting on change order to repair the signs (replace bulbs & repair) this should be the last CO, latest delivery date for new bricks for area beneath canopy is 12/12, do we want to install a plaque for renovation work, if so Blackline offered to purchase and install.**

- Sand Re-Nourishment #1064 (GP) – GOMESA Project, RFP for sand acquisition and trucking/spreading is in final draft, **plan to bid the 14th of December, advertise this month**
- Sediment Removal Phase III – hydrographic surveys complete, working on the permit applications, the sites that have SAV, Seymour is trying to work with DMR on a way to mitigate, Seymour updated council on Aug. 25th
 - o Hiller Park Pond (have permits)
 - o Cedar Lake Rd. Canal
 - o Cedar Lake Broadus (have permits)
 - o Kennedy Ln (SAV)
 - o Savannah Estates (DMR stated not eligible)
 - o Eagle Point Pin Oak (SAV)
 - o Linda Dr. (SAV)
 - o Beau Chene (DMR stated not eligible)
- Small Craft to Oak St Boardwalk (MH) – waiting on summary change order and final payment for warranty period to begin
- Tanglewood Infrastructure – received bids Aug. 19th, bids were up by about \$100K; award on Oct. 20th
- Visitors Center Repairs (CL) – Hopkins Construction for Zeta & non-Zeta repairs, Mangal's completed roof, now waiting clay tile and manufacturers roof warranty package, architect has started close out documentation
- Woolmarket Road Sidewalks (CL) – Sidewalk extended to Shriners Blvd., bid package reviewed by MDOT, working changes that resulted from MDOT review, environmental permitting documentation submitted and being reviewed by MDOT
- Woolmarket Road Traffic Study (EO) – Traffic counts for 3 intersection involving Shriners with (I-110, Shortcut, and Woolmarket Rd), 2 intersections with Old Hwy 67 (Hudson – Krohn, Woolmarket Road), and 1 intersection at Wash Fayard & John Lee Roads, activated with MDOT

ZETA Repairs

- Small Craft and Commercial Dock (GP) – JE Borries, \$555K, NTP for material procurement on 5/17/22, complete when material received estimated Nov. 1st NTP for 90 days estimated completion

HCUA Projects

- West Biloxi Treatment Plant clarifier being repaired
- Extension of Lorraine Rd. waterline extension
- Shriners Blvd. waterline extension

Subdivisions

- The Preserve – Pickering, 207 units, preliminary plat approved, currently just clearing and grading
- Eula Cove Townhomes – Andy Phelan, 40 units, preliminary plan approved, infrastructure approved, paving complete, waiting on Bac-Ts
- Emerald Lake – Dennis Steiffel, 131 units, all phases complete need maintenance bond
- Anchors Landing – Heinrich & Associates, 66 units, **laying sewer this week**
- The Reserve at Marsh Landing - Machado Patano, 9 units, infrastructure approved, **waiting on will serve letter**
- Point Breeze (Grande View) – Knesal Engineering, 39 units, preliminary plat approved, infrastructure approved, has an easement issue, **water & sewer done, storm drain on-going**
- Shorecrest Road – Kris Reimann, 54 units, **denied by council**
- Caillavet Cottages – Machado Patano, 9 units, under review
- College Cove Townhomes – Andy Phelan, 12 units, see Eula Cove Townhomes
- Park Court North – Thom Newman, 11 units, no activity
- Jim Byrd Road – Dennis Steiffel, 30 units, no activity

Under Warranty

- Bayview Avenue Walkway
- Lighthouse Pier Parking
- ZETA Repairs – Oak Street Pier (South) (DN)
- ZETA Repairs – Coliseum Pier (GP)
- ZETA Repairs – Causeway Park Bait Shop Roof (DN)
- ZETA Repairs – Multiple Piers Minor Repairs (DN)
