


## BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF Mar 20 - Mar 26, 2023

1 - Fires (Structure & Vehicle)	6
2 - Rupture/Explosion	1
3 - Emergency Medical Services/Rescue	125
4 - Hazardous Conditions	1
5 - Service Calls	12
6 - Good Intent	10
7 - Fire Alarm Calls; Active, Malfunction	20
8 - Weather/Natural Disaster	0
9 - Special Incident Type	4
Total	<u>179</u>

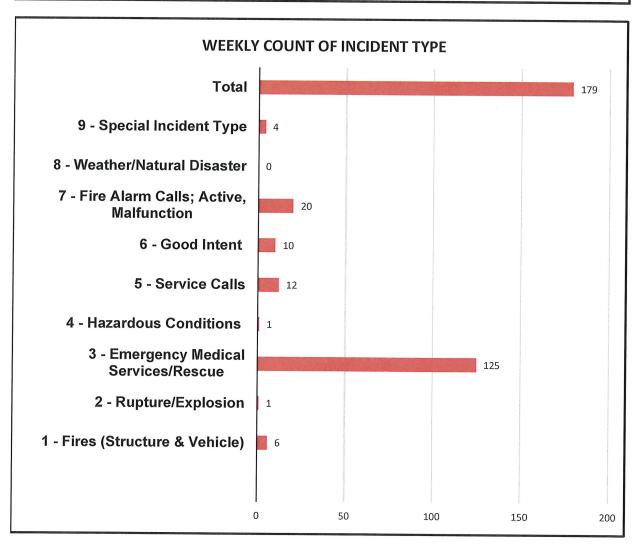

### **Criminal Intelligence Unit**

T. (228) 435-6159 F. (228) 702-3179 ciu@biloxi.ms.us



## Police Chief John B. Miller


170 Porter Avenue Biloxi, Mississippi 39530 Office: 228.435.6100 Fax: 228.374.1922 www.biloxi.ms.us


**DATE:** March 27, 2023

RE: Biloxi Police activity for March 20-26, 2023

TOTAL CALLS FOR SERVICE	1,771
TOTAL INCIDENT REPORTS	207
TOTAL OFFENSES (Violations/Reports)	218
TOTAL ARRESTS	125

Calls excluded from call type charts were: Extra Patrol – 445; Suspicious Circumstances – 100; Traffic Stops – 203; and Walk & Talk – 55. The Biloxi Police Crime Map may be viewed at https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f.







**DATE:** *March* 27, 2023

# COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Mar 20 - 26, 2023

Building permits issued	57
Construction Valuation of permits issued	\$2,280,000
Building inspections performed	85
Business licenses	7
Renewals	4
Charter Boats	
Peddler's licenses	
Certificates of Occupancy issued	8 (0 were Short-
	Term Rentals)
Code enforcement cases opened	38
Code enforcement cases resolved	32

## **Engineering Department**

Christy LeBatard, P.E. Director of Engineering



214-A Delauney Street P. O. Box 429 Biloxi, Mississippi 39533 Office: 228.435.6269 Fax: 228.435.6179 www.biloxi.ms.us

#### **Engineering Department Weekly Update**

March 27, 2023 (updates in red)

#### **Projects Out to Bid**

Sports Complex Field Improvements (April 26<sup>th</sup>)

#### **Projects in the Process of Being Awarded**

- Lorraine Road Waterline
- BRIC Grant (Cedar Lake Bridge) Application RFP

#### **Projects Under Construction**

- East Beach Sand Beach Renourishment
- Main Street RR Crossing
- Holley St. RR Crossing Closure
- Point Cadet Marina West
- Shriners Blvd. Water/Sewer Extension

#### **Private Utility Work in ROW**

- Lorraine Rd. (Cspire) boring starting soon
- Jim Byrd Rd. (Cspire) boring starting soon
- Sunkist South (Cspire) boring complete in 2 weeks X
- Sunkist North (Cspire) boring starting this week X
- East Biloxi (AT&T) boring complete, making asphalt repairs X
- Nature's Trail (Coast Connect) boring complete, working on grass issues
- Eagle Point (Coast Connect) complete

## **Projects**

- Bay Vista Water Well Received permit, design complete, ready to bid pending ARPA funding; tree removal by Public Works needed for access to site
- Canaan Fishing Dock Improvements (reconstruction) received DMR & Corps permits, on hold for GOMESA funding
- Causeway Lights Lamey is working on the existing lights to see if he can get them working

- Causeway Pier Zeta Repairs Plans being reviewed, should be ready to advertise next week
- Cedar Lake Bridge Repairs Plan to submit for MDOT Emergency Road & Bridge Repair Grant and BRIC Grant for M&E and structural repairs
- City Hall Preservation & Improvements PO for historical condition assessment has been issued
- Citywide Street Paving (Landshapers) scheduling with contractor, will have start date this week – Still waiting for Landshapers Mix Design to be approved by BCD
  - o Croesus

Laurelwood

o G.E. Ohr

o Ravenwood

○ Esters – Main to Holley

Ward 4 Streets

- o Esters Caillavet to Reynoir
- Concrete Annual Contract (ADS)
- CSX Crossings Nixon and Dorries Closed; Holley St next waiting on CSX Construction Agreement; Holley St. demo will start in early April
- East Biloxi Connector Road Porter to Hopkins (CDBG Funded) appraisals have been started, expect to start making offers in December, starting on Phase I from Porter to Benachi
- Fence Repairs PO's have been issued for Savarro Park, St. Mary's, Civic Center, & Gruich
- Fire Station No. 5 (Mark Williams) design kick off meeting on Feb. 3<sup>rd</sup>
- Hiller Park Drainage Improvements Cypress getting me a proposal to do conceptual drawings for grant application
- Hwy 90 Small Craft to Oak Street Curb & Gutter Repairs pending design contract, have conceptual
- Lighthouse Pier design efforts continue, Corps permits out for public hearing
- Keegan Bayou Restoration Permits being requested, GOMESA project submitted to DMR, also in the Restore Act Portal Working with DMR to get dredging permit approval
- Kuhn St. Boat Launch Expansion Conceptual started by Pickering, vegetation removal started, project scope revised to match tidelands funding grants, have 90% plans for review, ready to bid

- Lorraine Road Water Line Extension Ph 2 ARPA application for funding submitted, Recommendation to award will be on the March 21<sup>st</sup> council agenda for approval, lowest apparent bidder is Bottom to Top at \$1.1M
- Main Street Railroad Crossing Upgrades (Gulf Breeze Construction) NTP Jan. 16<sup>th</sup>,
   Flagger will be available early April
- Oak Street Pier (South) Cypress presented conceptual plans, working on a design contract
- Parker's Creek Sediment Removal Seymour contract approved by council, added scope to go as far north of I-10 as possible
- Pickleball Restroom ready to be advertise pending funding
- Point Cadet Re-Development #1092 Machado Patano is working concept
- Point Cadet Living Shoreline BMA No cultural resources issues, should have COE permit by end of March then will be ready to advertise
- Point Cadet Nearshore #1096 Held grant kickoff meeting, BMA is working on a contract, received MDEQ approval of contract, will be on council agenda in April
- Point Cadet Marina West AnderCorp NTP 10/24, 240-day contract, work on-going
- Popp's Ferry Extension #913 Coliseum has the draft MOU for Board approval; ROW acquisition continues, funding secured for construction, close one additional RR crossing and send find crossing design to CSD, final roadway design required, Plan is to bid in 2023
- Popp's Ferry Bridge & Approaches Ph I design complete, contract for right of way
  acquisition being developed, EA being updated, top priority to obtain funding to repair
  existing bridge, submitted to emergency road and bridge repair program
- Popp's Ferry Recreational Complex Lighting Asked Machado Patano to get me a proposal to do a condition assessment of the lights
- Port Repair Replace Contract
  - o Porter Avenue North Pier

o Forrest Avenue Pier

- Repair/Replace Contract
  - Atkinson/Treetop Complete
  - o Bilglade Drainage
  - West Oaklawn Drainage

- Riverview Drive Drainage
- Saenger Alley under construction

- Rodenberg at Pass Road Intersection Activated with MDOT, kickoff meeting held and parcel research underway as initial steps in row & easement acquisition process starts
- Sand Re-Nourishment #1064 GOMESA / W.C. Fore NTP Jan. 17<sup>th</sup>, total of 20,000 tons, east of schooner pier is complete, small craft harbor to west most WAVE is complete, working between WAVES and east of WAVE 1 towards boat ramp, on track to be complete by mid-April
- Sediment Removal the sites that have SAV, Seymour is trying to work with DMR on a
  way to mitigate, asked them to do another SAV survey under their existing contract;
  DMR is starting to allow invasive SAV to be removed
  - Hiller Park Pond (have permits)
- o Parkers Creek pending permit
- o Point Cadet Marina pending permits
- Shriners Blvd. Water & Sewer Extension (Overstreet) Gulf Coast Solutions Completion date: 07/16/23
- Sports Complex #1093 (Machado Patano) Receive bid April 26<sup>th</sup>
- Sylvania Street Drainage Cypress Environmental getting me a price to investigate and make recommendations on repairs
- Tanglewood Infrastructure Ph II ARPA project that was not awarded, working on getting this project out to bid, working with Contracts/Accounting to get the funding moved into this project
- Woolmarket Road Sidewalks (Machado Patano) MDOT doing their final plan/spec review, ready to bid as soon as receive concurrence from MDOT, Still working through additional MDOT comments regarding the schedule
- Woolmarket Road Traffic Study Traffic counts for 3 intersection involving Shriners with (I-110, Shortcut, and Woolmarket Rd), 2 intersections with Old Hwy 67 (Hudson Krohn, Woolmarket Road), and 1 intersection at Wash Fayard & John Lee Roads, activated with MDOT, contract at MDOT for review
- Woolmarket Acres Infrastructure Improvements (Tiffany, Oaklawn, Boyette, Shorecrest)
   (Overstreet) design contract awarded, held kick off meeting, survey 90% complete

## **ZETA Repairs**

 Small Craft and Commercial Dock – JE Borries, \$555K, NTP for material procurement on 5/17/22, complete when material received estimated Nov. 1<sup>st</sup> NTP for 90 days estimated completion; installing cross members and decks
