


# BILOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF May 15 - May 21, 2023

1 - Fires (Structure & Vehicle)	2
2 - Rupture/Explosion	1
3 - Emergency Medical Services/Rescue	100
4 - Hazardous Conditions	0
5 - Service Calls	22
6 - Good Intent	5
7 - Fire Alarm Calls; Active, Malfunction	28
8 - Weather/Natural Disaster	1
9 - Special Incident Type	3
	<u>162</u>

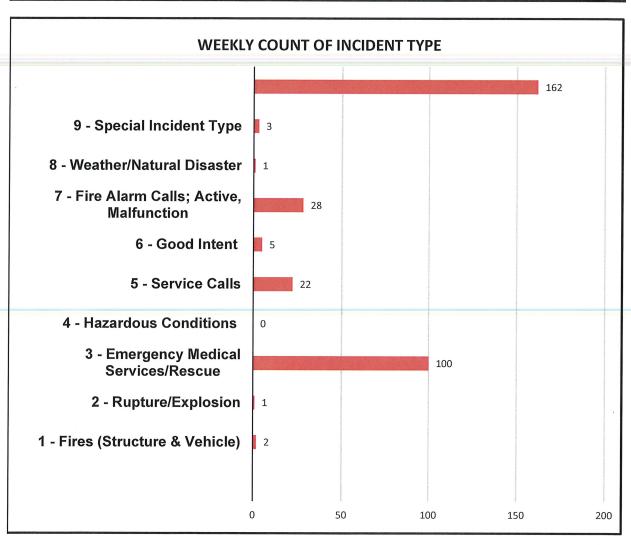

#### **Criminal Intelligence Unit**

T. (228) 435-6159 F. (228) 702-3179 ciu@biloxi.ms.us



#### Police Chief John B. Miller


170 Porter Avenue Biloxi, Mississippi 39530 Office: 228.435.6100 Fax: 228.374.1922 www.biloxi.ms.us


**DATE:** May 22, 2023

RE: Biloxi Police activity for May 15-21, 2023

TOTAL CALLS FOR SERVICE	1,679
TOTAL INCIDENT REPORTS	164
TOTAL OFFENSES (Violations/Reports)	206
TOTAL ARRESTS	87

Calls excluded from call type charts were: Extra Patrol – 318; Suspicious Circumstances – 95; Traffic Stops – 212; and Walk & Talk – 63. The Biloxi Police Crime Map may be viewed at <a href="https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f">https://www.arcgis.com/apps/dashboards/83df186bc01d41c9b035af33b058e76f</a>.



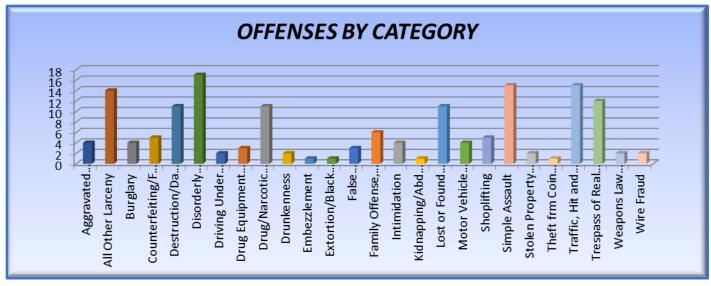



# **DATE**: *May 22, 2023* **COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR May 15 - 21, 2023**

Building permits issued	106
Construction Valuation of permits issued	\$4,603,200
Building inspections performed	87
Business licenses	6
Renewals	2
Charter Boats	
Peddler's licenses	
Certificates of Occupancy issued	15 (6 were Short-
	Term Rentals)
Code enforcement cases opened	
Code enforcement cases resolved	

### **Engineering Department**

Christy LeBatard, P.E. Director of Engineering



214-A Delauney Street P. O. Box 429 Biloxi, Mississippi 39533 Office: 228.435.6269 Fax: 228.435.6179 www.biloxi.ms.us

## **Engineering Department Weekly Update**

May 22, 2023 (updates in red)

#### **Projects Out to Bid**

#### **Projects in the Process of Being Awarded**

- Sports Complex Field Improvements (April 26<sup>th</sup>)
- BRIC Grant (Cedar Lake Bridge) Application RFP
- Pickleball Restroom (May 10<sup>th</sup>)

#### **Projects Under Construction**

- East Beach Sand Beach Renourishment
- Lorraine Road Waterline
- Main Street RR Crossing
- Holley St. RR Crossing Closure
- Point Cadet Marina West
- Shriners Blvd. Water/Sewer Extension

#### **Private Utility Work in ROW**

- Sunkist West (Cspire) boring starting next week
- Sunkist North (Cspire) boring underway
- East Biloxi (AT&T) boring complete, making asphalt repairs
- Nature's Trail (Coast Connect) boring complete, working on grass issues

#### **Projects**

- Bay Vista Water Well BMA is getting project ready to bid, MCWI grant agreement on council this week for approval
- Biloxi-OS Bridge Walking Path Ramp pending a design contract from BMA
- Biloxi/Keesler Welcome Sign pending a design contract from BMA
- Bridge Repairs
  - o Porter Avenue/Keegan Bayou Bridge Have PO waiting to schedule with contractor
  - o Wash Fayard Bridge Work is complete, except for final paving
  - Cedar Lake Bridge Have fracture critical repairs that need to be made asap, don't have quote yet on repairs

- Canaan Fishing Dock Improvements (reconstruction) received DMR & Corps permits, on hold for GOMESA funding
- Causeway Lights Lamey is working on the existing lights to see if he can get them
  working, Issue was with controller, manufacturer looking to see if he can get us a new
  controller because these lights are not made any long
- Causeway Pier Zeta Repairs Receive bids June 7<sup>th</sup>
- Causeway Pier Repairs (west side) Design pending Tidelands grant paperwork received and approved
- Cedar Lake Bridge Repairs Plan to submit for MDOT Emergency Road & Bridge Repair Grant and BRIC Grant for M&E and structural repairs
- Churchill Drive Ditch Improvements Have received a proposal from BMA to study the Churchill ditch and make recommendation on improvements, will be on the council agenda for approval in the next few weeks
- City Hall Preservation & Improvements Site visit is complete, waiting for the updated condition assessment, from there we can start the design process
- Citywide Street Paving (Landshapers) scheduling with contractor, will have start date this week – Waiting on a start date from Warren Paving

o Croesus

o Laurelwood

o G.E. Ohr

o Ravenwood

○ Esters – Main to Holley

Ward 4 Streets

- Esters Caillavet to Reynoir
- Concrete Annual Contract (ADS)
- CSX Crossings Holley, Nixon and Dorries Closed; Holley St. demo underway
- East Biloxi Connector Road Porter to Hopkins (CDBG Funded) –starting on Phase I from Porter to Benachi, all property is expected to be acquired by the end of May
- Eagle Point Park Working on design for lights, picnic tables, benches at playground, benches around walkway, trash cans, and possible shade structure
- Fire Station No. 5 (Mark Williams) design underway
- Hiller Park Drainage Improvements Cypress getting me a proposal to do conceptual drawings for grant application

- Hwy 90 Small Craft to Oak Street Curb & Gutter Repairs pending design contract, have conceptual
- Lighthouse Pier design efforts continue, Corps permits out for public hearing
- Keegan Bayou Restoration Permits being requested, GOMESA project submitted to DMR, also in the Restore Act Portal Working with DMR to get dredging permit approval
- Kuhn St. Boat Launch Expansion Conceptual started by Pickering, vegetation removal started, project scope revised to match tidelands funding grants, Pickering working on adding the 3<sup>rd</sup> boat ramp
- Lorraine Road Water Line Extension Ph 2 ARPA application for funding submitted, Awarded to Bottom 2 Top at \$1.1M - NTP May 22<sup>nd</sup> 150 days completion Oct. 19<sup>th</sup>
- Main Street Railroad Crossing Upgrades (Gulf Breeze Construction) NTP Jan. 16<sup>th</sup>, construction has started
- McDonnell Avenue Extension Pending design
- MGCCC Traffic Signal Have agreement with college in place for the 20% match, have received the MOU from MDOT for the construction, MOU under review then will be place on agenda
- Oak Street Pier (South) Cypress presented conceptual plans, pending Tidelands notification (\$400K) to start design; pending a design contract from Cypress
- Parker's Creek Sediment Removal Seymour contract approved by council, added scope to go as far north of I-10 as possible
- Pickleball Restroom Apparent low bidder Argus Building, \$142K, reviewing bids preparing to award contract
- Point Cadet Re-Development #1092 Machado Patano is working concept
- Point Cadet Living Shoreline BMA No cultural resources issues, should have COE permit by end of May then will be ready to advertise
- Point Cadet Nearshore #1096 -BMA contract will be on council agenda this month
- Point Cadet Marina West AnderCorp NTP 10/24, 240-day contract, work on-going, still
  waiting on electrical components and floating docks Change order on this agenda to
  make welding repairs on sheet pile wall (above water and below water) and grout to fill
  behind wall when complete

- Popp's Ferry Extension #913 Coliseum has the draft MOU for Board approval; ROW acquisition continues, funding secured for construction, close one additional RR crossing and send find crossing design to CSD, final roadway design required, Plan is to bid in 2023
- Popp's Ferry Bridge & Approaches Ph I design complete, contract for right of way
  acquisition being developed, EA being updated, top priority to obtain funding to repair
  existing bridge, submitted to emergency road and bridge repair program
- Popp's Ferry Recreational Complex Lighting Have condition assessment for lights, meeting with Sparta vendor to review their lights, then will have to decide how to proceed
- Port Repair Replace Contract
  - o Porter Avenue North Pier
- Repair/Replace Contract
  - o Bilglade Drainage
  - West Oaklawn Drainage started today
  - Riverview Drive Drainage starting next
  - Saenger Alley lining
  - Father Ryan Sewer Service Repair
  - o City Hall Water leak
  - o Hiller Park LS Erosion+
  - o Rue Sanchez water & sewer next on the schedule
  - Cedar Lake Rd. water backing up
  - Woodrow Place/Franklin Ct. manhole sinking

- o Forrest Avenue Pier
- Mason Road turn around for garbage trucks
- Camp Wilkes /Sharon Hills Sewer Repairs
- o Bay Vista Drive Pothole @ Churchill
- Sheridan Court Drainage
- o Campbell Drive Road sinking
- Old Woolmarket Rd./John Lee shoulder repairs
- Louise Street Drainage
- Oakcrest Sinkholes
- o City Hall Water Leak Complete
- Orleans & Carter pothole
- o Oakridge Place ditch
- o Hiller Park LS Erosion
- Rodenberg at Pass Road Intersection Activated with MDOT, kickoff meeting held and parcel research underway as initial steps in row & easement acquisition process starts
- Sand Re-Nourishment #1064 GOMESA / W.C. Fore NTP Jan. 17<sup>th</sup>, total of 25,000 tons, only 2000 tons remaining and expect to be complete by May 12<sup>th</sup>
- Sediment Removal the sites that have SAV, Seymour is trying to work with DMR on a
  way to mitigate, asked them to do another SAV survey under their existing contract;
  DMR is starting to allow invasive SAV to be removed
  - o Hiller Park Pond (have permits)
- Point Cadet Marina pending permits

- o Parkers Creek pending permit
- Shriners Blvd. Water & Sewer Extension (Overstreet) Gulf Coast Solutions Completion date: 07/16/23 going to do the change order work as a phase 2 project since the cost is so high, phase 2 will go out to bid in the next few weeks Change Order 1 on council this week to provide stubouts for future bores
- Sports Complex #1093 (Machado Patano) Rejected bids received April 26<sup>th</sup>, readvertising this week, open bids June 28<sup>th</sup>
- Spratley sewer/storm drain repairs Complete just waiting on the county to do the paving
- Sylvania Street Drainage Cypress Environmental approved on May 2<sup>nd</sup>
- Tanglewood Infrastructure Ph II –MP getting project ready to bid, the MCWI grant agreement is on this council agenda for approval
- Ward 2 Recreational Center Met with Pickering last week to review final layout
- Woolmarket Road Sidewalks (Machado Patano) MDOT doing their final plan/spec review, ready to bid as soon as receive concurrence from MDOT, waiting on MDOT to approve CE&I contract
- Woolmarket Road Traffic Study Traffic counts for 3 intersection involving Shriners with (I-110, Shortcut, and Woolmarket Rd), 2 intersections with Old Hwy 67 (Hudson Krohn, Woolmarket Road), and 1 intersection at Wash Fayard & John Lee Roads, held MDOT kickoff meeting, project has starting
- Woolmarket Acres Infrastructure Improvements (Tiffany, Oaklawn, Boyette, Shorecrest)
   (Overstreet) design contract awarded, held kick off meeting, survey 90% complete

#### **ZETA Repairs**

 Small Craft and Commercial Dock – JE Borries, \$555K, NTP for material procurement on 5/17/22, complete when material received estimated Nov. 1<sup>st</sup> NTP for 90 days estimated completion; installing cross members and decks
