




BIŁOXI FIRE DEPARTMENT INCIDENT SUMMARY REPORT FOR THE WEEK OF February 2 - February 9 2026

1 - Fires (Structure & Vehicle)	5
2 - Rupture/Explosion	
3 - Emergency Medical Services/Rescue	95
4 - Hazardous Conditions	4
5 - Service Calls	31
6 - Good Intent	39
7 - Fire Alarm Calls; Active, Malfunction	3
8 - Weather/Natural Disaster	0
9 - Special Incident Type	0
Total	<u>177</u>

WEEKLY COUNT OF INCIDENT TYPE

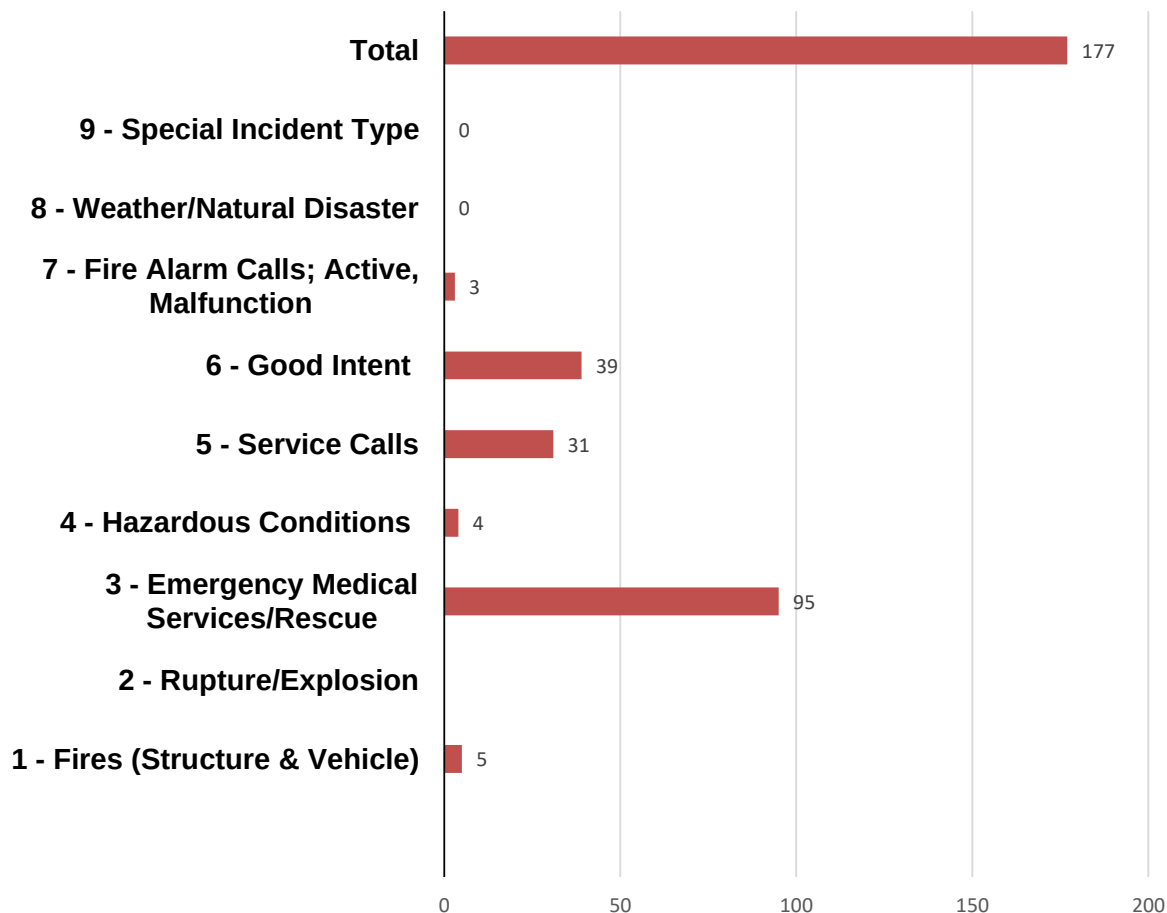


Biloxi Fire Department

Biloxi, MS



Breakdown by Major Incident Types (5530)

Start Date: 2/2/2026 7:00:00 | End Date: 2/9/2026 7:00:00

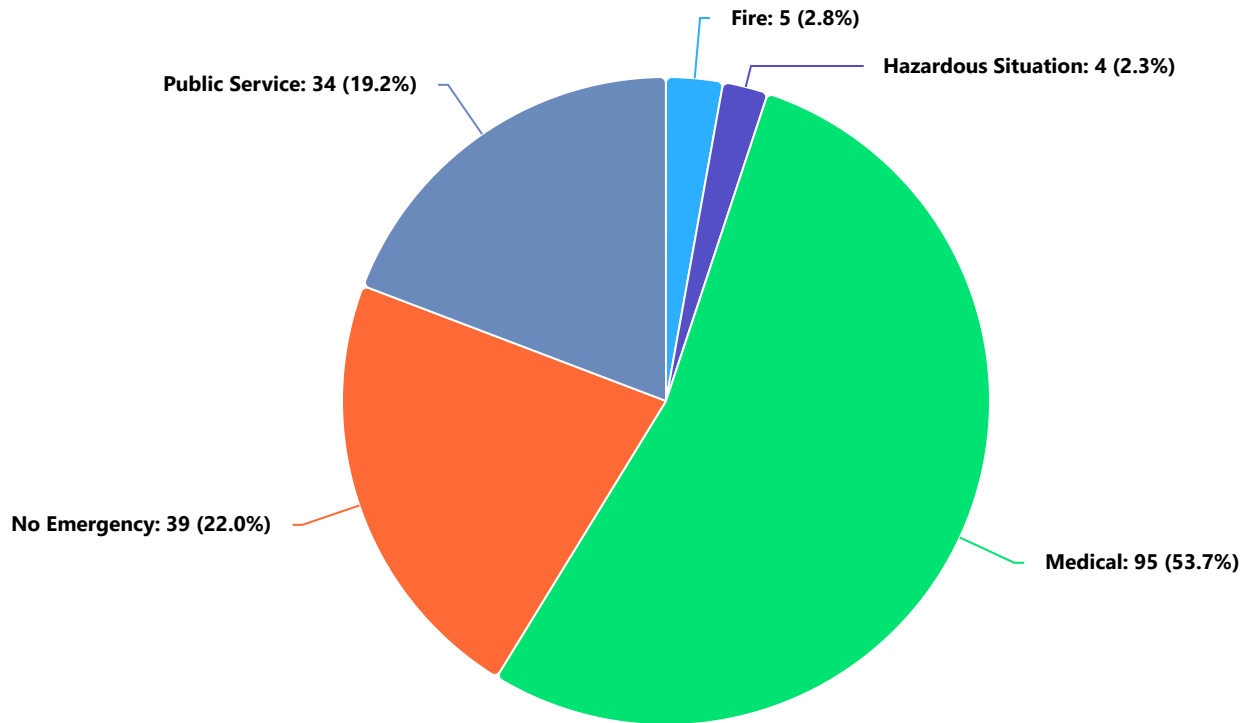

Fire	Hazardous Situation	Medical	No Emergency	Public Service
5	4	95	39	34

Primary Incident Type	Count	Percentage
Abdominal Pain / Problems	2	1.13%
Accidental Alarm	9	5.08%
Altered Mental Status	5	2.82%
Back Pain (Non-Trauma)	3	1.69%
Breathing Problems	21	11.86%
Cancelled	16	9.04%
Chest Pain (Non-Trauma)	8	4.52%
Choking	1	0.56%
Citizen Assist / Service Call	2	1.13%

Incident / Issue / Service Call	Count	Percentage
Confined Cooking / Appliance Fire	1	0.56%
Convulsions / Seizures	4	2.26%
Diabetic Problems	3	1.69%
Dumpster / Other Outdoor Contain...	1	0.56%
Electrical Hazard / Short Circuit	1	0.56%
Fall	15	8.47%
Fire Alarm	3	1.69%
Headache	1	0.56%
Heart Problems	2	1.13%
Hemorrhage / Laceration	2	1.13%
Law Enforcement	1	0.56%
Lift Assist	27	15.25%
Malfunctioning Alarm	6	3.39%
Medical Alarm	2	1.13%
Motor Vehicle Collision	7	3.95%
Nausea	1	0.56%
No Appropriate Choice	1	0.56%
No Incident Found Upon Arrival / Lo...	6	3.39%
Odor	1	0.56%
Other Traumatic Injury	1	0.56%
Overdose / Poisoning	1	0.56%
Person In Distress	1	0.56%
Room and Contents Fire	1	0.56%
Sick Case	6	3.39%
Smoke From Nonhostile Source (Sm...	2	1.13%
Smoke Investigation	2	1.13%
Stroke / CVA	2	1.13%
Trash / Rubbish Fire	1	0.56%
Unconscious Victim	2	1.13%
Unknown Problem	2	1.13%
Vehicle Fire - RV	1	0.56%
Well Person Check	3	1.69%
Grand Total	177	100.00%

This report runs off of the Dispatch Time. If you do not have a Dispatch Time in a report it will not show here.



emergencynetworking.com
#5530



Weekly Update
February 2, 2026

Public Works

152 Work Orders Completed for a total of \$120,804

- Water Billing
 -
- Sign Shop
 - 12 signs repaired/installed
 - 7 Obstruction removals
 - Azalea & Irish Hill – installed traffic mirror
 - Removed banner hardware on Howard Ave. wooden poles
- Construction Crew
 - Churchill concrete ditch repairs
 - State St. curb/driveway repairs
 - Installed total of 25 sy of concrete
- Water/Sewer Maintenance
 - 3 Hydrant repairs
 - 1 New water taps
 - 3 Water well repairs
 - 15 Meter/Meter box repairs
 - 4 Chlorine adjustments or change outs
 - Cleaned 2 lift stations
- 12 lift station electrical repairs
- Streets & Drainage
 - Cleaned 4 catch basins
 - 1 culvert replacement
 - Cleaned 1 ditch
 - 1 barricade set up
 - 4 Tree trimming work orders
 - 31 trash pickups
 - 10 pothole repairs
 - Cut grass on Runnymede, Greenwood, Pass Rd., Kuhn St. Medical Park Dr.
- Vehicle Maintenance
 - 2 Battery changes
 - 6 Misc. repairs
 - 4 Oil changes
 - 2 Replace tires
 - 4 Bridge maintenance work orders
- Building Maintenance
 - Working on rebuilding Mardi Gras stands

(Updates in Red)

Projects Out to Bid

Projects in the Process of Being Awarded

- RFQ for White Avenue Outfalls – selection committee meets 12/15/2025 –
- East Biloxi Access Rd. Ph III (01/14/2026) – **JE Talley**

Projects Under Construction

- Bay Vista Water Lines
- Gruich Center HVAC

- Keegan Bayou Restoration
- North Biloxi Well Casing
- Popps Ferry Extension
- Repair/Replace 2025-2028

Private Utility Work in ROW

- Bryn Mawr Ave. (Cspire) – bored through a sewer main, Harts Cont.; **repair is complete**
- Currie Subdivision (Cspire) – Pass Rd. to McDonnell Ave. & McDonnell Ave. to Glenn St.; **start construction Feb. 2nd; this will now start after Hawk Creek is complete**
- Forrest Ave., Benachi Ave. from Division to Bayview (AT&T) – start date TBD
- Greater Ave., Iris St., Gardenia St. and Daisy St. (AT&T) – start date TBD
- **Hawk Creek (CSpire) – Construction begins today**
- Howard Ave. from I-110 to Porter (transfer of wires to new poles) – AT&T has removed 13 of the 20 poles lines have been transferred; Lumen is complete and Sparklight still has a few poles left before AT&T can finish
- Main St., Esters Blvd., to Keller Ave. & Howard Ave. (AT&T) – aerial and underground work; start date TBD
- Mallard Creek (Sparklight) – Construction starting 02/03/26
- Rue Magnolia (Jackson St. Parking Lot) – Requested all utilities move from the old pole to the new pole so the old pole can be removed; Sparklight has moved, waiting on AT&T
- Southern Avenue & Greater Ave – Will be started after Circle Park and after BEA sidewalks

Projects

- Bay Vista Water Line Replacement Project No. 1013 – DNA Underground; \$3.3 million; Start May 1, 2025; 335 days; Completion April 1, 2026, 55% Complete as of December 2025
- Biloxi-OS Bridge Walking Path Ramp – BMA working on design, estimated cost \$120,000 project needs funding MDOT had some comments that BMA addressed they're now waiting for final MDOT approval
- Avery Bay Subdivision (Brodie Rd.) – 100% plans have been approved; project is waiting on decision by developer on the detention pond
- Falcon Glen Subdivision (Belle La Vie Ph 2) – starting to set manholes and lay sewer, working on sod around detention ponds
- Hawk Creek Subdivision Ph III (Oaklawn & Shorecrest) – Construction plans have been approved, project on hold until the issue with the trees has been resolved
- Howard Creek Bridge (Old Hwy 67, just east of Hudson Krohn/Cedar Lake Intersection) – Received \$1.6M in State Aid funding (\$0 match) to replace this bridge, DMR/Corps permit has been issued; bridge temporarily closed for emergency repairs; will receive bids for the replacement beginning of March.

- Gruich Center HVAC upgrades – apparent low bidder DNP \$624,750; equipment delivery will begin the week but the air handlers won't be here until February 2026
- Keegan Bayou Restoration – JE Borries, Inc.; \$698K; Awarded April 18, 2025; Pre-construction meeting May 29, 2025; NTP December 1, 2025, work has started.
- Kinglsey Ridge Subdivision – Tribe Drive; issued construction plan approval for phase 1
- Kuhn St. Boat Ramp – Tidelands Application submitted for FY27 funding in the amount of \$500K in additional funding for construction
- North Biloxi Well Casing – Receive bids August 13, 2025, apparent low bidder Lyman Well \$450,000, under construction
- Oak Street Pier (South) – Received 60% design plans; project needs funding; Tidelands application submitted for FY27 funding in the amount of \$2.6M for construction
- Preserve at Parker's Creek Phase II (Shriners Blvd.) – Construction plans have been approved, developer waiting on his contractor
- Phase II Paving (Ward is parenthesis)

▪ Pinecrest (7)	▪ Briarfield Ave. (5)	▪ Stacy Ln (6)
▪ Dundewood (7)	▪ Beacon Pl. (5)	▪ Schonewitz (6)
▪ RSR 1 & 2	▪ Deming Pl. (5)	▪ La Bonne Terre Concrete Streets (4)
▪ Point Cadet Marina area (1)	▪ Fayard Street (1)	▪ Copp Street (2)
▪ Cuevas Street (1)	▪ Victory Lane (7)	▪ Destiny Plantation (6)
▪ Mercury Lane (5)	▪ Jackson St. bricks (1)	▪ Keller Ave (1)
▪ Pine Grove Ave. (5)	▪ Comfort Pl Lee to Keller (1)	
	▪ Jenkins Alley (1)	
- Point Cadet Nearshore #1096 (BMA) – design on-going, permitting is going to take longer than we thought, it's probably going to be another 4-6 months in permitting; Corps is waiting for concurrence from National Marine Fisheries before they can issue their permit.
- Point Cadet Marina Phase II – will be receiving \$5.5 million in Restore funding, grant agreement was approved June 10, 2025; working through the documentation to submit to MDEQ
- Popp's Ferry Extension #913 – Necaise Bros. \$20.8M, NTP 11/25/2024
 - Contractor is working on installing the road base on the south side of the RR tracks
 - Water, sewer and storm drain between Hwy 90 and RR tracks is substantially complete
 - Will begin working on the retaining wall that leads up to the underpass soon
 - Work is 33% complete as of end of December

- Popp’s Ferry Bridge Draw Replacement – Neel-Schaffer, \$506K,
 - Design on-going
- Repair/Replace Contract – Currently on hold under additional funding is allocated
- Rodenberg at Pass Road Intersection – ROW acquisition is almost complete, one property one is holding out
- Shriners Blvd. Widening – Project was approved in the STIP; ready to begin the MDOT process by requesting Project Activation as soon as grant match is funded
- Southern Magnolia Subdivision (Shorecrest Blvd.) – Construction plans have been approved; construction pending outside agenda approvals; contractor waiting for gas main crossing agreement for the off-site water line
- Woolmarket Acres Infrastructure Improvements (Tiffany, Oaklawn, Boyette, Shorecrest) (Overstreet) Corps walked to the project prior to developing their final scope of work for our review
