BILOXI FIRE DEPARTMENT
INCIDENT SUMMARY REPORT FOR
THE WEEK OF NOV. 13-19, 2017

Turned around in route (no fire) / Citizen Complaint/Explosion/ other	**2**
Fires (Structure & Vehicle)	**5**
Rescue & Emergency Medical Services	**103**
Medical Involving Homeless Persons	**2**
Hazardous Conditions	**4**
Service Call;	**5**
Good Intent Call:	**22**
Special Incident Type	**0**
Fire Alarm Calls; Active, Malfunction	**19**
Total	***162***

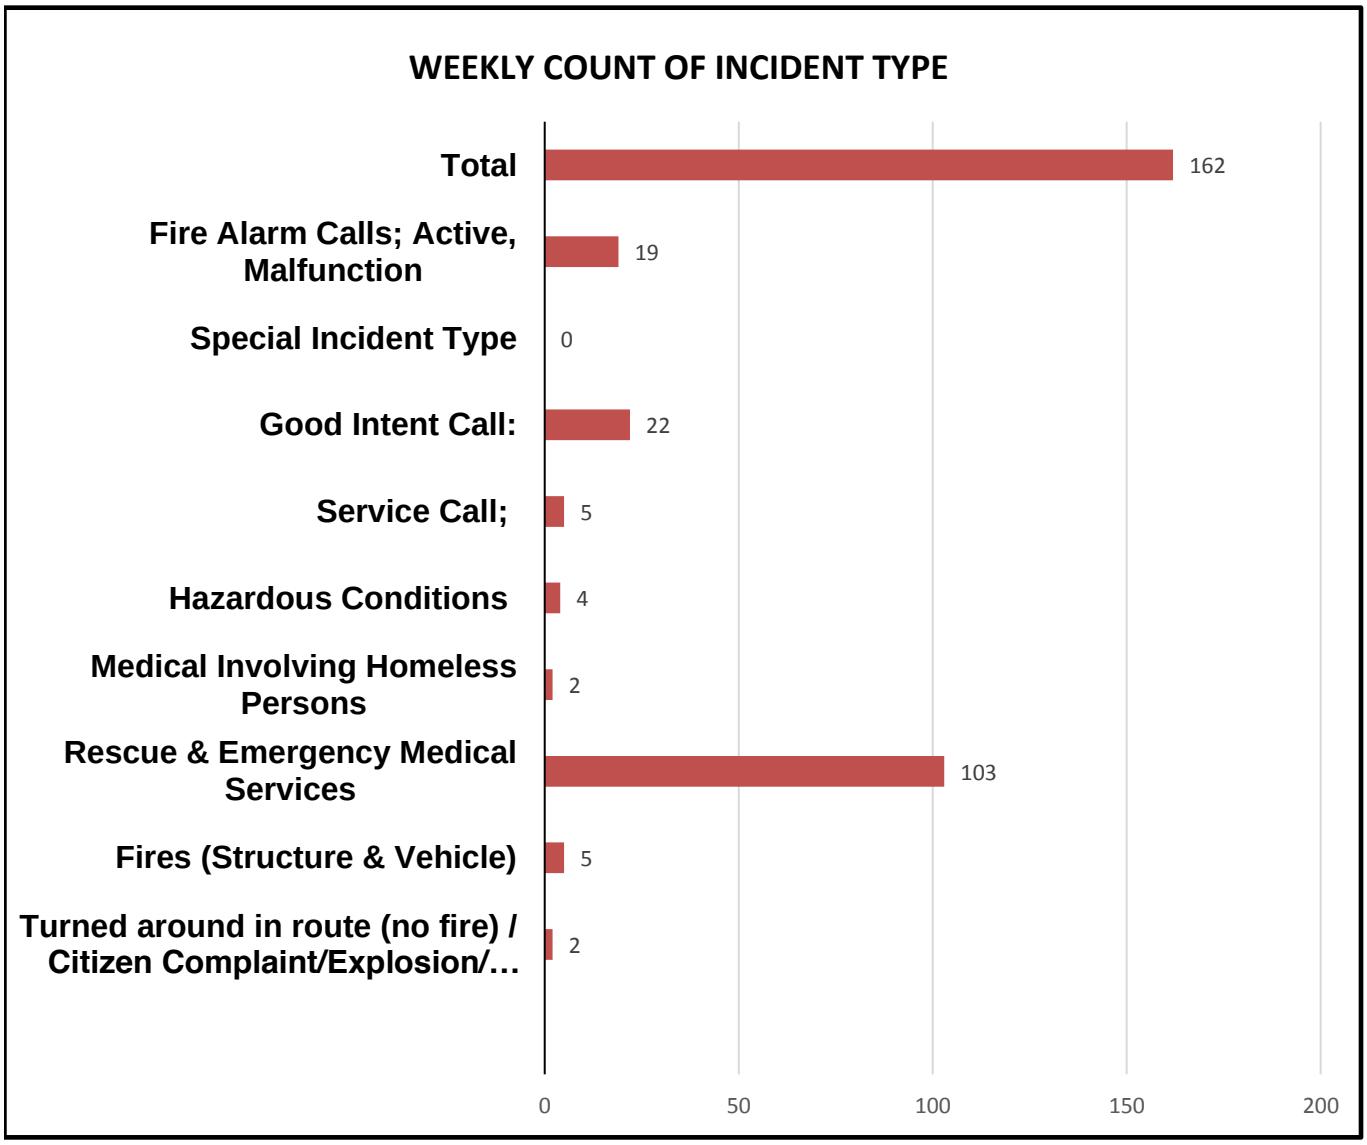

Criminal Intelligence Unit
T. (228) 702-3160
T. (228) 702-3122
T. (228) 702-1276
F. (228) 702-3179
ciu@biloxi.ms.us

Police Chief
John B. Miller

170 Porter Avenue
Biloxi, Mississippi 39533
Office: 228.435.6100
Fax: 228.374.1922
www.biloxi.ms.us

DATE: November 20, 2017

RE: Biloxi Police activity for Nov 13 – 19, 2017

TOTAL CALLS FOR SERVICE	***2,374***
TOTAL INCIDENT REPORTS *(Case Numbers)*	***249***
TOTAL OFFENSES *(Violations/Reports)*	***197***
TOTAL ARRESTS	***115***

Calls excluded from call type charts were: Checking Building – 130; Extra Patrol – 933; Suspicious Circumstances – 86; Traffic Stops – 311; and Walk & Talk – 121. Additional details may be viewed at http://www.crimemapping.com/map/ms/biloxi.

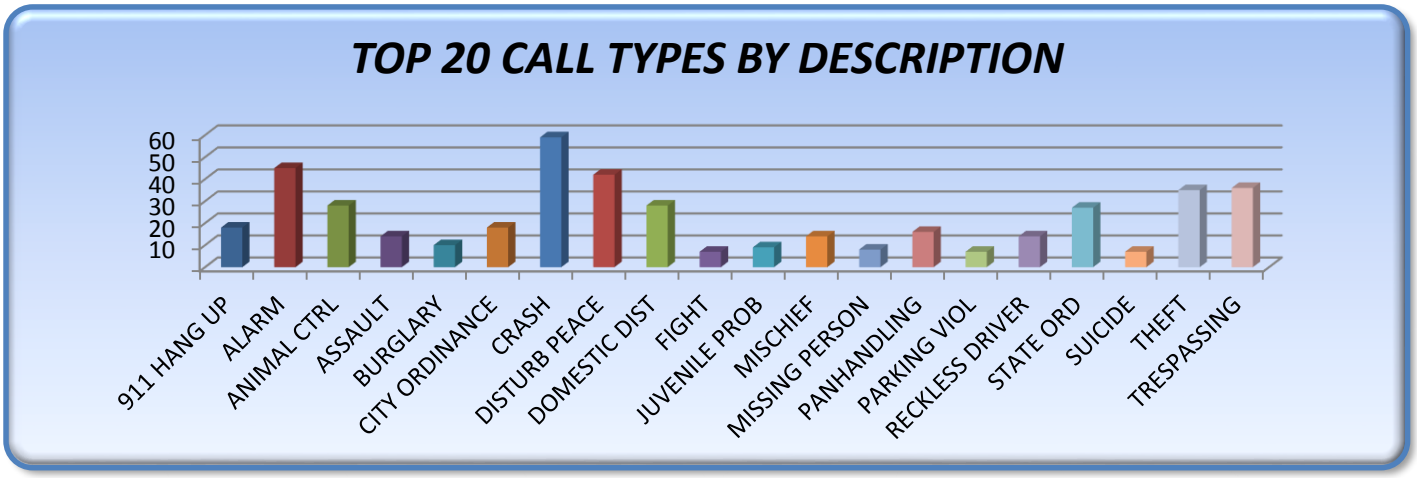

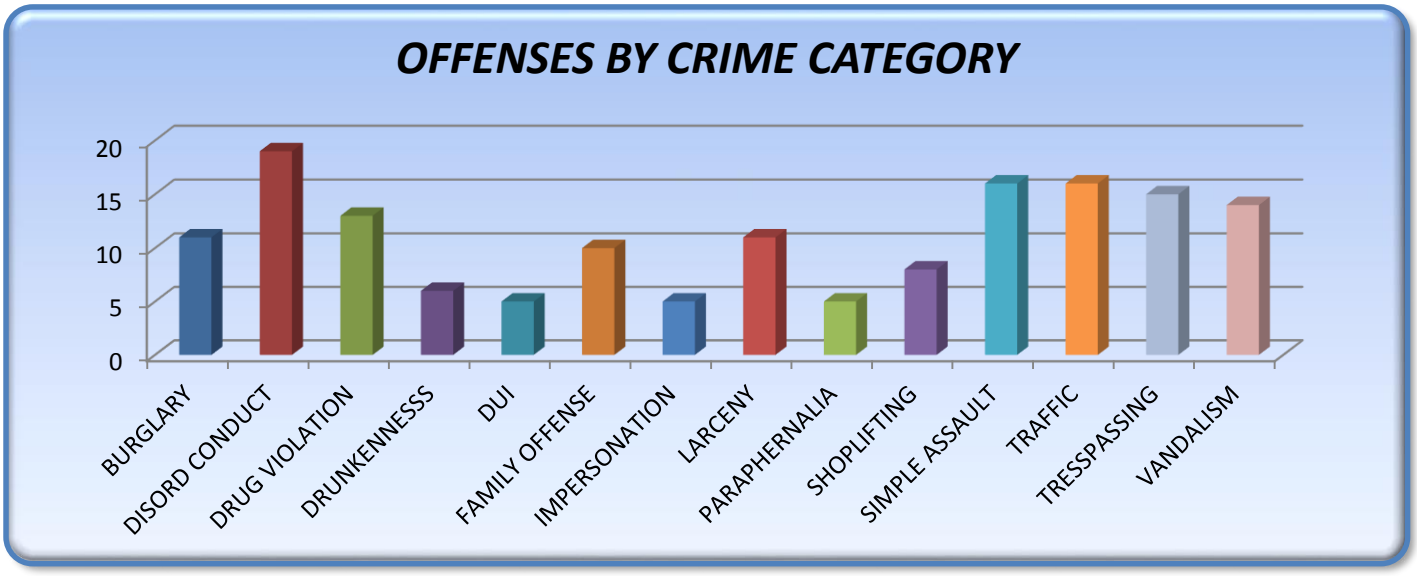

DATE: November 20, 2017

COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Nov 13 – 19, 2017

Building permits issued	75
Construction Valuation of permits issued	$2,625,500
Building inspections performed	136
Business licenses **Renewals** **Charter Boats** **Peddler's licenses**	4 14
Certificates of occupancy issued	10
Code enforcement cases opened	137
Code enforcement cases resolved	350

Engineering Department
Christy LeBatard, P.E.
Director of Engineering

214-A Delauney Street
P. O. Box 429
Biloxi, Mississippi 39533
Office: 228.435.6265
Fax: 228.435.6179
www.biloxi.ms.us

Biloxi
established 1699

Engineering Department Weekly Update
November 20, 2017
(updates in bold)

Railroad sign installation is complete, contractor working on punchlist

Cityworks –

- P&R training is complete
- CD is working on inputting their data then training can start
- Fire Department training is complete

Census Address Points – 85% complete

Hurricane Nate

- Starting detailed cost estimates for damages
- Damage repairs for large items pending budget
- **Lighthouse Pier Permit being submitted to DMR this week**
- **Getting quotes on Ice Wharf and Oak St. pier repairs**

Projects

- Amtrak rail platform grant – Continuing assisting Southern Rail Commission with grant application

- Bellewood Subdivision – paving complete, contractor still working on punchlist

- **Canaan Fishing Dock Improvements** – met with Seymour Wednesday Nov. 15th for project update

- **Clearview Drainage** – started this work, should be finished in a few weeks

- CSX Crossing Closure – NS contract awarded to begin preliminary work; have MOU with MDOT, working through minor changes; waiting for authority to enter into contract with NS for design work from MDOT

- **Dredging** – Finished Canaan, working at Point Cadet; Point Cadet permit modification was received last week, Borries will finish all of Point Cadet before moving on. Bayou LaPointe DMR permit modifications currently being processed with DMR, should go to next Commission meeting

- Ellzey Place II – continuing with storm drain installation, water & sewer 95% done

- Ellzey Place III – design contract awarded, Rumsey Engineering given ok to proceed

- Emerald Lake Subdivision (Hudson Krohn Rd.) – Utility installation complete; water line still to be testing; working on grading, digging pond, asphalt installation is planned for this week

- Excursion Pier – J.E. Borries given NTP date Oct. 1st.

- Fire Station No. 7 – design 95% complete; working out bid details with SMPDD

- Fire Station No. 10 – clearing and grubbing complete, topographic survey pending

- **Holly Bluff & Cedar Lake Sewer** – preparing letters to homeowners for sewer connections; plan for those to go out next week

- Howard Avenue –50% design review underway; getting PO for survey for maps & deeds for ROW; 4 way intersection for MLK/Howard/Dukate; need to contact Cotton Fore to request permission to dig up bricks

- Lighthouse Parking Lot - change order to add alternates back to project was approved

- Jordan Subdivision (Old Hwy 78) – Utility installation complete; waiting for road base to set

- Kayleigh Cove Sewer – Sidewalk change order approved, contractor preparing to start

- Keesler Gate Outside – ready to begin parcel acquisition

- Keesler Gate Inside – design work approximately 90% complete; bidding still on schedule for January 2018

- **Keesler Privatization** – working on 2nd round of responses, meeting internally today at 1:00, preparing for meeting in January

- **Ohr O'Keefe Fire Damage Repairs** – clean up finished, additional PO for $1,700 to fix one piece of equipment. Got a 2nd quote to replace the damaged cooler for $2,500 but holding off on that for now.

- Popps Ferry Extension – preparing maps & deeds for property acquisition; talking to Coliseum about contributing funds for project

- Pedestrian Crosswalk @ MGM – MDOT opened bids, bids were over budget, waiting to hear back from MDOT on how they plan to proceed

- Pedestrian Crosswalk @ Harbor – Survey complete

- Point to Palace Boardwalk – survey being finalized

- Police Substation Exterior – under construction; expected completion date Nov. 17th

- Police Substation Interior – preparing bid documents to harden the interior, plan to have ready to bid in 30 days

- Public Safety Center Roof Leaks – met with Dale Partners last week, getting a proposal

- **Popps Ferry Bridge Submarine Cable** – Pre-bid meeting on November 15th, had about 5 contractors present

- Popps Ferry Bridge & Approaches – adding funding back to budget for this year to keep project moving forward

- Popps Ferry Causeway – construction continuing; adding the following work – sidewalk to Cambridge Drive, additional solar lights, fishing cleaning stations, bait tanks at bait shop, kayak racks at bait shop, additional educational signs and components, upgrade walking trail materials to flexipave; trying to fit in additional parking but looking like there's not enough room; any work at the boat ramp was denied because it wasn't in original scope and there are not permits covering that area

- **Post Office Build-out** – Finalizing layout for empty space for IS and training facility; need ok on floor plan; then will start preparing plans to go out to bid

- Rock Creek Subdivision Phase II – contractor finishing punchlist, working toward final plat approval; contractor working on re-grading some of the properties along Sage Road to drain toward street instead of toward existing homes in rear

- **Saenger Theater** – Dale Partners amendment on the Dec. 1st council meeting

- **Small Craft Boat Launch** – Work is 90% complete

- Snyder Center Roof – Met with Dale Partners last week, getting a proposal

- **Tennis Court Repairs** – Started last Friday, will be complete this week

- Tremont (Lloyd Moon) driveway repairs – contractor will complete Lafayette Street then move to Tremont, expect work to begin before end of year

- **West Biloxi Boardwalk** - Opened bids on Nov. 8th, apparent lowest bidder CM Combs Construction at $1.097M; bid award pending legal review

- Woolmarket Master Plan – Received final draft for review

- Woolmarket Drainage – ready to start easement acquisition and environmental

- Woolmarket water line – have identified a potential grant through the Corps of Engineers, waiting for confirmation from Corps
