BILOXI FIRE DEPARTMENT
INCIDENT SUMMARY REPORT
FOR THE WEEK OF 29 Oct - 04 Nov 2018

Turned around in route (no fire) / Citizen Complaint/Explosion/ other	0
Fires (Structure & Vehicle)	3
Rescue & Emergency Medical Services	106
Rescue & Emergency Medical Services for Homeless Encounters	5
Hazardous Conditions	9
Service Call;	8
Good Intent Call:	9
Special Incident Type	0
Fire Alarm Calls; Active, Malfunction	11
Total	***151***

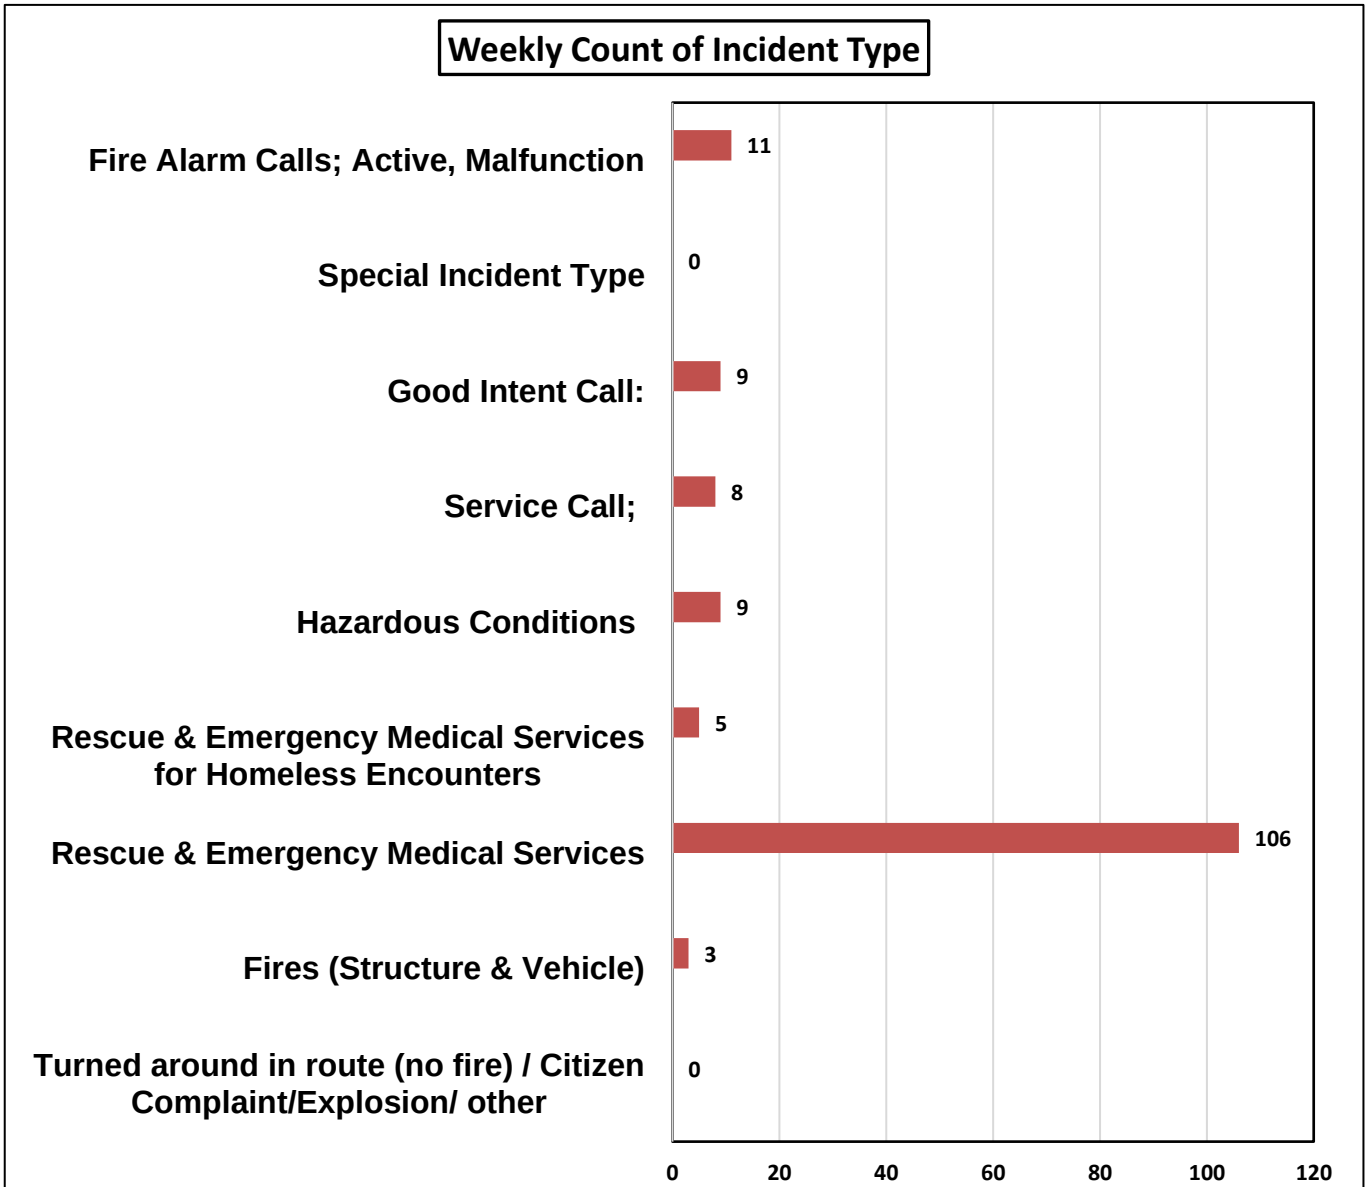

Criminal Intelligence Unit
T. (228) 702-3122
T. (228) 702-1276
T. (228) 702-3113
F. (228) 702-3179
ciu@biloxi.ms.us

Police Chief
John B. Miller

170 Porter Avenue
Biloxi, Mississippi 39530
Office: 228.435.6100
Fax: 228.374.1922
www.biloxi.ms.us

DATE: November 5, 2018

RE: Biloxi Police activity for October 29-4 November, 2018

TOTAL CALLS FOR SERVICE	***2,207***
TOTAL INCIDENT REPORTS ***(Case Numbers)***	***277***
TOTAL OFFENSES ***(Violations/Reports)***	***223***
TOTAL ARRESTS	***107***

Calls excluded from call type charts were: Checking Building – 90; Extra Patrol – 867; Suspicious Circumstances – 98; Traffic Stops – 179; and Walk & Talk – 147. Additional details may be viewed at http://www.crimemapping.com/map/ms/biloxi.

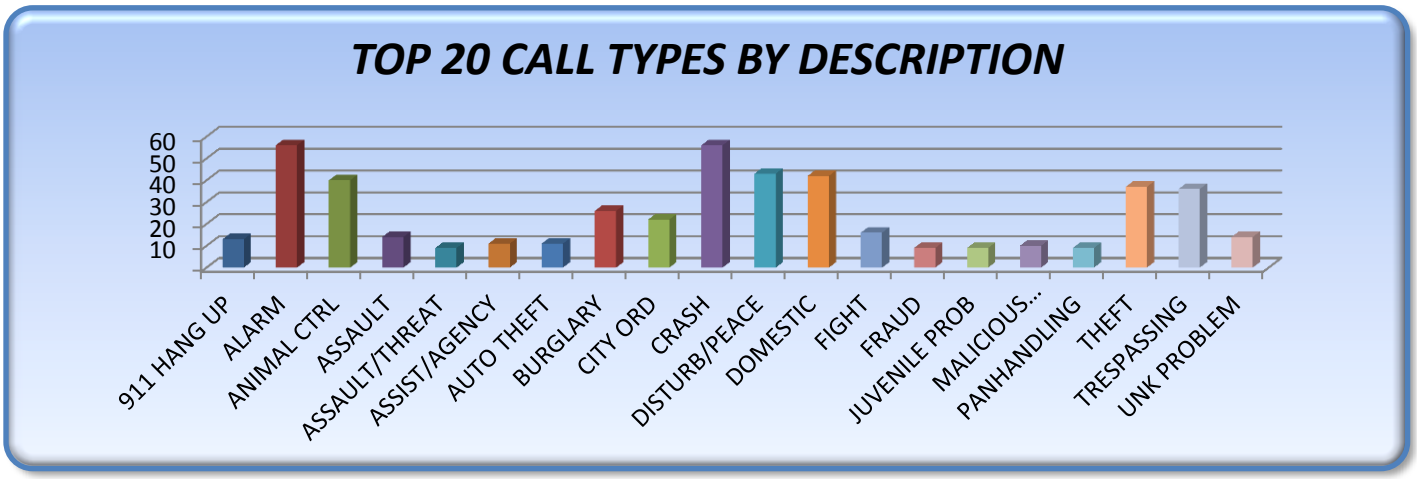

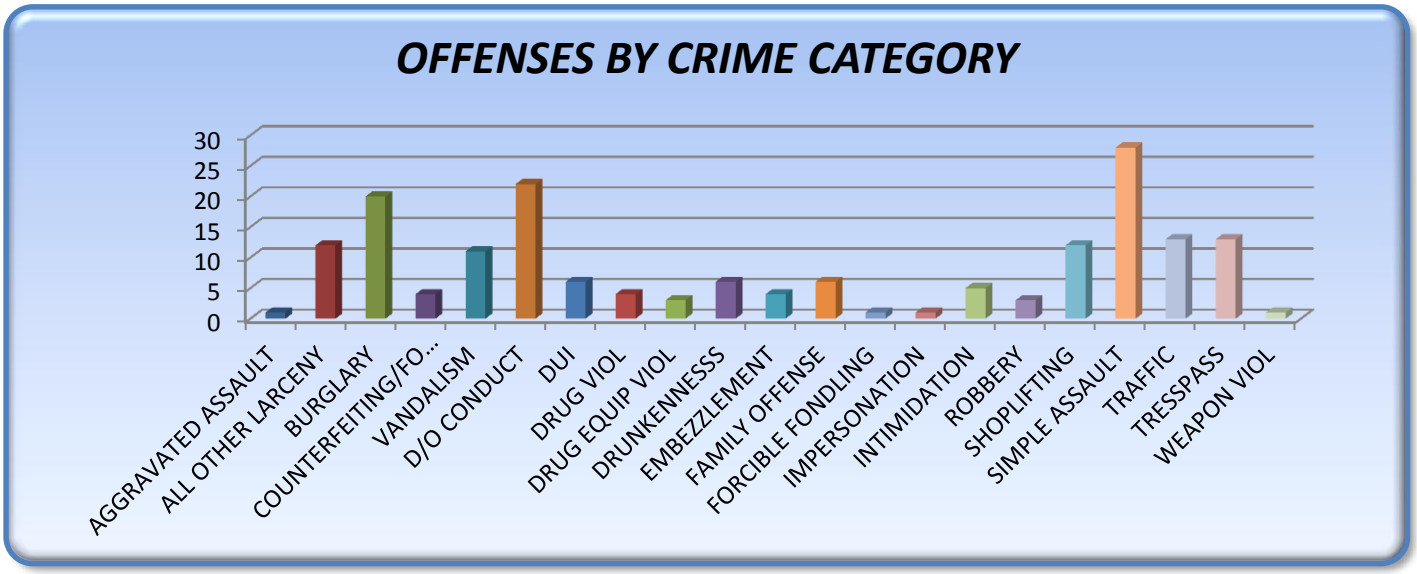

DATE: *Nov. 5, 2018*
COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Oct. 29 – Nov. 4, 2018

Building permits issued	*75*
Construction Valuation of permits issued	*$582,050*
Building inspections performed	*134*
Business licenses **Renewals** **Charter Boats** **Peddler's licenses**	*5* *3*
Certificates of occupancy issued	*14*
Code enforcement cases opened	*138*
Code enforcement cases resolved	*122*

Engineering Department
Christy LeBatard, P.E.
Director of Engineering

214-A Delauney Street
P. O. Box 429
Biloxi, Mississippi 39533
Office: 228.435.6265
Fax: 228.435.6179
www.biloxi.ms.us

Biloxi
established 1699

Engineering Department Weekly Update
November 5, 2018
(updates in bold)

FunTime USA Drainage – Public Works going to close up boxes, developer to handle the rest

Cemetary Project – Website is now active, next phase is to work on filling in the missing information, have over 15,000 gravesites in the website

Hiller Park Playground Covers – Have quotes for both playgrounds $6500 for small one and $11,700 for big one;

Rue Petit Bois Ditch – work beginning this week pending weather; should be complete in 4-6 weeks

Natatorium – Coordinating with contractor, should have quote for testing by end of week

Woolmarket Master Plan - now available on the Engineering Department website for the public to access

Hurricane Nate

- Lighthouse Pier Repairs – JE Borries $140K; NTP 6/6/2018; completion date on 7/21/2018; all decking and handrail done; change order for submersible electrical cabinet on 10/2/18 Council agenda

Projects

- **Bayview Avenue Boardwalk** – permit application pending DMR approval; estimated cost $1.2 million

- Belle La Vie Parkway – topographic and geotechnical work beginning on Increment 1A

- Canaan Fishing Dock Improvements – permit application submitted to DMR; public hearing was held last week at DMR, there were no comments;

Commission approved permit; Corps Permit still pending but there have been no public comments or questions from Corps

- Cedar Lake Bridge Repairs (Const. Funding 2021) – project activation request on council agenda Nov. 6th

- Creole Cottage Roof – Waiting for quotes to be returned by contractors

- CSX Crossing Closure (MDOT Funded) – Neel-Schaffer study completed, finalizing surveys now

- CSX Crossing Closure (CDBG Funded) – 30% submittal reviewed by CSX; working toward 60% submittal; EA has been approved, design moving forward

- Dredging – Finished Canaan, Point Cadet, Hiller Park, and Mercedes now; contractor moved on to North Haven; still coordinating Oak St. Pier debris removal costs with Borries

- Dukate Street Paving – Received quote for $15,000, paving pending completion of heavy construction at hotel

- **East Biloxi Public Access & Living Shoreline** – Task D (South of Bridge to Point Cadet Marina) and Task E (North of Bridge to Palace); *DCD Construction awarded Alt. A & B for a total of $1.8M; NTP date pending exploratory work behind the bulkhead may see small equipment and temporary fencing on site*

- East Biloxi Boardwalk (Small Craft to Kuhn St.) – BMA performing structural analysis

- Ellzey Place II – Lane Construction is expected to be completed in July

- Ellzey Place III – final construction plans and specs currently under review

- **Fire Station No. 7** – *NTP August 15, 2018, Starks Construction; foundation work underway*

- **Fire Station No. 10** – *NTP 8/27/18; Contractor: JW Puckett $2.35 million; foundation work underway*

- **Hiller Park Pond Dredging** – *A permit will be required; Purchase Order pending for survey to determine depth and quantity to be dredged*

- Hiller Park Trail – Need to submit quarterly report

- **Howard Avenue** – Gulf Breeze Landscaping NTP 4/9/2018; Completion 10/6/2018; *brick installation continuing through Lameuse Street; contractor working at MLK;*

- **Keesler Gate Outside** – Property acquisition continuing; setting up meeting with CD to determine DRC/tree needs

- **Keesler Gate Inside** – Awarded to Necaise Brothers Const. $4.8 million on 4/24, NTP 5/21/2018; 540 Calendar Days; Completion Date 11/12/2019; *still working on "C" Street ditch; working on limestone roadway base and electrical*

- Keesler Privatization – Pending final decision Oct – Dec 2018; currently reviewing contract from Neel-Schaffer for assistance during the transition period

- Main Street Railroad Crossing Upgrades (MDOT Funding 2020) – project activation on 10/2/18 council agenda; work cannot begin until GO19 Bond funds are available

- **Point Cadet Marina Electrical Upgrades** – Full electrical upgrade of entire harbor expected to cost in the $150K to $200K range; existing transformer is adequate to upgrade the necessary pedestals; *project will be ready to bid by end of Nov.*

- Point Cadet Marina Improvements (West) #1024 – Old Task "A" & "C"; currently on hold

- **Popps Ferry Extension #913** – *Coliseum has the draft MOU for Board approval; 33 parcels to acquire; surveys and appraisals are underway; Public Hearing on updated EA on Nov. 13th at 6 pm Donal Snyder Center*

- Pedestrian Crosswalk @ MGM – Malouf Construction; Completion Date 12/30/2018;

- **Pedestrian Crosswalk @ Harbor** –Dan Hensarling, Inc. $2.4M; NTP October 8, 2018*; MDOT permit and lane closures have been approved; contractor mobilized beginning work on relocating water lines on the north side*

- Public Excursion Pier South of Pine/Cedar #1030 – Old Task "B"

- **Public Safety Center Roof Leaks** – Dale Partners doing assessment of building, had a specialist look at the buildings on 8/9/2018; waiting report of that inspection; *received spec on Friday, will be out for quotes by the end of this week*

- Popps Ferry Bridge Submarine Cable – Contract documents were returned 6/1/2018, preconstruction meeting was held June 21st, they have 6 months to get the materials in then Notice to Proceed will be issued;

- Popps Ferry Bridge & Approaches – pending EA approval; met with BMA draft EA is at MDOT for preliminary approval once receive comments back final EA

will go to MDOT/FHWA for approval; once approval is granted the City can petition MDOT to start ROW Acquisition

- **Popps Ferry Causeway** – *Fire Alarm issue resolved; therefore CO can be issued; we have verbal approval on contingency items with the exception of Landscape Maintenance and floating docks*

- Post Office Build-out – Project ready to bid

- Saenger Theater Phase I Fly Tower – Currently under design, planning to advertise for construction by the end of the year

- Saenger Theater Phase II Exterior walls, roof, HVAC and canopy – design started but on hold until Phase I complete; planning to advertise for construction by Summer 2019

- Saenger Theater Phase III Interior – start design in summer 2019, bid for construction by beginning of 2020

- Smith Subdivision (north corner of Woolmarket Rd. & Old Hwy 67) – Started clearing and grubbing; may look at developer donating property for a city detention pond

- **Snyder Roof Bid** – *received bids on the roof replacement on 9/19/18, bids on the Oct. 16th council agenda; work pending receipt of executed contract documents*

- Sports Complex Tennis Courts Phase II – Council approved PO; scheduling work with contractor

- West Biloxi Boardwalk Phase 1A - Construction complete, awaiting close-out documents

- West Biloxi Boardwalk Phase 1B – Issued Buzzy Bolton authorization to proceed with design

- **Woolmarket Rd. East Drainage** – Working on getting easements; right now estimated at 45 easements needed; *requested contract from DE with modified scope will be on council agenda as soon as received*

- Woolmarket Rd. East (Larkin) water line – DNA Underground; NTP 4/23/18; completion date 2/17/2019; connections to utility authority and city mains are complete; pending change order for a decrease of $94,000 due to underruns in limestone base and backfill therefore the full width overlay can be done with no addition costs to the project

- **Woolmarket Road Sidewalk from Lorraine to Old Hwy 67** – *Project Activation Request will be on council agenda Nov. 6th*
