BILOXI FIRE DEPARTMENT
INCIDENT SUMMARY REPORT FOR
THE WEEK OF FEB. 04-10, 2019

Turned around in route (no fire) / Citizen Complaint/Explosion/ other	2
Fires (Structure & Vehicle)	3
Rescue & Emergency Medical Services	96
Medical Involving Homeless Persons	5
Hazardous Conditions	5
Service Call;	12
Good Intent Call:	14
Special Incident Type	0
Fire Alarm Calls; Active, Malfunction	9
Total	***146***

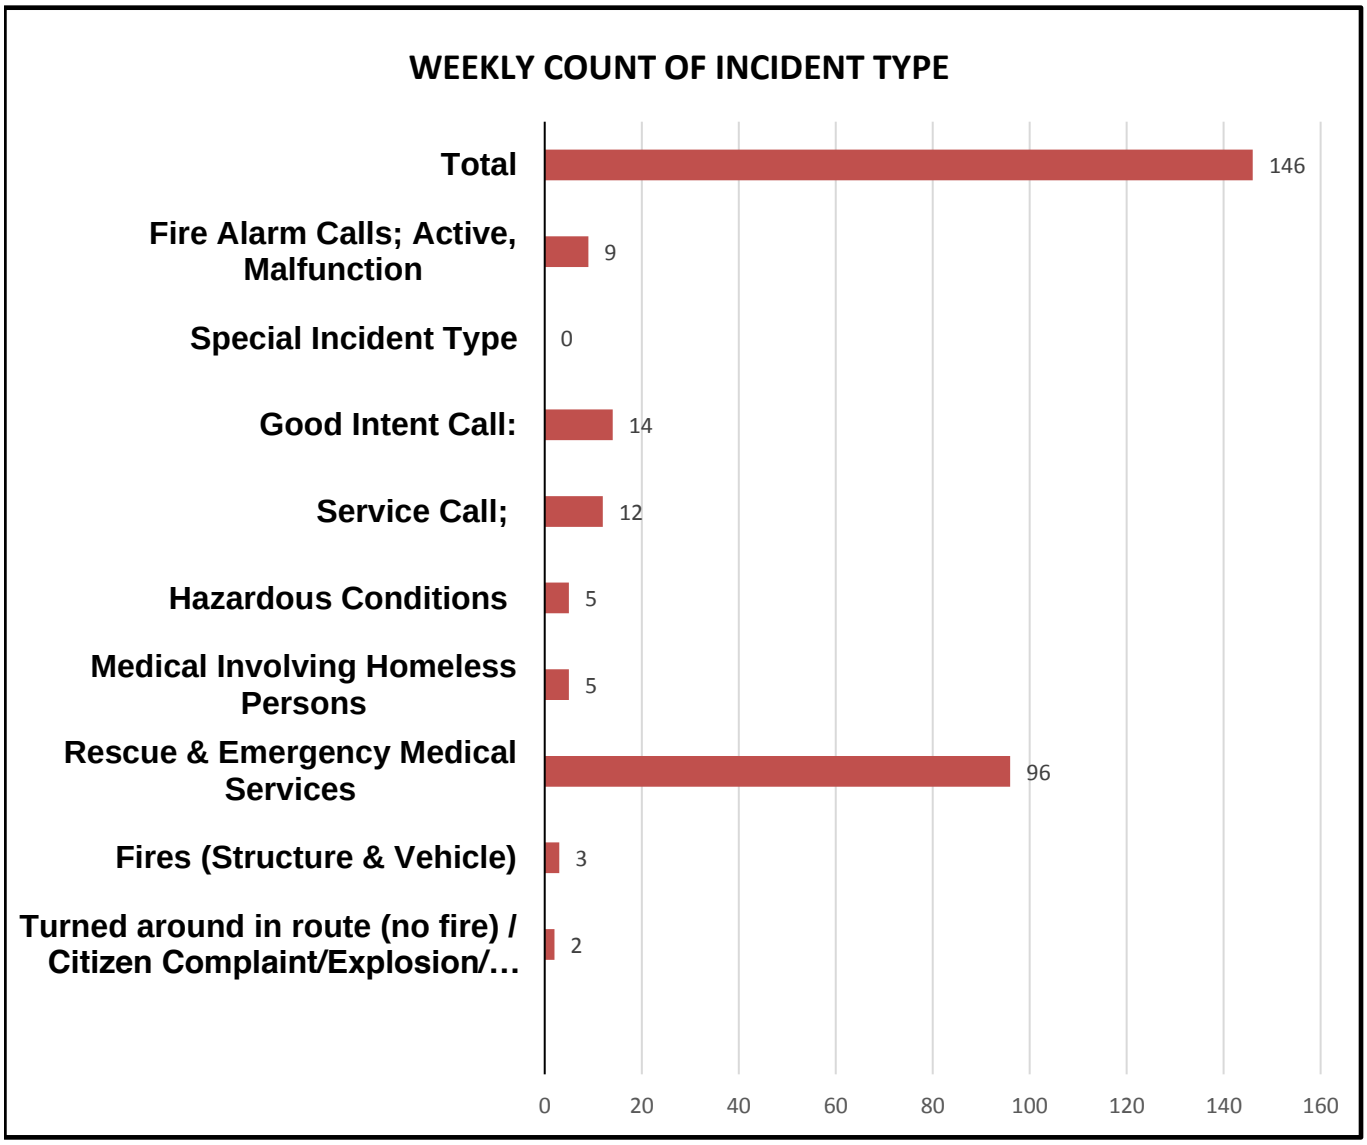

Criminal Intelligence Unit
T. (228) 702-3122
T. (228) 702-1276
T. (228) 702-3113
F. (228) 702-3179
ciu@biloxi.ms.us

Police Chief
John B. Miller

170 Porter Avenue
Biloxi, Mississippi 39530
Office: 228.435.6100
Fax: 228.374.1922
www.biloxi.ms.us

DATE: February 11, 2019

RE: Biloxi Police activity for February 4-10, 2019

TOTAL CALLS FOR SERVICE	***2,197***
TOTAL INCIDENT REPORTS *(Case Numbers)*	***315***
TOTAL OFFENSES *(Violations/Reports)*	***232***
TOTAL ARRESTS	***126***

Calls excluded from call type charts were: Checking Building – 94; Extra Patrol – 749; Suspicious Circumstances – 99; Traffic Stops – 265; and Walk & Talk – 175. Additional details may be viewed at http://www.crimemapping.com/map/ms/biloxi.

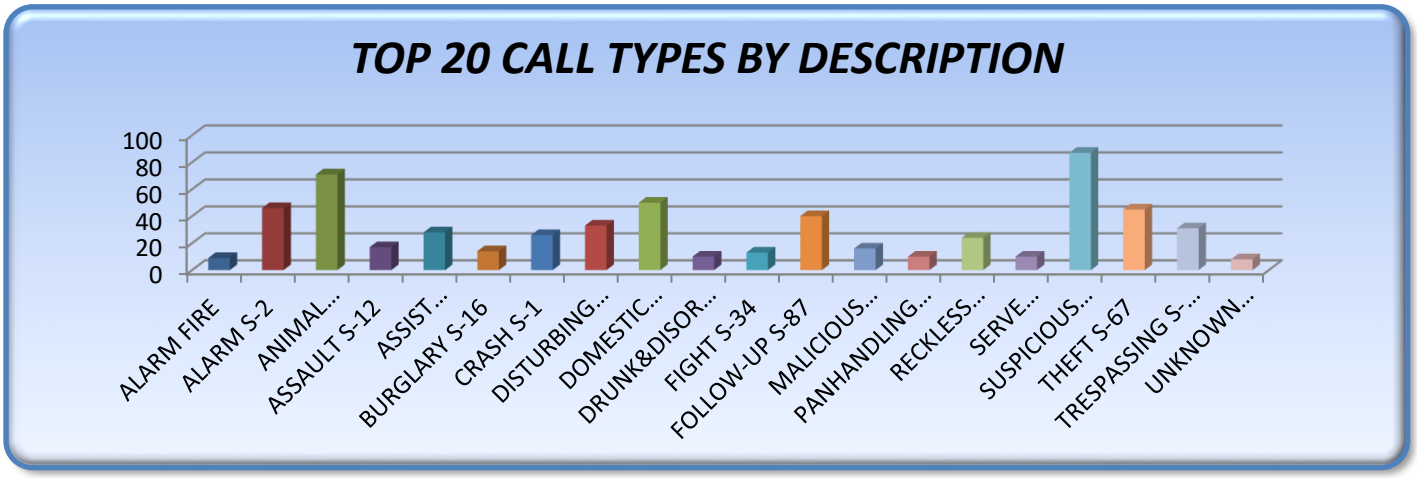

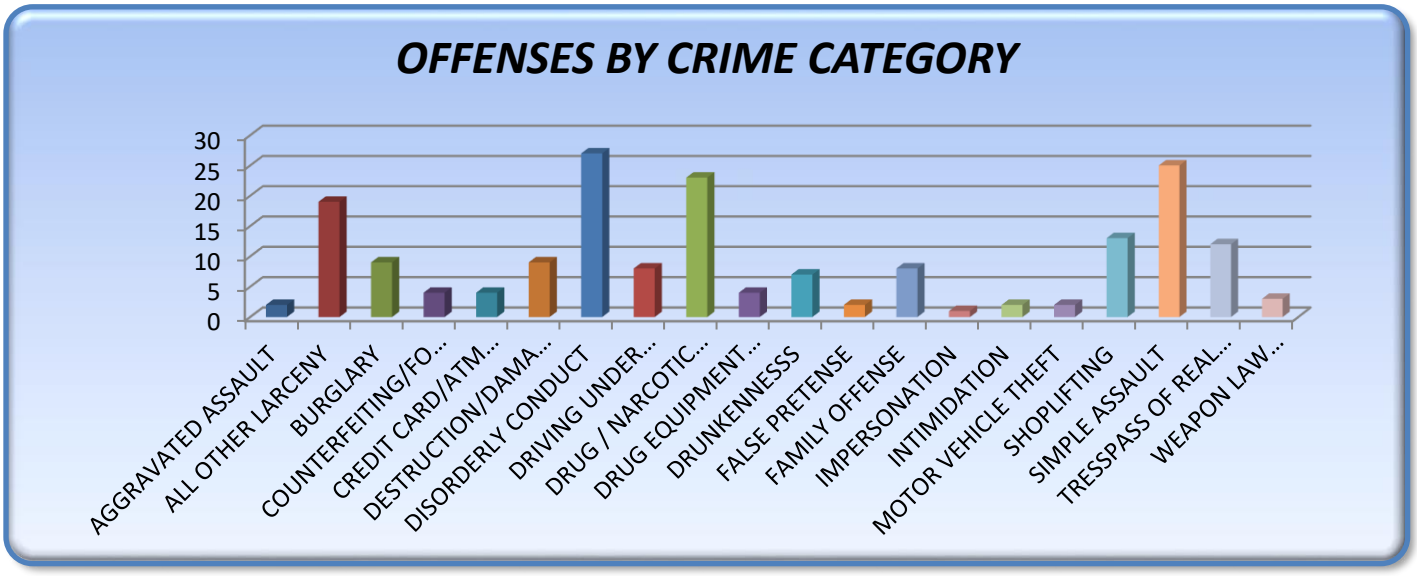

DATE: *February 11, 2019*
COMMUNITY DEVELOPMENT ACTIVITY REPORT FOR Feb 4 – 10, 2019

Building permits issued	*64*
Construction Valuation of permits issued	*$233,000*
Building inspections performed	*165*
Business licenses **Renewals** **Charter Boats** **Peddler's licenses**	*2* *2*
Certificates of occupancy issued	*11*
Code enforcement cases opened	
Code enforcement cases resolved	

Engineering Department
Christy LeBatard, P.E.
Director of Engineering

214-A Delauney Street
P. O. Box 429
Biloxi, Mississippi 39533
Office: 228.435.6265
Fax: 228.435.6179
www.biloxi.ms.us

Biloxi
established 1699

Engineering Department Weekly Update
February 11, 2019
(updates in bold)

Natatorium – Repairing the leak first then going to remediate the mold

MGM Park Stadium Lights – Temporary power to scoreboard materials have been ordered; the board has to be working before March 1st for the high school games. As for the lights, there is a concern that the issue with the board may be backfeeding and causing the lights issue.

MS Power Fiber Agreement – Passed this on to Rachel for council approval

Projects

- Bayview Avenue Boardwalk – permit application pending DMR approval; estimated cost $1.2 million; setting up meeting with Seymour to kick off design contract

- Bayview Ave. Bridge Replacement (State-Aid Project) – This project is nearing bidding, the waterline will need to be removed from the bridge; public works to look into this work

- Belle La Vie Parkway – 90% plans under development

- Canaan Fishing Dock Improvements – permit application submitted to DMR; public hearing was held last week at DMR, there were no comments; Commission approved permit; Corps Permit still pending; setting up meeting with Seymour to kick off design

- **Cedar Lake Bridge Repairs (Const. Funding 2021)** – project activation request on council agenda Nov. 6th, ERBRF grant application not awarded; MOU from MDOT on the 80/20 funding approved by council, waiting for executed copy to come back from MDOT to proceed

- **Circle Park Upgrades** – *working up preliminary site plan for approval*

- Campbell Drive Drainage – Need to define scope of work

- CSX Crossing Closure (MDOT Funded) – Neel-Schaffer study completed, finalizing surveys now

- **CSX Crossing Closure (CDBG Funded)** – 90% submittal submitted to CSX and comment received back, have conference call with CSX today regarding the drainage ditches; surveys and appraisals should be done by mid February to begin acquisition; *conference call Friday with CSX to review 90% submittal comments*

- **Dredging** – complete

- **Dukate Street Paving** – Received quote for $15,000, *paving pending completion of heavy construction at hotel*

- **East Biloxi Public Access & Living Shoreline** – Task D (South of Bridge to Point Cadet Marina) and Task E (North of Bridge to Palace); DCD Construction awarded Alt. A & B for a total of $1.8M; NTP Oct. 8, 2018; Completion Aug. 9, 2019; *bulkhead work complete, boardwalk cap being installed; change order to add shade structures and benches will be on council agenda in Feb.*

- East Biloxi Boardwalk (Small Craft to Kuhn St.) – Pending design contract

- **Eagle Point Park** – *design contract on Feb. 19th council agenda*

- Ellzey Place II – Currently under punchlist

- **Ellzey Place III (Medical Park Drive Extension)** – *Preparing to advertise for bids*

- Fire Station No. 7 – NTP August 15, 2018, Starks Construction; foundation work complete; structure going up

- Fire Station No. 10 – Completion Date: 6/28/2019; Contractor: JW Puckett $2.35 million; foundation work complete & waterline along old Hwy 67 underway; structure going up

- Glen Eagle Subdivision (formerly Jordan Subdivision) – clearing and grubbing

- **Henry Beck Park Restroom –** *Working through the CBDG process and developing an estimated cost*

- **Hiller Park Pond Cleaning** – *permit application submitted to DMR this week*

- Hiller Park Trail – design on-going

- **Howard Avenue** – Gulf Breeze Landscaping NTP 4/9/2018; Completion 10/6/2018; *bricks from Lameuse to Main being installed; striping at diagonal spaces have been replaced just need to be resanded; upgrading intersection of Howard and Main to match Howard and Lameuse*

- **Keesler Gate Outside** – Property acquisition continuing; need to discuss private utility relocations

- **Keesler Gate Inside** – Awarded to Necaise Brothers Const. $4.8 million on 4/24, NTP 5/21/2018; 540 Calendar Days; Completion Date 11/12/2019; work on-going

- Keesler Privatization – Pending final decision Oct – Dec 2018;

- **Main Street Railroad Crossing Upgrades (MDOT Funding 2020)** – *waiting for executed MOU back from MDOT in order to proceed*

- Watersview Drainage/Malpass Landing – Need to define scope of work for this first phase

- **MGM Stadium Capital Maintenance** – Developed a list of potential capital maintenance items; *dugout steps and hand rail painting being completed by PW; elevator flooring, scoreboard, seats, and field lights*

- Nature's Trail – sewer complete, waterline delayed due to rain

- Pedestrian Crosswalk @ Harbor –Dan Hensarling, Inc. $2.4M; NTP October 8, 2018; structure beginning to come out of the ground

- **Pedestrian Crosswalk @ MGM** – Malouf Construction; *need to work on irrigation issue*

- **Point Cadet Marina Electrical Upgrades** – Full electrical upgrade of entire harbor; Awarded to *DNP $228,360; construction pending return of contract documents*

- Point Cadet Marina Improvements (West) #1024 – Old Task "A" & "C"; currently on hold

- **Point Cadet Marina Pile Repairs** – *Will advertise for bids this week*

- Popps Ferry Extension #913 – Coliseum has the draft MOU for Board approval; 33 parcels to acquire; surveys and appraisals are underway; met with utility companies to begin coordination

- Popps Ferry Bridge Submarine Cable – Contract documents were returned 6/1/2018, new generator and switch in place and operational

- Popps Ferry Bridge & Approaches – pending EA approval; met with BMA draft EA is at MDOT for preliminary approval once receive comments back final EA will go to MDOT/FHWA for approval; once approval is granted the City can petition MDOT to start ROW Acquisition

- Popps Ferry Causeway – Received CO on building, worked out final change order with DCD last week, should be receiving close out documents from DCD this week so we'll be ready to close out the construction project; still need to award the landscape maintenance contract; have met with Gulf Breeze about the additions that will be needed and they are working up costs

- Post Office Build-out – Preparing project for advertising at the end of February

- **Port Commission Roof Repairs** – *Design contract will be on the Feb. 19th council agenda*

- Public Excursion Pier South of Pine/Cedar #1030 – Old Task "B"

- Public Safety Center Roof Leaks – Will advertise for bids this week.

- **Saenger Theater Phase I & II Fly Tower & Exterior** – *need concrete removed in the alley so MS Power can reroute the power; lead and asbestos testing complete, report pending; planning to advertise for construction in Summer 2019*

- Saenger Theater Phase III Interior – start design in summer 2019, bid for construction by beginning of 2020

- Shorecrest Subdivision – clearing and grubbing

- Smith Subdivision (north corner of Woolmarket Rd. & Old Hwy 67) – water line tie into Larkin should be this week

- Snyder Fence Repairs – Parks and Rec to get quotes

- Snyder Pool Repairs – Need to meet with pool company to develop scope of work

- Snyder Roof Bid – Work underway

- Sports Complex Tennis Courts Lighting – Have a rough estimate of anywhere from $50K to $100K to add lighting; meeting with lighting consultant that may be able to help us spec it out

- **Tanglewood Infrastructure** – *Met with Machado Patano; should have a design contract in the next two weeks*

- Veterans Avenue Signal Upgrade – to be completed by the VA; work underway

- West Biloxi Boardwalk Phase 1B – Issued Buzzy Bolton authorization to proceed with design; BMA preparing tidelands lease application and easement surveys

- Woolmarket City Center Addition – Will coordinate with A&E as necessary

- **Woolmarket Rd. East Drainage** – A&E *contract on the 2nd council meeting in February.*

- Woolmarket Rd. East (Larkin) water line – DNA Underground; NTP 4/23/18; completion date 2/17/2019; paving still pending due to manhole rings and weather; custody transfer station installation is last item of work

- **Woolmarket Road Sidewalk from Lorraine to Old Hwy 67** – Project Activation Request was on council agenda Nov. 6th; *MOU was approved by council, waiting for executed copy from MDOT to proceed*
